



TECHNICAL MEMORANDUM

To: Julie Kinzie, Sr. Environmental Program Manager Sound Insulation
From: Eric Cox, Principal Technical Analyst
Date: May 4, 2026
Subject: Acoustical Testing Results for SEA Repair and Replacement Program
Reference: HMMH Project Number 03-12150.001.004

Harris Miller Miller & Hanson Inc. (HMMH) completed sound insulation measurements for the Seattle-Tacoma International Airport (SEA) Repair and Replacement Program (the Program), during March 2026 to determine the median interior Day-Night Average Sound Level (DNL) value for 30 residential structures, in accordance with Federal Aviation Administration (FAA) guidance as specified in Chapter 8 of Advisory Circular (AC) 150/5000-9B.¹

Appendix R of FAA Order 5100.38D² (AIP Handbook) stipulates that the median interior DNL sound level must be 45 decibels (dB) or greater with windows closed for a structure to qualify for sound insulation treatments. The interior DNL sound levels are determined by subtracting the measured outdoor-indoor Noise Level Reduction (NLR) for each tested habitable room from the exterior DNL sound level for each residential property.

Sections 1 through 3 of this technical memorandum summarize the test procedures and analysis methods. Results are provided in Section 4 and detailed acoustical measurement data are provided in the attachment.

1. Exterior Sound Level

The process used to determine the exterior DNL for a residential property is outlined in Chapter 8 of FAA AC 150/5000-9B. A value of 70 dB is assigned to structures located within the 65 to 70 dB contour interval, as determined by the most recent FAA-approved Noise Exposure Map (NEM). Currently, the 2018 Forecast Condition NEM³ is the most recently approved set of contours.

2. Noise Level Reduction

To determine the median interior DNL value for a residential structure, the NLR of all habitable rooms within the structure must be measured. HMMH conducted the acoustical testing using a Hottinger Brüel & Kjær (HBK) Model 2245 sound level meter with current calibration traceable to the U.S. National Institute of Standards and Technology (NIST) and conforming to American National Standards Institute (ANSI) Standard S1.4⁴ and International Electrotechnical Commission (IEC) 61672⁵ for Type 1 (precision) spectrum analyzers. Additional calibrations were carried out during each day of testing using a NIST-certified HBK Model 4231 calibrator.

¹ FAA Advisory Circular 150/5000-9B “Guidelines for Sound Insulation of Structures Exposed to Aircraft Noise”, Chapter 8 “Acoustical Engineering and Testing”, June 8, 2022, https://www.faa.gov/documentLibrary/media/Advisory_Circular/150-5000-9B-Sound-Insulation-2022.pdf

² FAA Order 5100.38D, Change 1 “Airport Improvement Program Handbook”, Appendix R “Noise Compatibility Planning/Projects”, February 26, 2019, https://www.faa.gov/airports/aip/aip_handbook/media/AIP-Handbook-Order-5100-38D-Chg1.pdf

³ Seattle-Tacoma International Airport 14 CFR Part 150 “Noise Compatibility Study Update”, October 2013

⁴ American National Standards Institute, ANSI/ASA S1.4-2014 – Part 1 “American National Standard Electroacoustics – Sound Level Meters – Part 1: Specifications”

⁵ International Electrotechnical Commission, IEC 61672-1:2013 “Electroacoustics – Sound Level Meters – Part 1: Specifications”

The noise source used for the measurements consisted of a Mackie SRM450 loudspeaker. The acoustical testing procedure conformed to industry best practices and followed the methodology outlined in Section 8.5 of FAA AC 150/5000-9B.

HMMH exposed each tested room to the exterior noise source (loudspeaker) and measured the resultant exterior and interior sound levels. The loudspeaker generated a test signal containing equal energy levels in each octave band (known as “pink noise”) and was positioned outside each tested room so that uniform distribution of the amplified sound was achieved over the exterior room façade under evaluation. The outdoor and indoor octave band noise levels were then measured with a sound level meter/spectrum analyzer. Ambient sound levels were also collected to ensure a sufficient signal-to-noise ratio for valid testing results.

The Outdoor-Indoor Noise Reduction (OINR) was calculated for each tested room by subtracting the interior sound levels measured in each octave band from the corresponding exterior sound level measurements. The indoor sound level data collected with the exterior noise source operating were also adjusted to account for the ambient acoustical energy measured in each room with the noise source turned off. The outdoor sound level data were adjusted to account for the exterior ambient sound levels measured with the noise source turned off and to correct for the acoustic energy reflected from the exterior room façades with the noise source operating.

The NLR was then calculated for each tested room by applying the OINR data to the aircraft noise spectrum generated by a Boeing 737-800 aircraft, which was determined to be the representative aircraft type per the analysis procedure outlined in Section 8.5.10.1 of FAA AC 150/5000-9B.

3. Interior Sound Levels

The measured NLR values were subtracted from the exterior DNL sound level for each property to compute the interior DNL sound level for each tested room within a structure. A median interior DNL value was then calculated for the entire structure from the interior sound levels determined for each individual habitable room.

4. Acoustical Test Results

Table 1 summarizes the acoustical testing results for 30 residential structures. Overall, the measurements indicate that no structures have a median interior DNL sound level above 45 dB. However, nine of the structures have one or more individual habitable rooms with interior DNL sound levels above 45 dB that could potentially benefit from repair or replacement of acoustical windows and doors. Note that this is not the current FAA policy.

Table 1. Acoustical Testing Results for SEA Repair and Replacement Program

Resident	Address	Room	Measured Noise Level Reduction NLR (dB)	Day-Night Average Sound Level DNL (dB)		
				Exterior ¹	Interior ²	Median Interior
Woloszyn	20736 9th Ave S Des Moines	Living Room	32.8	70.0	37.2	37.5
		Dining / Kitchen	32.5	70.0	37.5	
		Bedroom 1	27.4	70.0	42.6	
		Bedroom 2	29.8	70.0	40.2	
		Bedroom 3	28.7	70.0	41.3	
		Bedroom 4	32.7	70.0	37.3	
		Office	33.1	70.0	36.9	
Fevriere	20735 10th Ave S Des Moines	Living / Kitchen	28.1	70.0	41.9	36.8
		Bedroom 1	33.2	70.0	36.8	
		Bedroom 2	34.5	70.0	35.5	
Gobena	21457 13th Ave S Des Moines	Living Room	30.6	70.0	39.4	36.6
		Sitting Room	34.6	70.0	35.4	
		Dining / Kitchen 1	26.9	70.0	43.1	
		Kitchen 2	34.3	70.0	35.7	
		Bedroom 1	30.1	70.0	39.9	
		Bedroom 2	33.9	70.0	36.1	
		Bedroom 3	33.4	70.0	36.6	
		Bedroom 4	33.4	70.0	36.6	
		Bedroom 5	23.2	70.0	46.8	
Sharma	11418 14th Ave S Burien	Living Room	25.9	70.0	44.1	42.4
		Dining Room	28.3	70.0	41.7	
		Kitchen	20.0	70.0	50.0	
		Bedroom 1	29.9	70.0	40.1	
		Bedroom 2	30.7	70.0	39.3	
		Bedroom 3	27.0	70.0	43.0	
Carbary	11510 14th Ave S Burien	Living Room	31.7	70.0	38.3	38.3
		Sitting Room	27.6	70.0	42.4	
		Kitchen	23.6	70.0	46.4	
		Bedroom	40.7	70.0	29.3	
McDonald	21823 14th Ave S Des Moines	Living / Dining	25.7	70.0	44.3	41.1
		Family Room	14.2	70.0	55.8	
		Kitchen	35.6	70.0	34.4	
		Bedroom 1	33.3	70.0	36.7	
		Bedroom 2	21.7	70.0	48.3	
Zuluaga	10106 16th Ave S Seattle	Office	32.1	70.0	37.9	39.6
		Living Room	30.4	70.0	39.6	
		Dining / Kitchen	26.6	70.0	43.4	
		Kitchenette	23.7	70.0	46.3	
		Bedroom 1	31.3	70.0	38.7	
		Bedroom 2	31.8	70.0	38.2	
Gauthier	22459 16th Ave S Des Moines	Bedroom 3	27.1	70.0	42.9	35.9
		Office	32.0	70.0	38.0	
		Living Room	28.0	70.0	42.0	
		Sitting Room	33.5	70.0	36.5	
		Dining / Kitchen	32.9	70.0	37.1	
		Bedroom 1	36.8	70.0	33.2	
		Bedroom 2	33.3	70.0	36.7	
		Bedroom 3	34.7	70.0	35.3	
		Bedroom 4	38.2	70.0	31.8	
		Bedroom 5	44.6	70.0	25.4	

Table 1. Acoustical Testing Results for SEA Repair and Replacement Program

Resident	Address	Room	Measured Noise Level Reduction NLR (dB)	Day-Night Average Sound Level DNL (dB)		
				Exterior ¹	Interior ²	Median Interior
Stanley	22620 16th Ave S Des Moines	Living Room	32.0	70.0	38.0	38.8
		Sitting Room	30.8	70.0	39.2	
		Dining / Kitchen	27.4	70.0	42.6	
		Bedroom 1	38.5	70.0	31.5	
		Bedroom 2	30.7	70.0	39.3	
		Office	31.5	70.0	38.5	
Betelhem	23249 17th Pl S Des Moines	Living / Dining	28.7	70.0	41.3	37.6
		Sitting Room	32.2	70.0	37.8	
		Kitchen	32.1	70.0	37.9	
		Bedroom 1	32.2	70.0	37.8	
		Bedroom 2	37.8	70.0	32.2	
		Bedroom 3	41.2	70.0	28.8	
		Bedroom 4	32.7	70.0	37.3	
		Bedroom 5	34.6	70.0	35.4	
Engstrum	10457 19th Ave S Seattle	Living Room	33.7	70.0	36.3	32.1
		Family Room	42.7	70.0	27.3	
		Sitting Room	33.5	70.0	36.5	
		Dining / Kitchen	26.2	70.0	43.8	
		Bedroom 1	37.9	70.0	32.1	
		Bedroom 2	40.3	70.0	29.7	
Tiemens	10422 20th Ave S Seattle	Bedroom 3	39.3	70.0	30.7	44.2
		Living / Dining	25.6	70.0	44.4	
		Kitchen	21.2	70.0	48.8	
		Bedroom 1	30.6	70.0	39.4	
		Bedroom 2	33.7	70.0	36.3	
		Bedroom 3	26.1	70.0	43.9	
Nguyen	11248 20th Ave S Burien	Office	25.6	70.0	44.4	34.8
		Living / Dining	32.1	70.0	37.9	
		Kitchen	32.6	70.0	37.4	
		Bedroom 1	37.9	70.0	32.1	
		Bedroom 2	38.8	70.0	31.2	
Pond	11254 20th Ave S Burien	Bedroom 2	38.8	70.0	31.2	39.7
		Living Room	29.2	70.0	40.8	
		Sitting Room	24.4	70.0	45.6	
		Dining Room	22.4	70.0	47.6	
		Kitchen	33.4	70.0	36.6	
		Bedroom 1	30.3	70.0	39.7	
		Bedroom 2	34.7	70.0	35.3	
Gilderoy	23019 20th Ave S Des Moines	Office	32.8	70.0	37.2	38.7
		Living Room	30.5	70.0	39.5	
		Sitting Room	28.1	70.0	41.9	
		Dining Room	31.3	70.0	38.7	
		Kitchen	31.5	70.0	38.5	
		Bedroom 1	39.7	70.0	30.3	
		Bedroom 2	27.4	70.0	42.6	
Layer	23147 20th Ave S Des Moines	Bedroom 3	36.3	70.0	33.7	36.5
		Living Room	28.9	70.0	41.1	
		Family Room	33.5	70.0	36.5	
		Sitting Room	32.5	70.0	37.5	
		Dining Room	35.6	70.0	34.4	
		Kitchen 1	32.6	70.0	37.4	
		Kitchen 2	32.5	70.0	37.5	
		Bedroom 1	35.6	70.0	34.4	
		Bedroom 2	37.3	70.0	32.7	
		Office	35.3	70.0	34.7	

Table 1. Acoustical Testing Results for SEA Repair and Replacement Program

Resident	Address	Room	Measured Noise Level Reduction NLR (dB)	Day-Night Average Sound Level DNL (dB)		
				Exterior ¹	Interior ²	Median Interior
Dustin	12854 23rd Ave S SeaTac	Living / Kitchen	26.5	70.0	43.5	38.8
		Bedroom 1	32.7	70.0	37.3	
		Bedroom 2	31.2	70.0	38.8	
Tucker	20822 25th Ave S Des Moines	Dining / Kitchen	27.6	70.0	42.4	39.8
		Bedroom 1	30.0	70.0	40.0	
		Bedroom 2	30.2	70.0	39.8	
		Bedroom 3	32.4	70.0	37.6	
		Bedroom 4	30.2	70.0	39.8	
Wynn	2007 S 112th St Burien	Living Room	32.7	70.0	37.3	38.1
		Sitting Room	28.8	70.0	41.2	
		Dining Room	27.4	70.0	42.6	
		Dinette	35.4	70.0	34.6	
		Kitchen	31.1	70.0	38.9	
		Bedroom 1	41.5	70.0	28.5	
		Bedroom 2	35.3	70.0	34.7	
Carstensen	1244 S 120th St Burien	Study	27.7	70.0	42.3	36.2
		Living Room	31.5	70.0	38.5	
		Dining / Kitchen	32.6	70.0	37.4	
		Bedroom 1	29.6	70.0	40.4	
		Bedroom 2	35.3	70.0	34.7	
		Office	34.9	70.0	35.1	
Chey & Han	2516 S 146th St SeaTac	Den	36.4	70.0	33.6	35.0
		Living Room	33.4	70.0	36.6	
		Sitting Room	28.3	70.0	41.7	
		Dining / Kitchen	29.2	70.0	40.8	
		Bedroom 1	36.7	70.0	33.3	
		Bedroom 2	38.3	70.0	31.7	
Meza	2637 S 150th St SeaTac	Bedroom 3	39.1	70.0	30.9	33.1
		Living Room	30.5	70.0	39.5	
		Dining / Kitchen	33.8	70.0	36.2	
		Bedroom 1	39.5	70.0	30.5	
		Bedroom 2	36.9	70.0	33.1	
Lindeke	850 S 177th Pl Burien	Bedroom 3	39.4	70.0	30.6	36.1
		Living Room	33.9	70.0	36.1	
		Dining / Kitchen	32.7	70.0	37.3	
		Bedroom 1	35.2	70.0	34.8	
		Bedroom 2	36.2	70.0	33.8	
		Bedroom 3	33.0	70.0	37.0	
		Bedroom 4	36.8	70.0	33.2	
Zacher	1020 S 202nd St Des Moines	Office	26.9	70.0	43.1	35.5
		Living Room	32.5	70.0	37.5	
		Sitting Room	28.4	70.0	41.6	
		Bedroom 1	34.5	70.0	35.5	
		Bedroom 2	35.7	70.0	34.3	
Reeder	925 S 206th St Des Moines	Office	37.5	70.0	32.5	36.4
		Living Room	33.3	70.0	36.7	
		Sitting Room	34.8	70.0	35.2	
		Bedroom 1	33.3	70.0	36.7	
		Bedroom 2	28.4	70.0	41.6	
		Bedroom 3	33.8	70.0	36.2	
		Bedroom 4	39.9	70.0	30.1	

Table 1. Acoustical Testing Results for SEA Repair and Replacement Program

Resident	Address	Room	Measured Noise Level Reduction NLR (dB)	Day-Night Average Sound Level DNL (dB)		
				Exterior ¹	Interior ²	Median Interior
McCaughan	2209 S 222nd St Des Moines	Living Room	34.5	70.0	35.5	36.8
		Dining Room	28.1	70.0	41.9	
		Kitchen	33.4	70.0	36.6	
		Bedroom 1	33.2	70.0	36.8	
		Bedroom 2	38.5	70.0	31.5	
		Bedroom 3	23.5	70.0	46.5	
		Office	31.8	70.0	38.2	
Rivera & Boyle	2035 S 229th St Des Moines	Living Room	33.5	70.0	36.5	36.4
		Sitting / Dining / Kitchen	31.3	70.0	38.7	
		Bedroom 1	35.7	70.0	34.3	
		Bedroom 2	35.7	70.0	34.3	
		Bedroom 3	33.6	70.0	36.4	
		Office	33.6	70.0	36.4	
Alfaro	2050 S 229th St Des Moines	Living Room	30.8	70.0	39.2	39.2
		Dining / Kitchen / Office	28.4	70.0	41.6	
		Bedroom 1	35.7	70.0	34.3	
		Bedroom 2	26.5	70.0	43.5	
		Bedroom 3	37.4	70.0	32.6	
Canas	2106 S 229th St Des Moines	Living Room	29.7	70.0	40.3	39.7
		Sitting Room	28.9	70.0	41.1	
		Dining / Kitchen	29.4	70.0	40.6	
		Bedroom 1	35.3	70.0	34.7	
		Bedroom 2	35.3	70.0	34.7	
		Office	30.9	70.0	39.1	
Gavlinski	1803 S 233rd St Des Moines	Living Room	31.3	70.0	38.7	39.1
		Sitting Room	34.3	70.0	35.7	
		Dining Room	23.7	70.0	46.3	
		Kitchen	25.1	70.0	44.9	
		Bedroom 1	28.0	70.0	42.0	
		Bedroom 2	33.4	70.0	36.6	
		Bedroom 3	30.5	70.0	39.5	
		Bedroom 4	32.1	70.0	37.9	

Notes:

Rooms with Interior DNL of 45 dB and greater are indicated in **red**.

1) Exterior DNL assigned per FAA guidelines using 2018 Forecast NEM for SEA Program.

2) Interior DNL for each habitable room equals Exterior DNL minus measured room NLR.

Attachment – Acoustical Measurement Data

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	52.8	46.8	43.4	44.9	37.9	48.3
Exterior Measurement (flush)	100.5	99.8	100.8	97.2	93.9	102.7
Exterior Adjusted	94.5	93.8	94.8	91.2	87.9	96.7
Interior Background	44.0	40.2	29.3	25.3	20.1	34.8
Interior Measurement	71.7	69.9	62.7	51.7	43.5	64.3
Interior Adjusted	71.7	69.9	62.7	51.7	43.5	64.3
Noise Reduction	22.8	23.9	32.1	39.5	44.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.5	33.2	33.0	27.1	17.4	37.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.8 dB

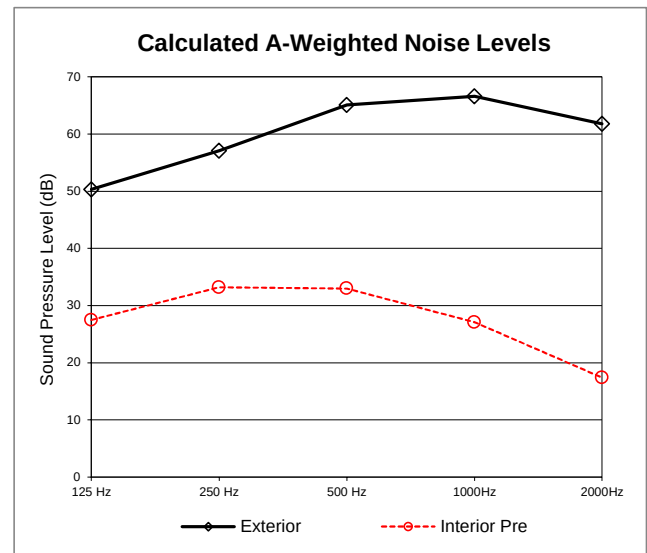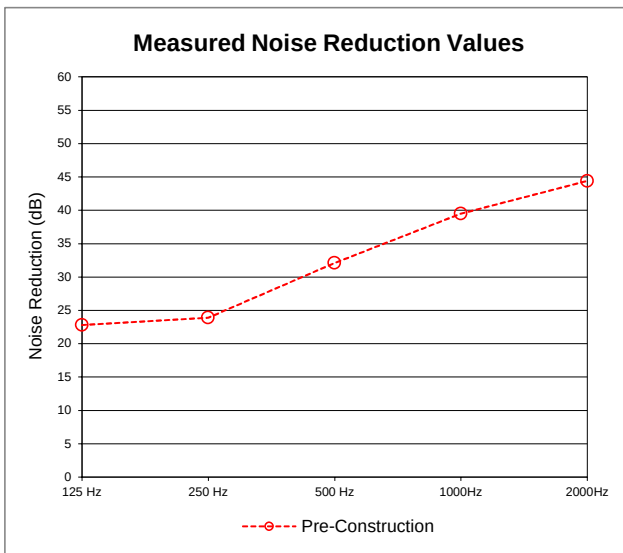

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.4	46.4	44.4	45.5	39.6	49.8
Exterior Measurement (flush)	88.9	88.7	89.0	86.3	84.8	92.8
Exterior Adjusted	82.9	82.7	83.0	80.3	78.8	86.8
Interior Background	46.1	41.9	34.2	26.8	19.6	37.2
Interior Measurement	63.7	57.1	51.6	41.5	39.0	54.3
Interior Adjusted	63.6	57.0	51.5	41.4	38.9	54.2
Noise Reduction	19.3	25.7	31.5	38.9	39.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.0	31.4	33.6	27.7	21.9	37.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.5 dB

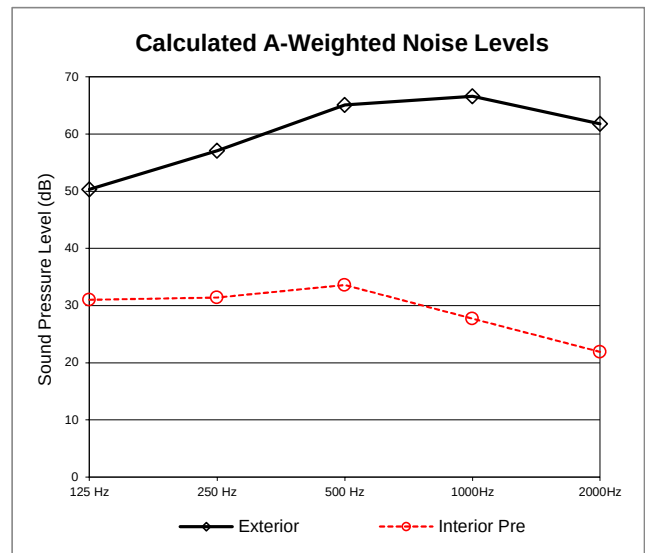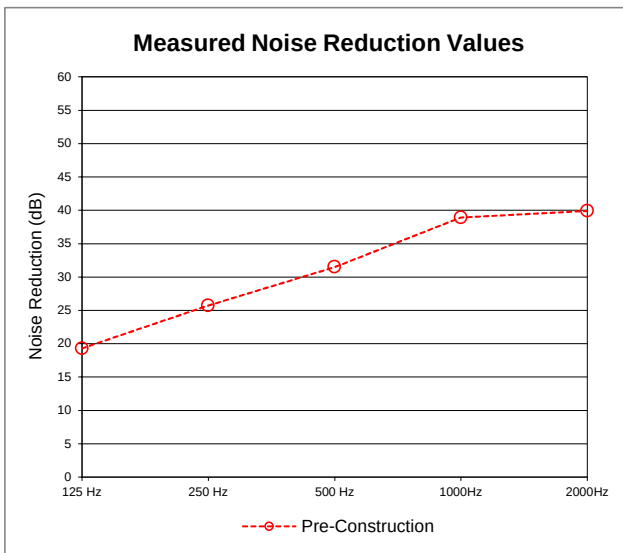



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	85.6	90.5	88.7	86.2	85.1	92.9
Exterior Adjusted	79.6	84.5	82.7	80.2	79.1	86.9
Interior Background	46.2	40.2	35.5	29.9	22.3	37.4
Interior Measurement	65.6	58.9	54.7	48.0	50.9	58.6
Interior Adjusted	65.5	58.8	54.6	47.9	50.9	58.6
Noise Reduction	14.1	25.7	28.1	32.3	28.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	36.2	31.4	37.0	34.3	33.6	41.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.1 dB

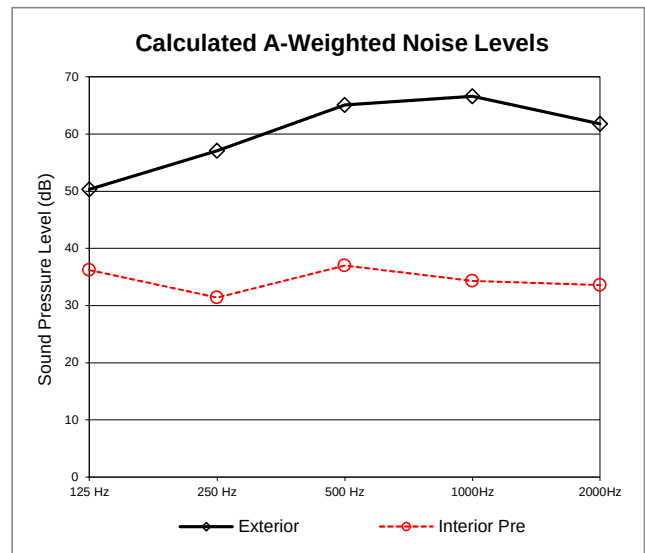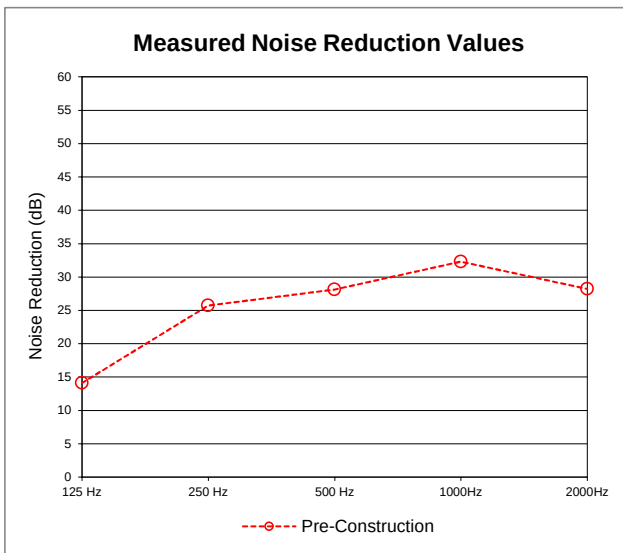



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	99.5	97.5	97.6	93.1	88.2	99.4
Exterior Adjusted	93.5	91.5	91.6	87.1	82.2	93.4
Interior Background	46.2	40.2	35.5	29.9	22.3	37.4
Interior Measurement	75.3	60.8	54.0	43.7	37.7	60.1
Interior Adjusted	75.3	60.8	53.9	43.5	37.6	60.1
Noise Reduction	18.2	30.7	37.7	43.6	44.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.1	26.4	27.4	23.0	17.2	34.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.4 dB

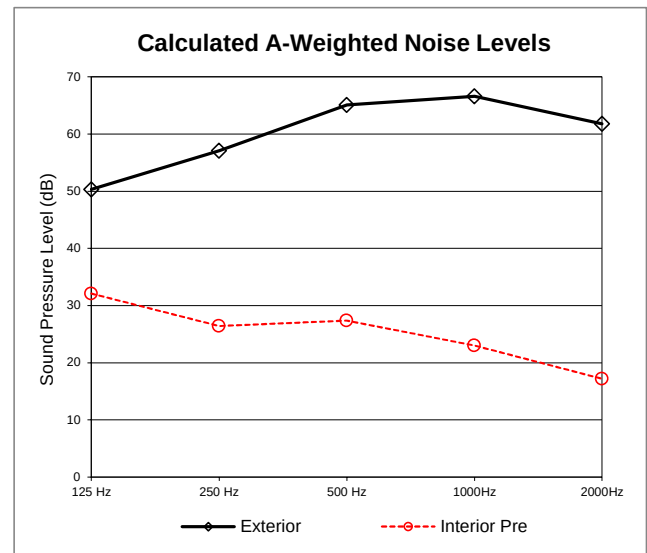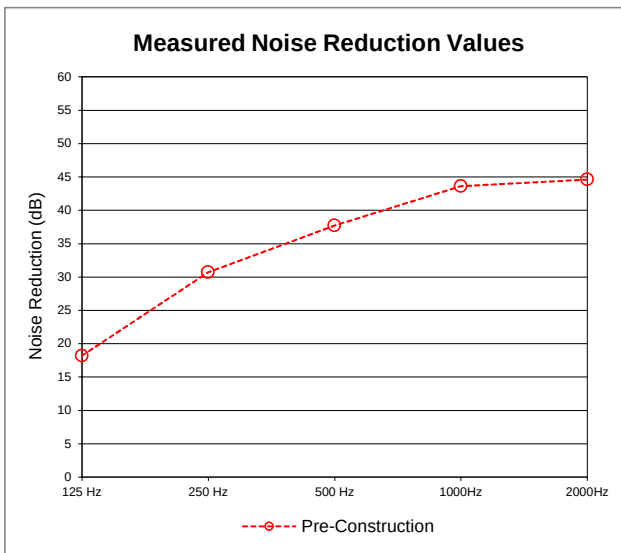



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	99.4	97.2	97.1	92.0	88.2	99.0
Exterior Adjusted	93.4	91.2	91.1	86.0	82.2	93.0
Interior Background	36.0	35.4	35.2	32.7	24.1	36.3
Interior Measurement	74.8	62.4	54.3	45.9	42.3	60.4
Interior Adjusted	74.8	62.4	54.2	45.7	42.2	60.4
Noise Reduction	18.6	28.8	36.9	40.3	40.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.7	28.3	28.2	26.3	21.8	35.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.7 dB

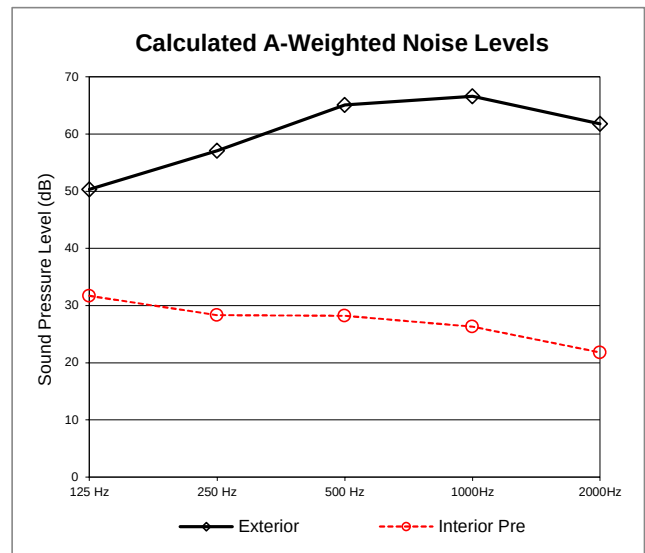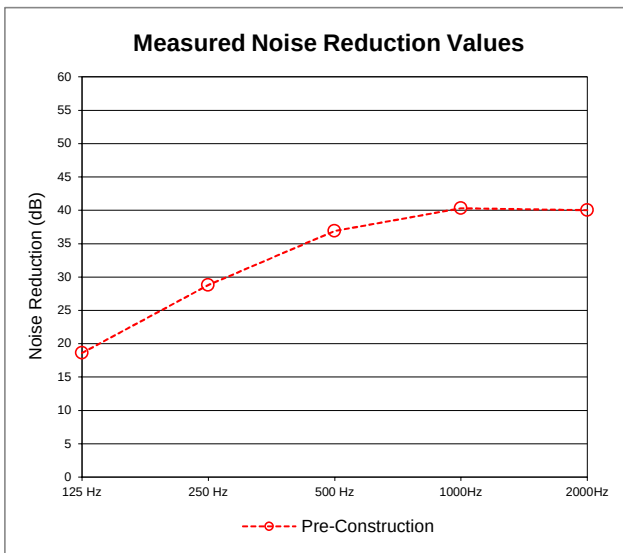



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	88.5	89.2	89.4	88.0	85.8	93.8
Exterior Adjusted	82.5	83.2	83.4	82.0	79.8	87.8
Interior Background	36.0	35.4	35.2	32.7	24.1	36.3
Interior Measurement	64.7	58.4	53.6	40.0	31.7	54.3
Interior Adjusted	64.7	58.4	53.5	39.1	30.9	54.2
Noise Reduction	17.8	24.8	29.9	42.9	48.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.5	32.3	35.2	23.7	12.9	38.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.5 dB

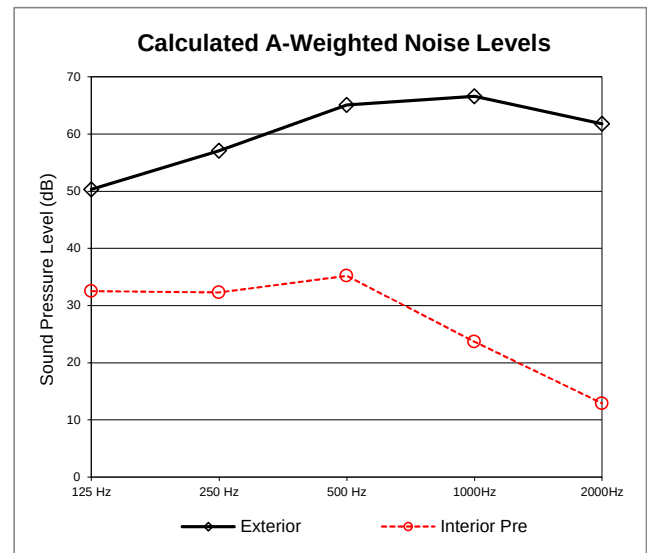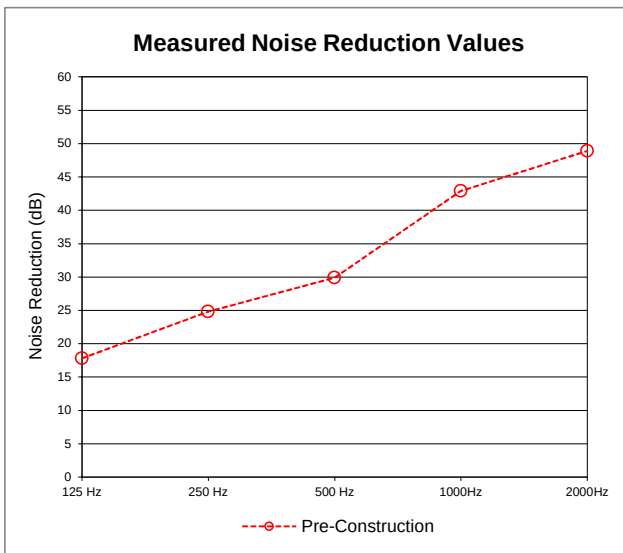



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	87.6	91.0	90.2	88.6	84.7	93.7
Exterior Adjusted	81.6	85.0	84.2	82.6	78.7	87.7
Interior Background	31.6	25.4	20.9	19.3	17.4	26.1
Interior Measurement	65.0	62.2	58.0	44.5	34.9	57.9
Interior Adjusted	65.0	62.2	58.0	44.5	34.8	57.9
Noise Reduction	16.6	22.8	26.2	38.1	43.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.7	34.3	38.9	28.5	17.9	41.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.7 dB

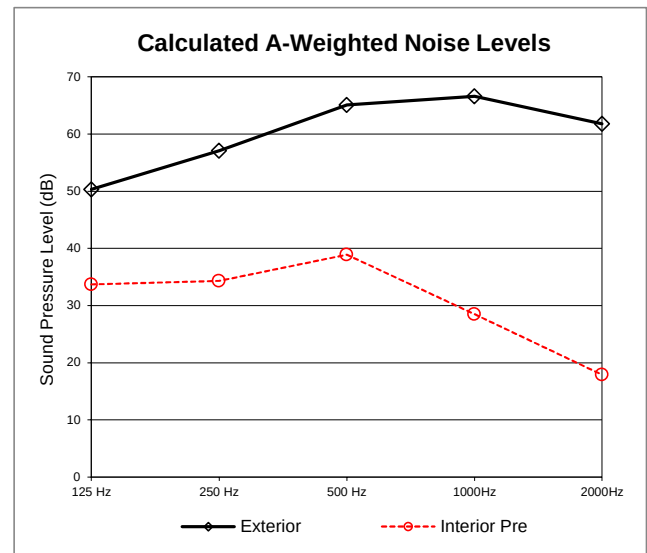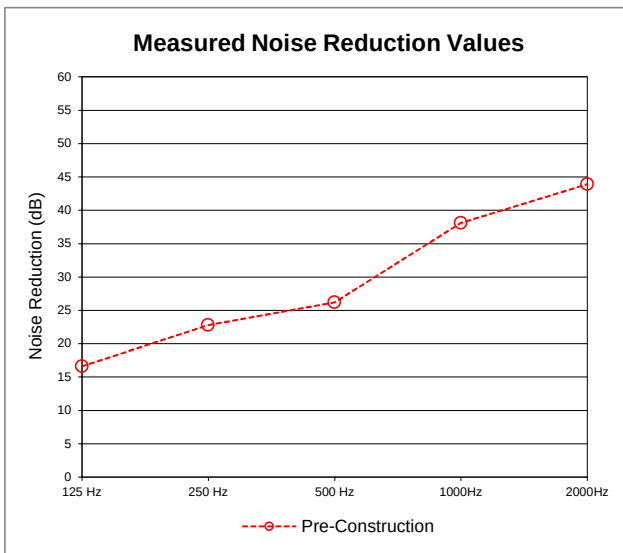



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	94.1	97.7	96.7	94.0	90.6	99.8
Exterior Adjusted	88.1	91.7	90.7	88.0	84.6	93.8
Interior Background	36.2	25.1	18.0	13.5	13.1	28.9
Interior Measurement	70.6	62.5	59.4	47.3	35.2	59.6
Interior Adjusted	70.6	62.5	59.4	47.3	35.2	59.6
Noise Reduction	17.5	29.2	31.3	40.7	49.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.8	27.9	33.8	25.9	12.4	37.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.7 dB

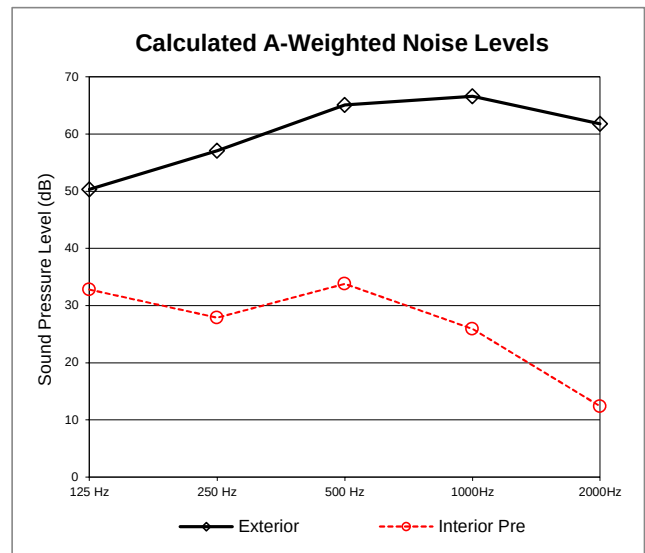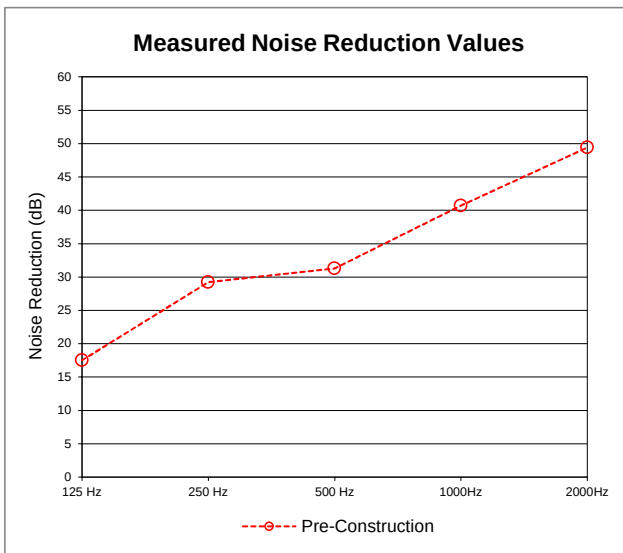



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Woloszyn
 Address: 20736 9th Ave S
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	52.2	48.0	47.3	38.7	51.2
Exterior Measurement (flush)	97.9	96.0	94.5	92.4	89.1	98.1
Exterior Adjusted	91.9	90.0	88.5	86.4	83.1	92.1
Interior Background	42.4	40.1	28.7	18.8	17.3	33.2
Interior Measurement	69.0	61.6	58.4	45.2	38.9	58.5
Interior Adjusted	69.0	61.6	58.4	45.2	38.9	58.5
Noise Reduction	22.9	28.4	30.1	41.2	44.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.4	28.7	35.0	25.4	17.6	36.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.1 dB

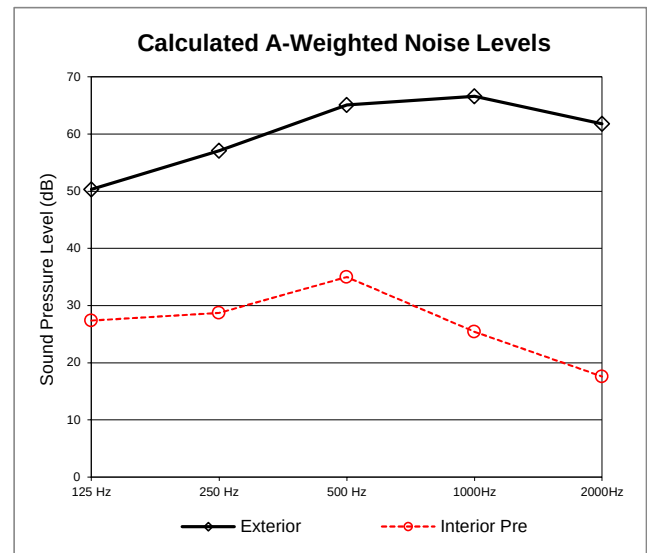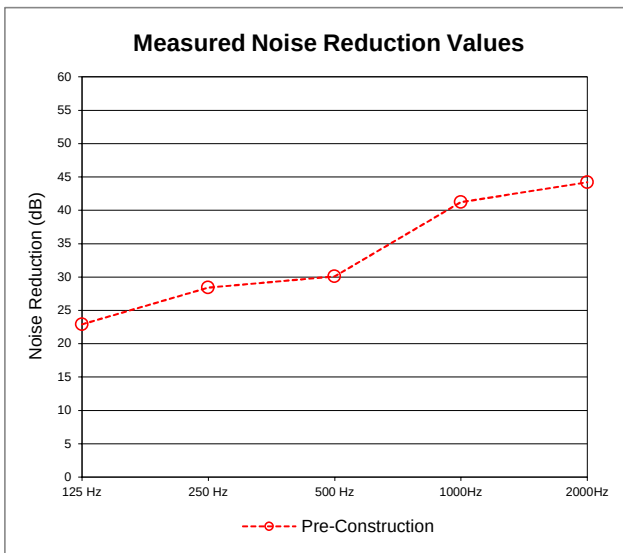

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Fevriere
 Address: 20735 10th Ave S
 Local City: Des Moines

Tested Room: Living / Kitchen Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.6	62.5	56.8	54.5	45.8	59.1
Exterior Measurement (flush)	100.1	98.8	99.2	94.7	92.3	100.9
Exterior Adjusted	94.1	92.8	93.2	88.7	86.3	94.9
Interior Background	45.1	37.2	28.1	25.5	21.8	33.9
Interior Measurement	73.4	64.6	60.3	52.0	48.0	62.0
Interior Adjusted	73.4	64.6	60.3	52.0	48.0	62.0
Noise Reduction	20.7	28.2	32.9	36.7	38.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.6	28.9	32.2	29.9	23.5	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

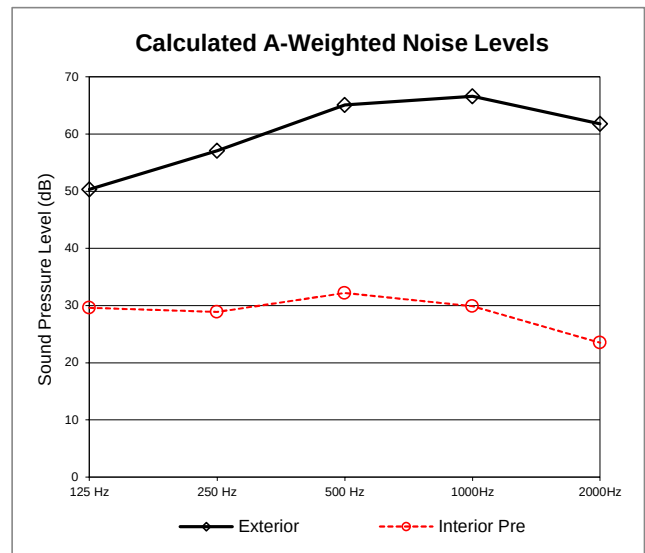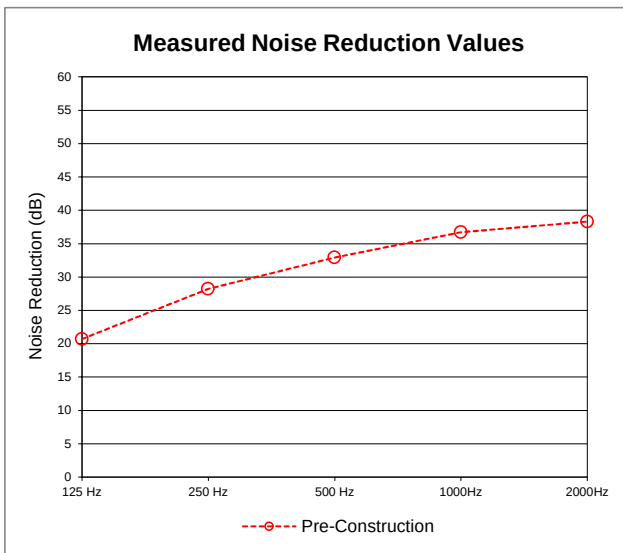



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Fevriere
 Address: 20735 10th Ave S
 Local City: Des Moines

Tested Room: Living / Kitchen Façade 2
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.2	51.2	47.0	47.5	40.3	51.0
Exterior Measurement (flush)	98.4	98.0	98.5	93.5	89.2	99.5
Exterior Adjusted	92.4	92.0	92.5	87.5	83.2	93.5
Interior Background	45.1	37.2	28.1	25.5	21.8	33.9
Interior Measurement	70.4	62.2	54.4	45.8	39.3	58.1
Interior Adjusted	70.4	62.2	54.4	45.8	39.2	58.1
Noise Reduction	22.0	29.8	38.1	41.7	44.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.3	27.3	27.0	24.9	17.8	33.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.8 dB

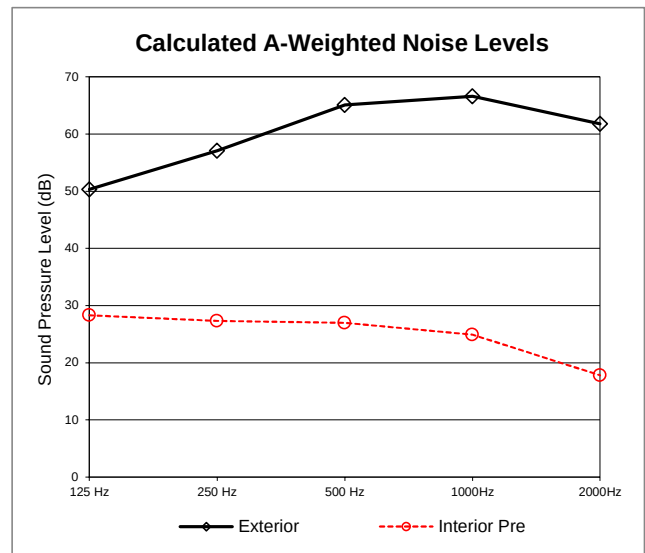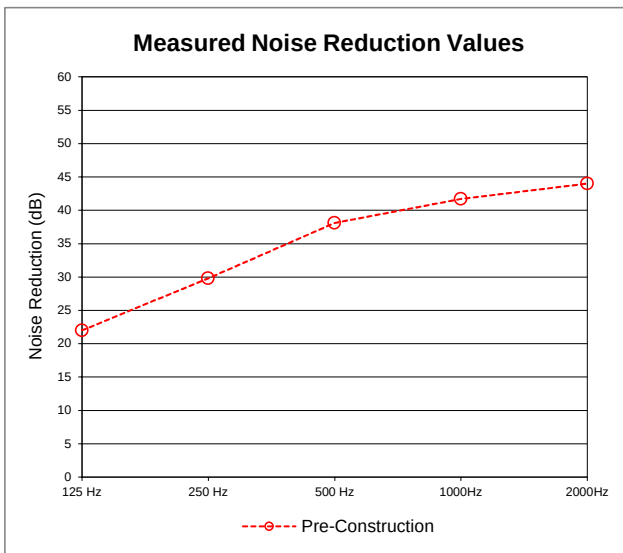

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Fevriere
 Address: 20735 10th Ave S
 Local City: Des Moines

Tested Room: Living / Kitchen Façade 3
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.6	45.9	42.8	40.3	33.5	45.5
Exterior Measurement (flush)	90.3	90.9	92.4	87.5	83.9	93.2
Exterior Adjusted	84.3	84.9	86.4	81.5	77.9	87.2
Interior Background	45.1	37.2	28.1	25.5	21.8	33.9
Interior Measurement	65.6	58.7	57.1	48.1	38.3	57.0
Interior Adjusted	65.6	58.7	57.1	48.1	38.2	57.0
Noise Reduction	18.7	26.2	29.3	33.4	39.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.6	30.9	35.8	33.2	22.1	39.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.6 dB

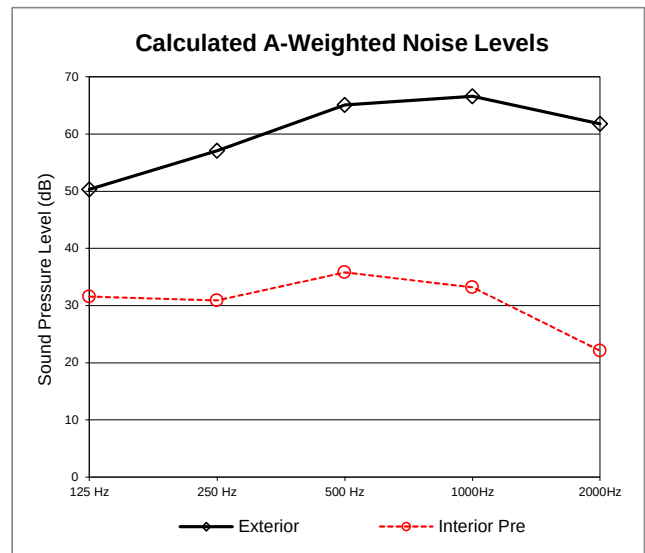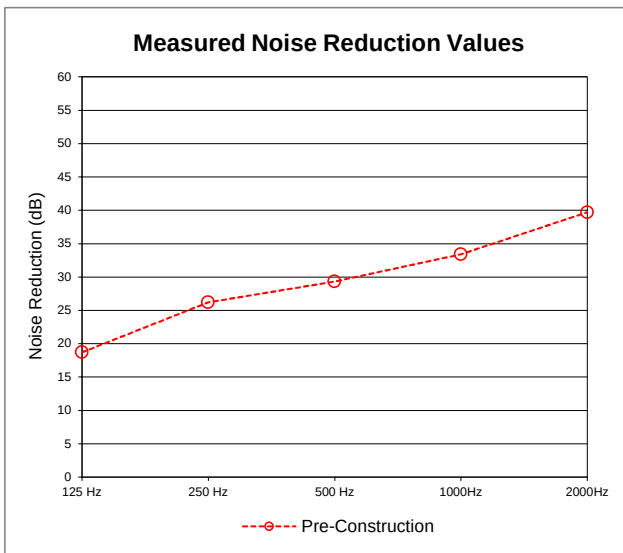

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Fevriere
 Address: 20735 10th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.3	50.9	45.9	43.3	36.4	48.6
Exterior Measurement (flush)	94.0	95.1	94.8	90.7	83.9	95.4
Exterior Adjusted	88.0	89.1	88.8	84.7	77.9	89.4
Interior Background	45.0	39.8	31.4	24.7	23.9	35.6
Interior Measurement	66.5	63.0	55.9	47.6	40.5	57.8
Interior Adjusted	66.5	63.0	55.9	47.6	40.4	57.8
Noise Reduction	21.5	26.1	32.9	37.1	37.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.8	31.0	32.2	29.5	24.3	36.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.2 dB

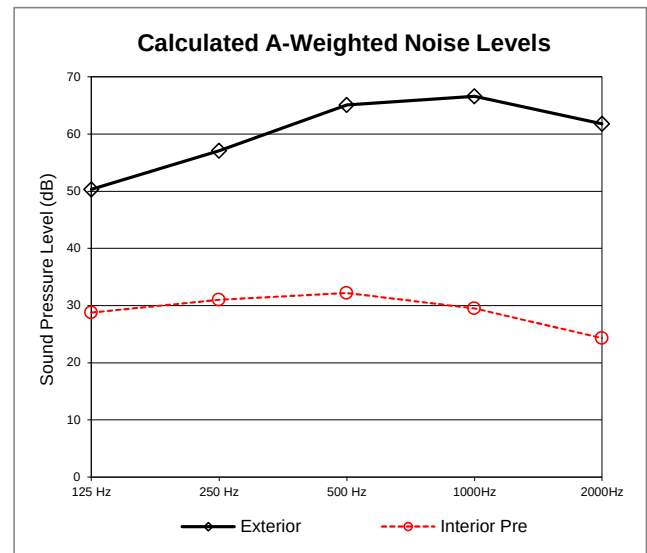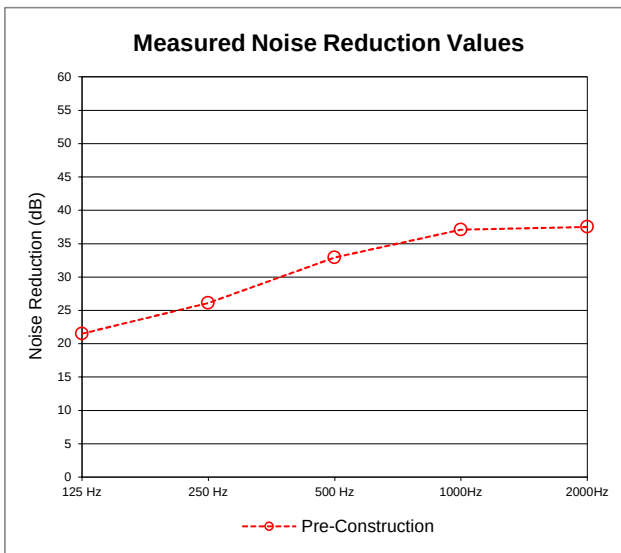

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Fevriere
 Address: 20735 10th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.9	61.3	59.6	54.8	50.1	60.5
Exterior Measurement (flush)	94.2	93.4	94.7	90.3	87.3	96.2
Exterior Adjusted	88.2	87.4	88.7	84.3	81.3	90.2
Interior Background	51.5	42.6	35.0	26.7	23.0	39.4
Interior Measurement	67.8	59.6	54.4	44.7	39.1	56.3
Interior Adjusted	67.7	59.5	54.3	44.6	39.0	56.2
Noise Reduction	20.5	27.9	34.4	39.7	42.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.8	29.2	30.7	26.9	19.5	35.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.5 dB

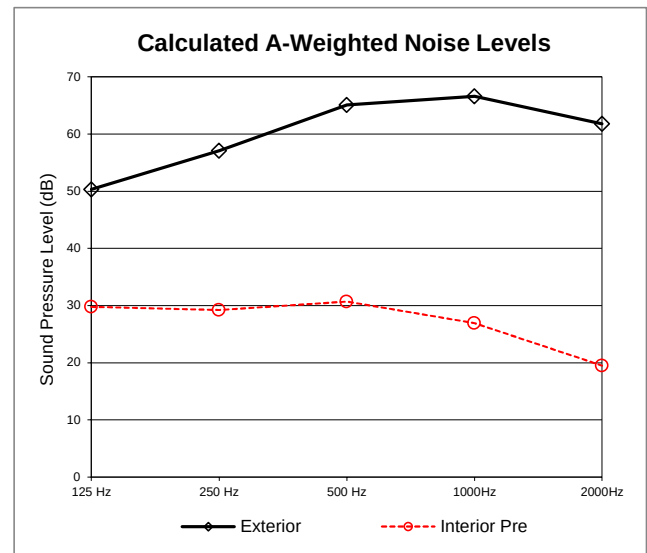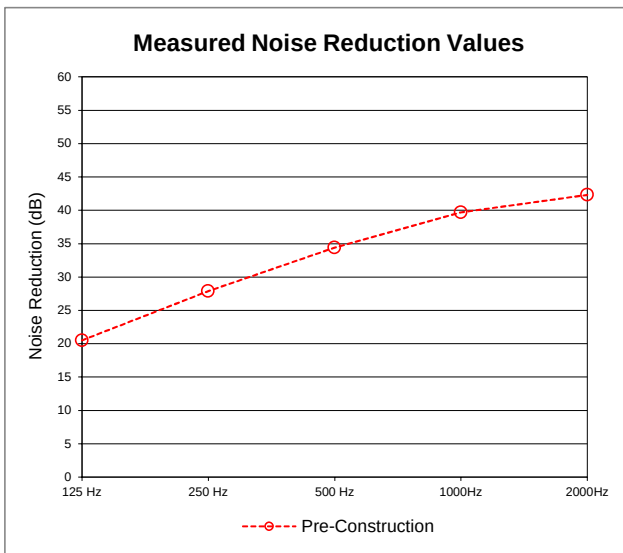



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	61.6	57.7	56.3	48.6	60.1
Exterior Measurement (flush)	90.4	91.1	90.8	89.5	88.6	95.8
Exterior Adjusted	84.4	85.1	84.8	83.5	82.6	89.8
Interior Background	39.9	34.3	28.7	33.2	29.3	36.6
Interior Measurement	64.9	58.4	54.3	50.0	52.4	58.8
Interior Adjusted	64.9	58.4	54.3	49.9	52.4	58.8
Noise Reduction	19.5	26.7	30.5	33.6	30.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.8	30.4	34.6	33.0	31.6	39.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.6 dB

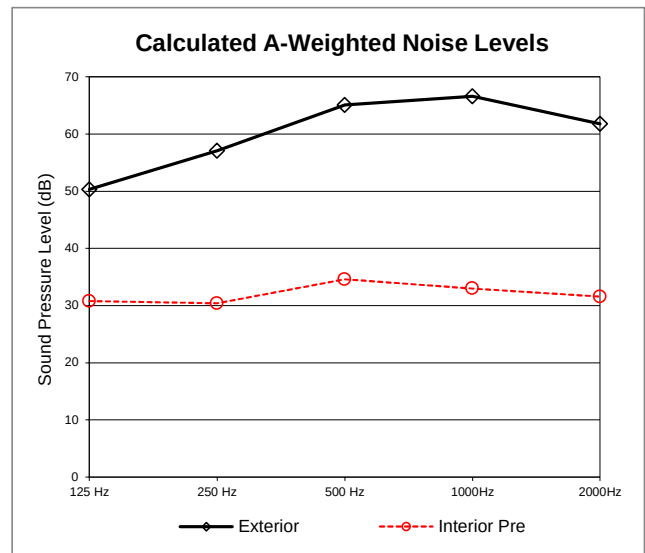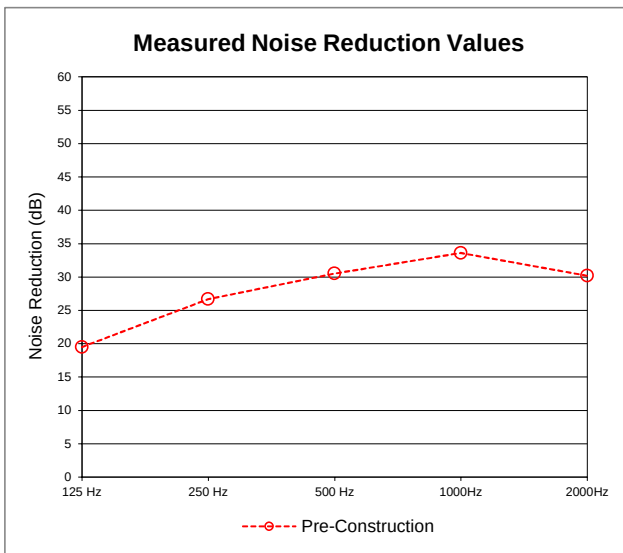



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	61.6	57.7	56.3	48.6	60.1
Exterior Measurement (flush)	94.1	87.5	88.4	89.4	83.9	93.1
Exterior Adjusted	88.1	81.5	82.4	83.4	77.9	87.1
Interior Background	37.4	33.6	29.8	27.0	24.7	32.7
Interior Measurement	58.2	50.2	50.5	45.3	39.0	51.1
Interior Adjusted	58.2	50.1	50.5	45.2	38.8	51.0
Noise Reduction	29.9	31.4	31.9	38.2	39.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	20.4	25.7	33.2	28.4	22.7	35.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.6 dB

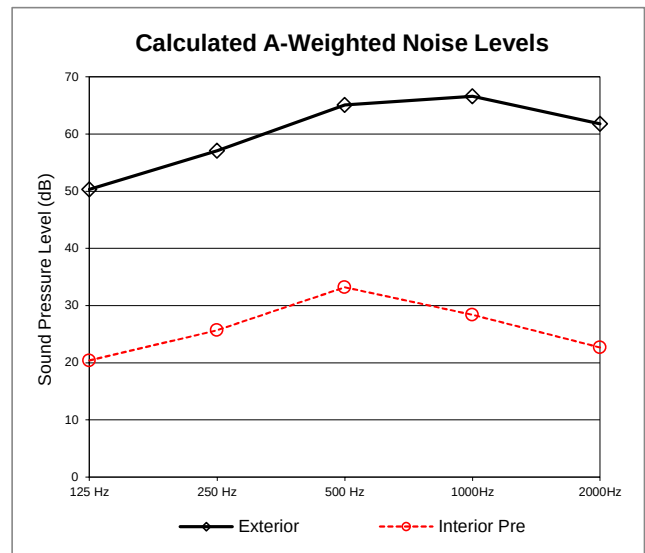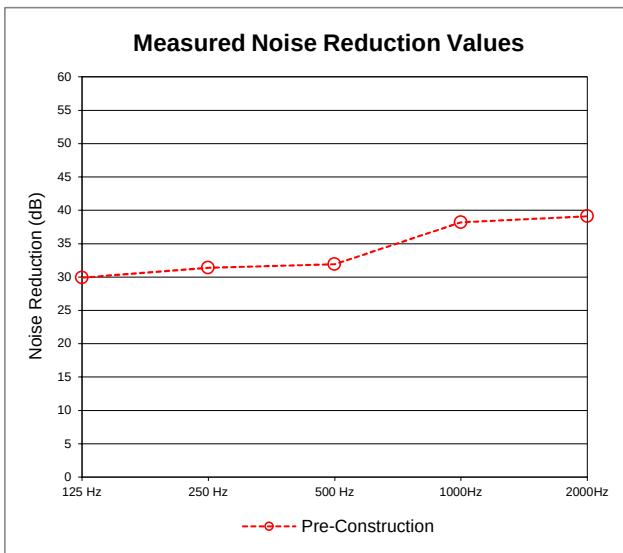

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen 1 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.2	50.7	50.2	52.2	46.0	54.8
Exterior Measurement (flush)	94.2	92.7	92.7	88.8	87.7	96.1
Exterior Adjusted	88.2	86.7	86.7	82.8	81.7	90.1
Interior Background	42.9	39.0	31.1	24.7	22.6	34.5
Interior Measurement	65.1	59.0	54.4	48.8	50.0	57.5
Interior Adjusted	65.1	59.0	54.4	48.8	50.0	57.5
Noise Reduction	23.1	27.7	32.3	34.0	31.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.2	29.4	32.8	32.6	30.1	37.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.1 dB

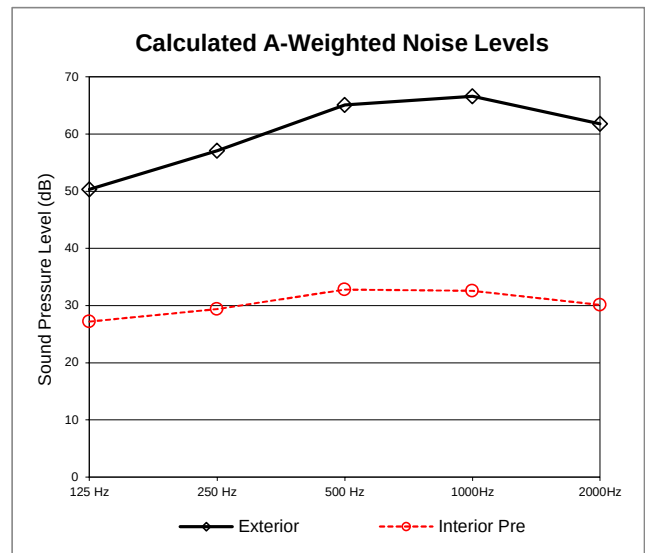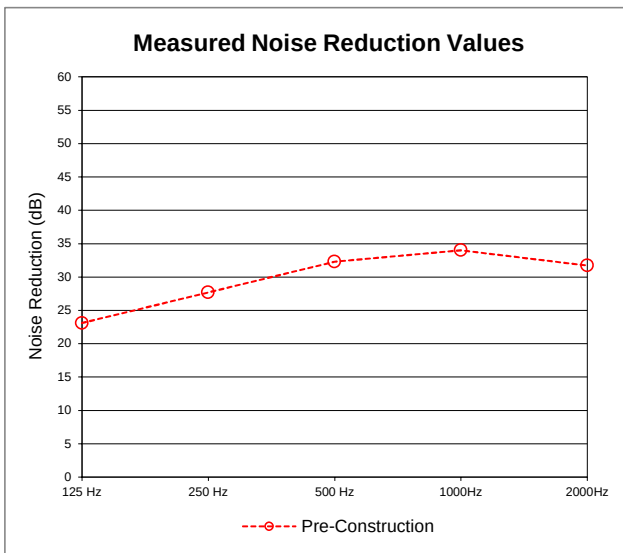

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen 1 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	50.5	46.8	50.3	43.8	53.1
Exterior Measurement (flush)	87.5	89.2	89.4	86.6	84.1	92.4
Exterior Adjusted	81.5	83.2	83.4	80.6	78.1	86.4
Interior Background	42.9	39.0	31.1	24.7	22.6	34.5
Interior Measurement	59.3	56.6	55.9	49.9	51.0	57.7
Interior Adjusted	59.2	56.5	55.9	49.9	51.0	57.7
Noise Reduction	22.3	26.7	27.5	30.7	27.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.0	30.4	37.6	35.9	34.7	41.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.4 dB

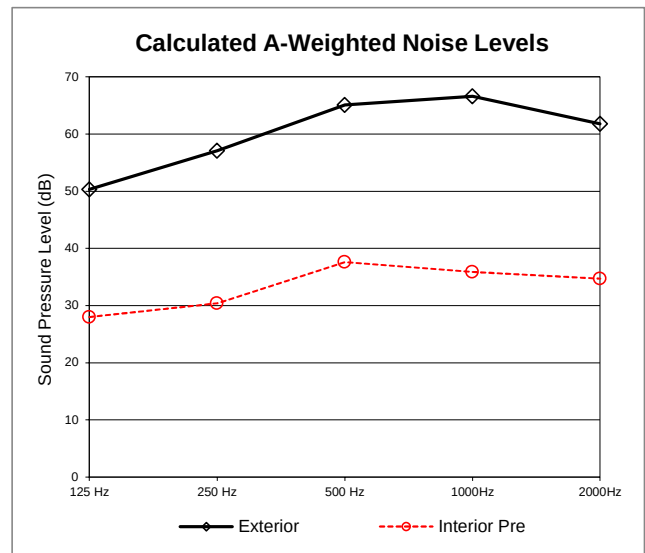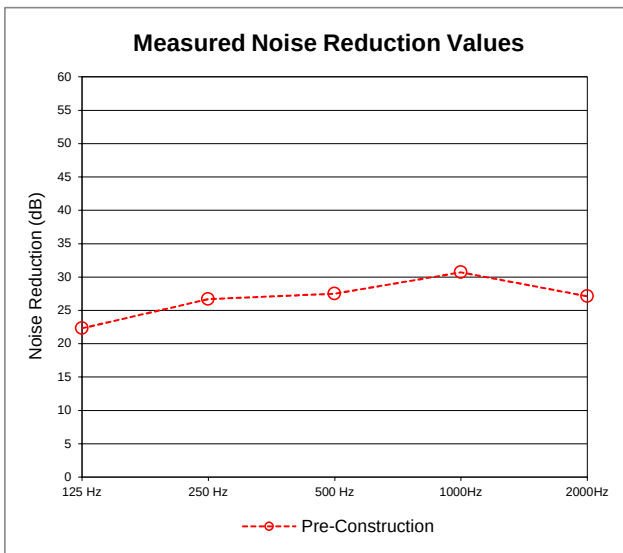



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Kitchen 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.2	50.7	50.2	52.2	46.0	54.8
Exterior Measurement (flush)	90.8	94.3	95.3	92.7	90.4	98.5
Exterior Adjusted	84.8	88.3	89.3	86.7	84.4	92.5
Interior Background	44.0	36.4	30.1	27.3	24.4	34.2
Interior Measurement	64.4	58.0	55.0	49.8	44.2	56.4
Interior Adjusted	64.4	58.0	55.0	49.8	44.2	56.4
Noise Reduction	20.4	30.3	34.3	36.9	40.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.9	26.8	30.8	29.7	21.6	35.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.3 dB

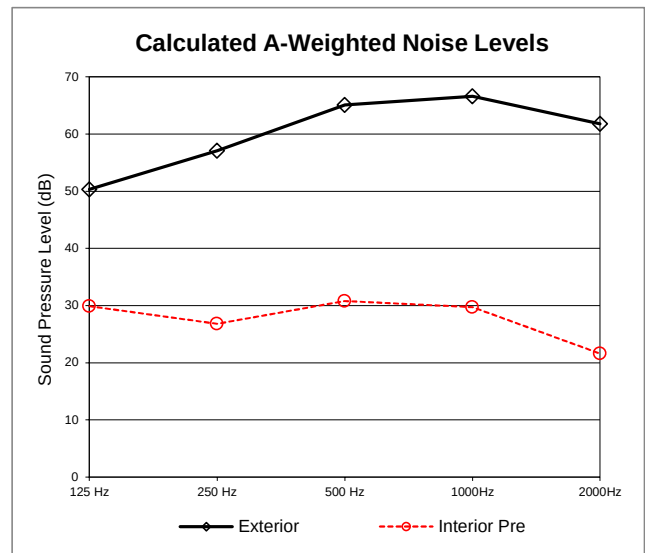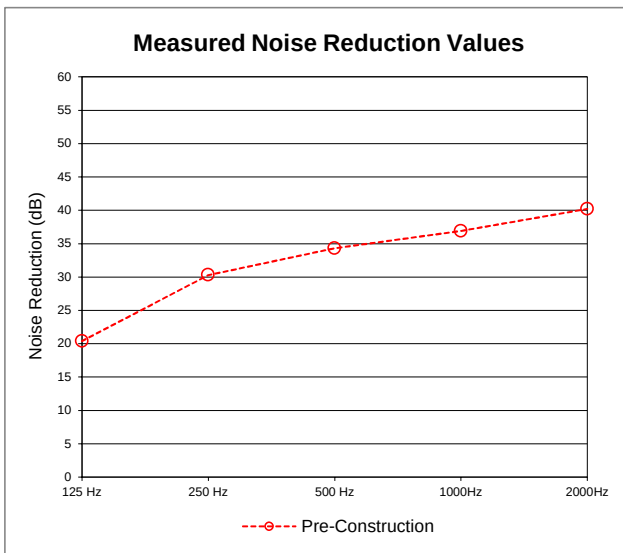



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	50.5	46.8	50.3	43.8	53.1
Exterior Measurement (flush)	87.2	90.2	91.4	89.2	85.1	93.5
Exterior Adjusted	81.2	84.2	85.4	83.2	79.1	87.5
Interior Background	41.9	35.2	25.1	17.6	14.2	30.2
Interior Measurement	59.3	56.6	55.9	49.9	51.0	57.7
Interior Adjusted	59.2	56.6	55.9	49.9	51.0	57.7
Noise Reduction	22.0	27.6	29.5	33.3	28.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.3	29.5	35.6	33.3	33.7	39.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.1 dB

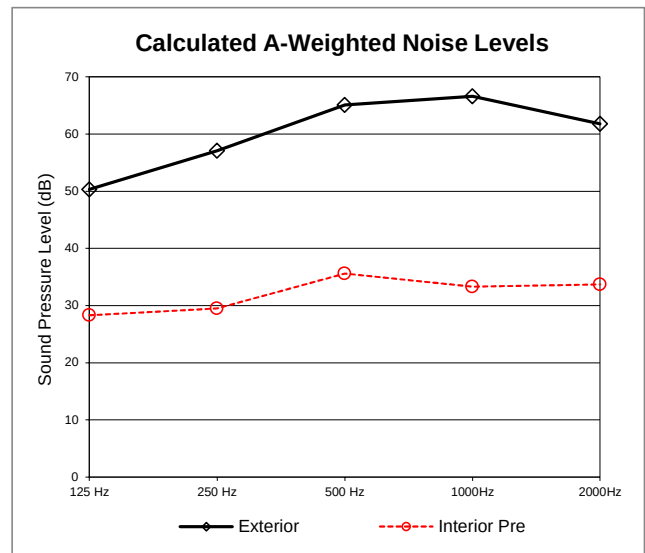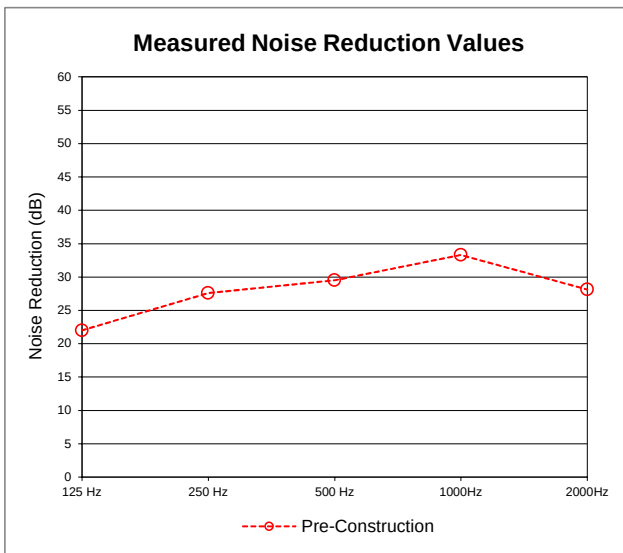



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	61.6	57.7	56.3	48.6	60.1
Exterior Measurement (flush)	90.1	91.1	91.1	89.3	85.4	94.3
Exterior Adjusted	84.1	85.1	85.1	83.3	79.4	88.3
Interior Background	27.8	21.9	17.7	13.9	13.2	23.0
Interior Measurement	60.0	57.1	52.2	44.4	45.4	53.9
Interior Adjusted	60.0	57.1	52.2	44.4	45.4	53.9
Noise Reduction	24.1	28.0	32.9	38.9	34.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.2	29.1	32.2	27.7	27.8	36.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.9 dB

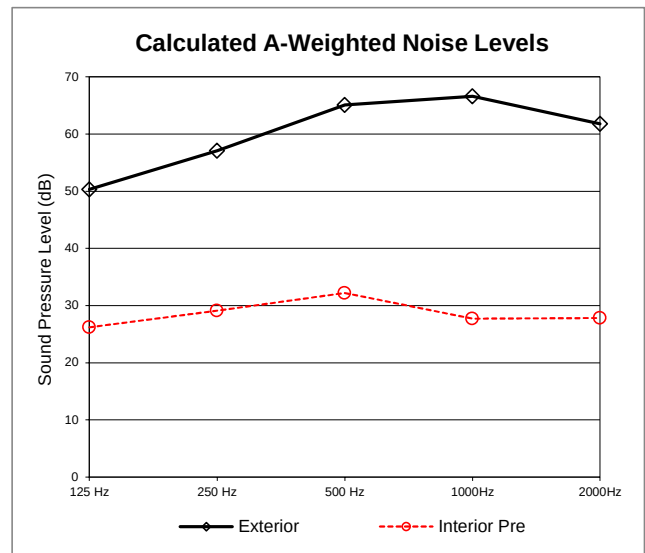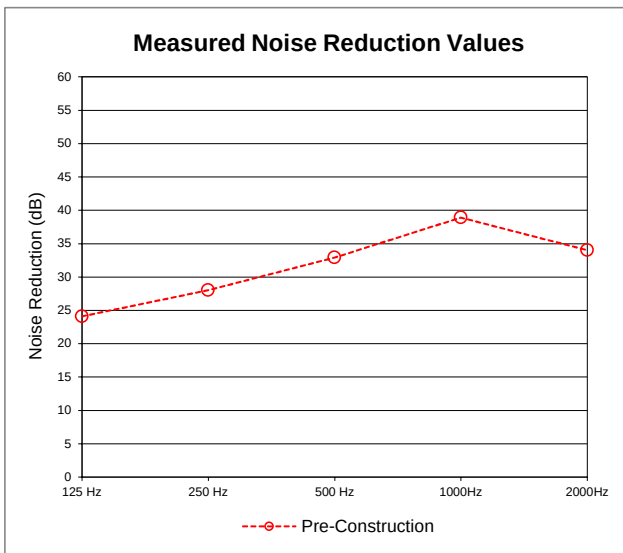



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	61.6	57.7	56.3	48.6	60.1
Exterior Measurement (flush)	94.2	92.2	93.4	92.3	90.0	97.4
Exterior Adjusted	88.2	86.2	87.4	86.3	84.0	91.4
Interior Background	38.0	30.2	27.8	26.0	24.9	33.4
Interior Measurement	68.6	59.7	55.0	42.9	44.0	57.1
Interior Adjusted	68.6	59.7	55.0	42.8	43.9	57.1
Noise Reduction	19.6	26.5	32.4	43.5	40.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.7	30.6	32.7	23.1	21.7	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

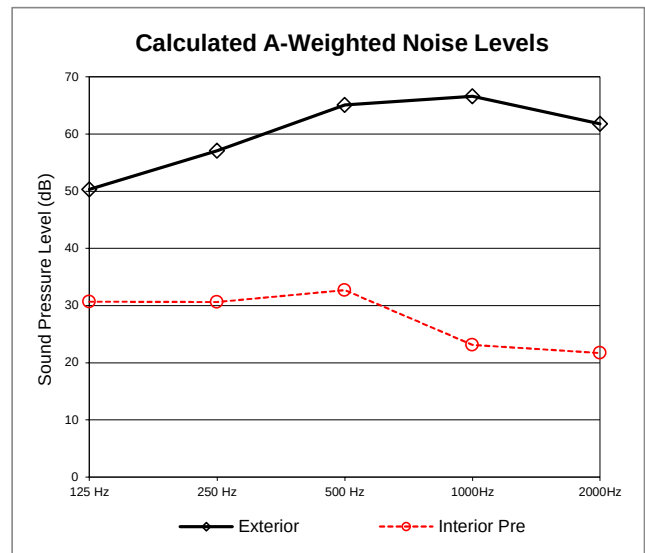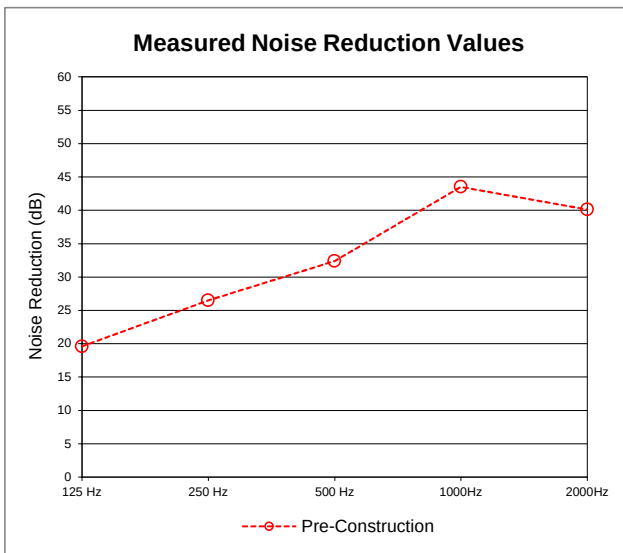

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	50.5	46.8	50.3	43.8	53.1
Exterior Measurement (flush)	90.8	86.4	90.9	87.5	85.3	93.6
Exterior Adjusted	84.8	80.4	84.9	81.5	79.3	87.6
Interior Background	35.6	29.0	16.4	19.1	19.8	27.5
Interior Measurement	55.5	47.8	49.4	46.8	49.9	56.8
Interior Adjusted	55.5	47.7	49.4	46.8	49.9	56.8
Noise Reduction	29.3	32.7	35.5	34.7	29.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	21.0	24.4	29.6	31.9	32.4	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

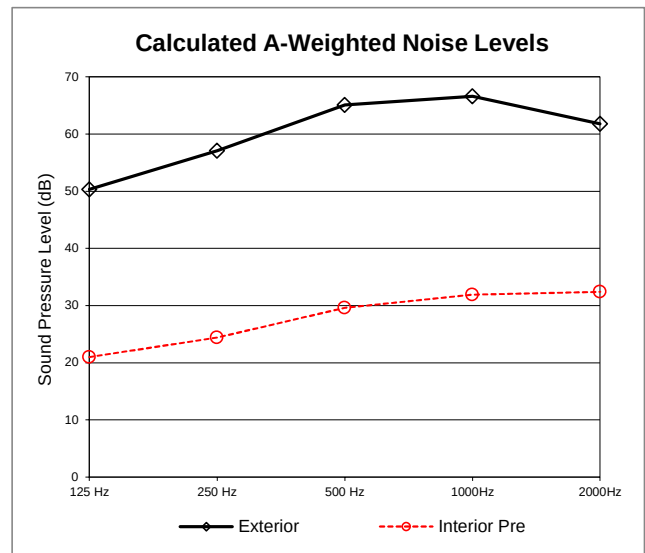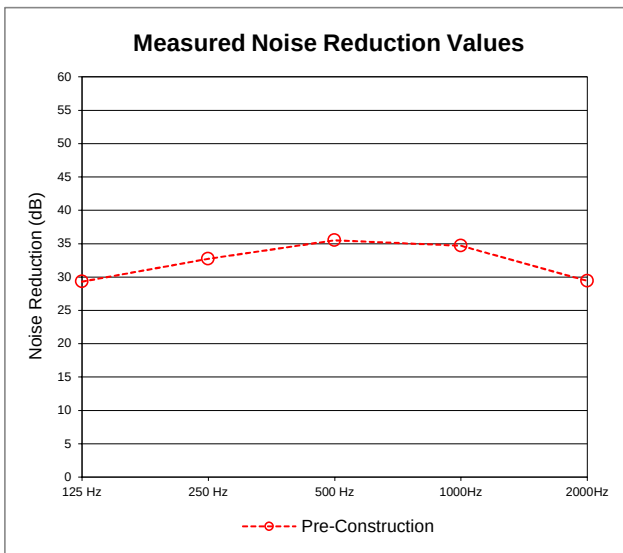



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Bedroom 5 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	50.5	46.8	50.3	43.8	53.1
Exterior Measurement (flush)	89.8	88.9	91.7	89.1	85.8	94.8
Exterior Adjusted	83.8	82.9	85.7	83.1	79.8	88.8
Interior Background	29.1	23.6	19.0	15.1	11.2	22.6
Interior Measurement	72.1	65.2	65.0	51.6	48.3	64.2
Interior Adjusted	72.1	65.2	65.0	51.6	48.3	64.2
Noise Reduction	11.7	17.7	20.7	31.5	31.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	38.6	39.4	44.4	35.1	30.3	46.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						23.2 dB

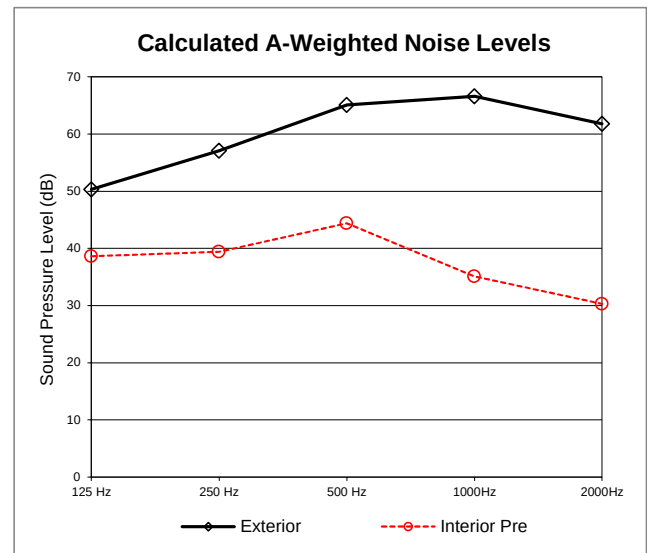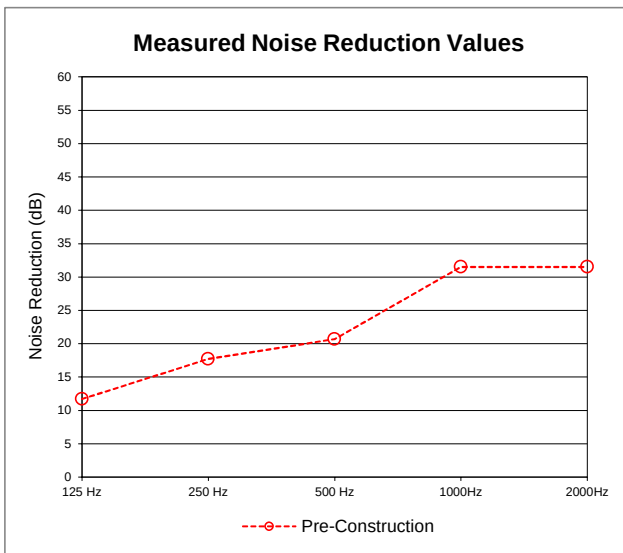

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gobena
 Address: 21457 13th Ave S
 Local City: Des Moines

Tested Room: Bedroom 6 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	61.6	57.7	56.3	48.6	60.1
Exterior Measurement (flush)	94.9	89.2	93.6	92.9	87.0	96.4
Exterior Adjusted	88.9	83.2	87.6	86.9	81.0	90.4
Interior Background	25.7	21.7	15.6	14.0	13.8	22.3
Interior Measurement	60.1	54.9	54.8	46.9	41.5	54.4
Interior Adjusted	60.1	54.9	54.8	46.9	41.5	54.4
Noise Reduction	28.8	28.3	32.8	40.0	39.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	21.5	28.8	32.3	26.6	22.3	35.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.9 dB

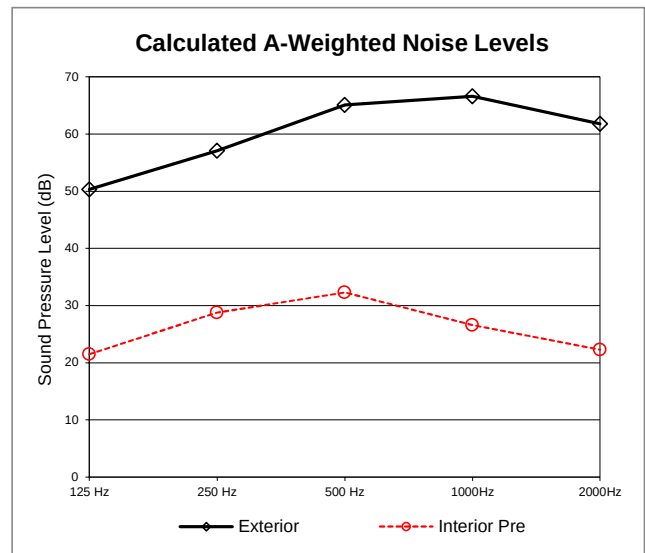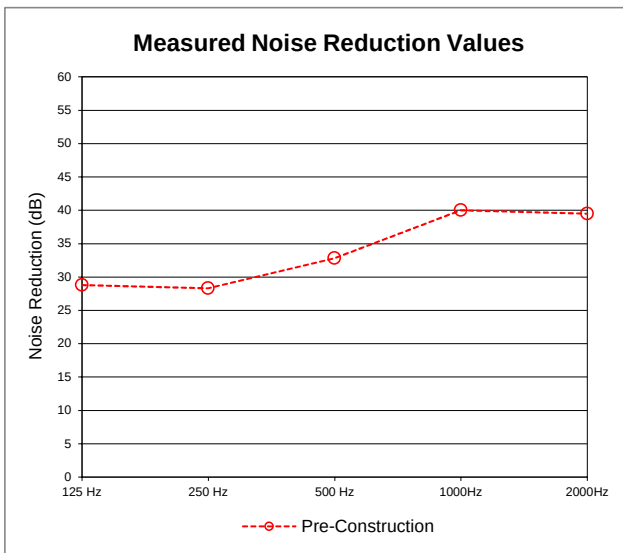



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.1	49.7	51.2	54.3	45.3	56.0
Exterior Measurement (flush)	89.9	85.6	89.2	88.2	83.6	92.8
Exterior Adjusted	83.9	79.6	83.2	82.2	77.6	86.8
Interior Background	41.5	34.5	27.9	22.6	17.2	31.0
Interior Measurement	67.8	59.0	59.1	52.6	46.5	59.5
Interior Adjusted	67.8	59.0	59.1	52.6	46.5	59.5
Noise Reduction	16.1	20.6	24.1	29.6	31.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.2	36.5	41.0	37.0	30.7	44.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						25.9 dB

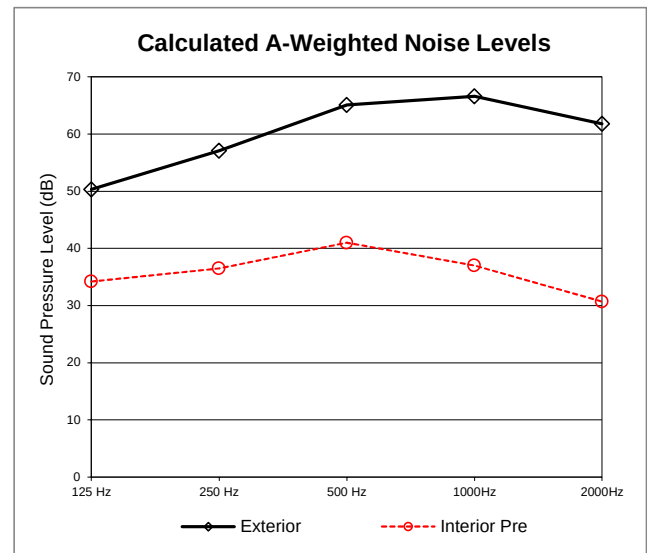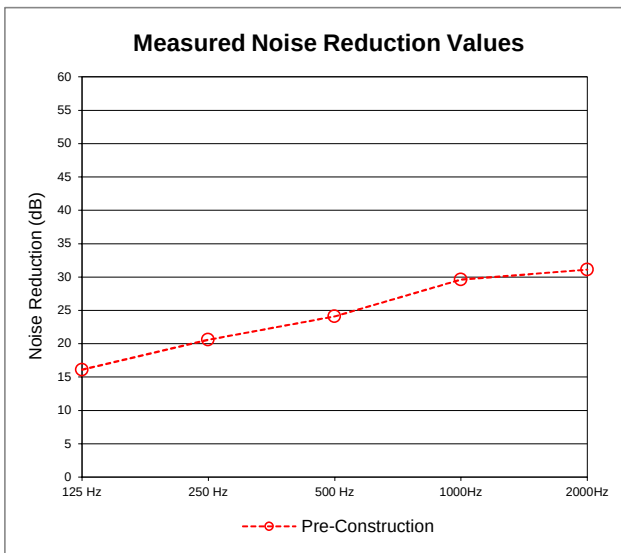

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Dining Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	52.1	51.0	51.4	51.9	47.1	54.9
Exterior Measurement (flush)	102.2	104.5	104.7	99.3	95.8	106.0
Exterior Adjusted	96.2	98.5	98.7	93.3	89.8	100.0
Interior Background	45.7	41.4	38.4	33.8	26.9	39.6
Interior Measurement	78.1	75.8	71.5	61.8	57.5	72.0
Interior Adjusted	78.1	75.8	71.5	61.8	57.5	72.0
Noise Reduction	18.1	22.7	27.2	31.5	32.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.2	34.4	37.9	35.1	29.5	41.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.3 dB

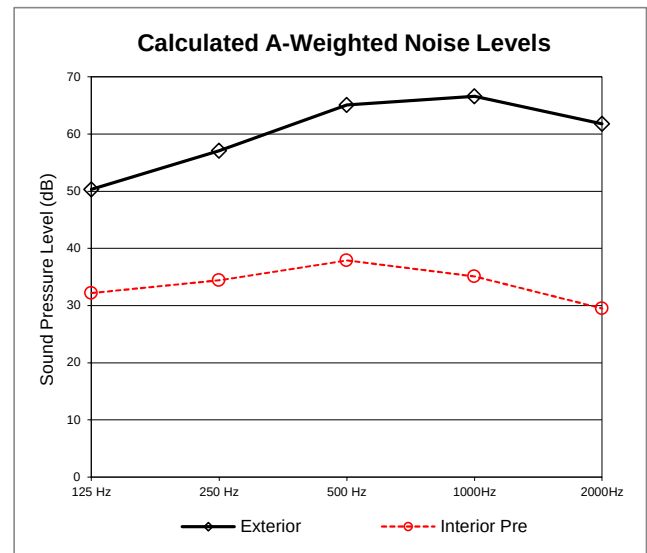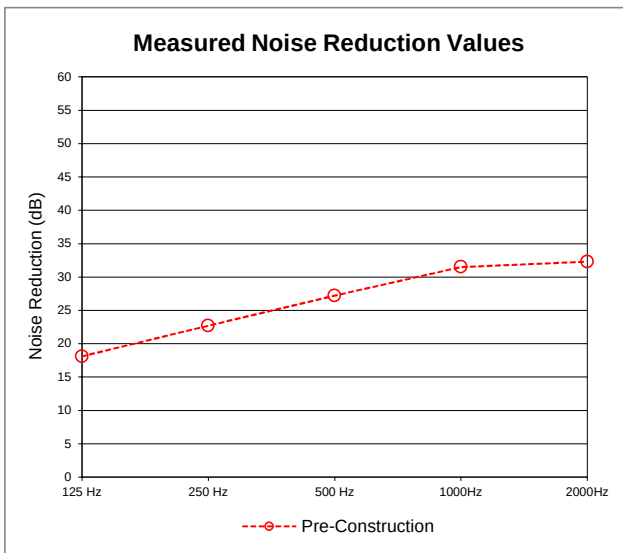



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Kitchen Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.7	52.0	50.8	50.9	43.7	53.8
Exterior Measurement (flush)	100.8	100.2	101.2	97.1	94.4	103.6
Exterior Adjusted	94.8	94.2	95.2	91.1	88.4	97.6
Interior Background	43.7	46.3	40.2	32.2	26.4	41.1
Interior Measurement	74.8	75.8	75.6	68.1	66.2	75.9
Interior Adjusted	74.8	75.8	75.6	68.1	66.2	75.9
Noise Reduction	20.0	18.4	19.6	23.0	22.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.3	38.7	45.5	43.6	39.6	48.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						21.2 dB

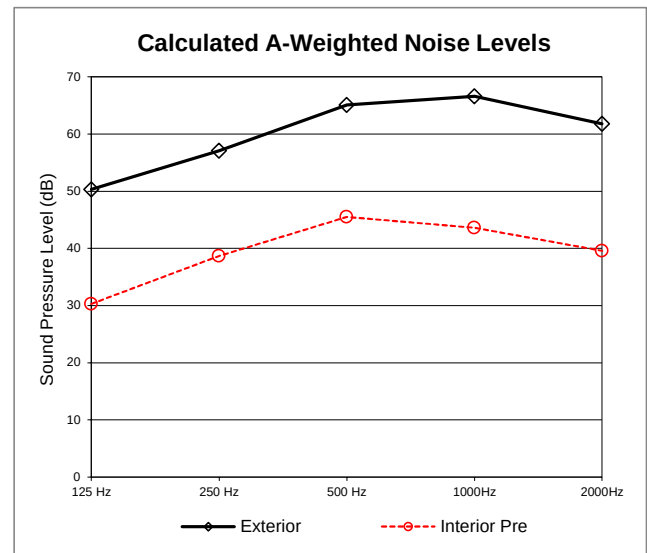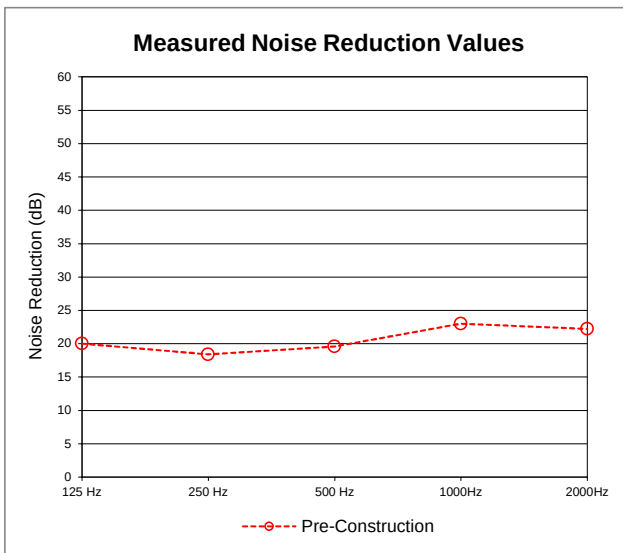



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Kitchen Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.7	52.0	50.8	50.9	43.7	53.8
Exterior Measurement (flush)	97.4	95.9	96.8	94.6	89.4	99.3
Exterior Adjusted	91.4	89.9	90.8	88.6	83.4	93.3
Interior Background	43.7	46.3	40.2	32.2	26.4	41.1
Interior Measurement	71.9	65.3	64.1	58.0	61.4	68.0
Interior Adjusted	71.9	65.2	64.1	58.0	61.4	68.0
Noise Reduction	19.5	24.7	26.7	30.6	22.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.8	32.4	38.4	36.0	39.8	43.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						26.3 dB

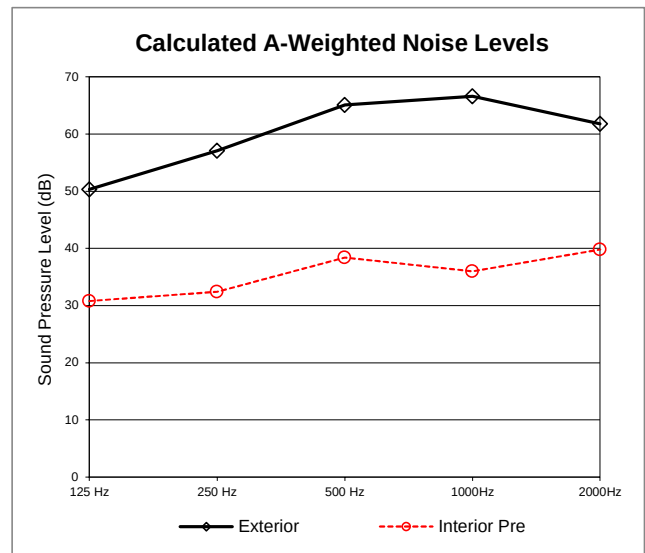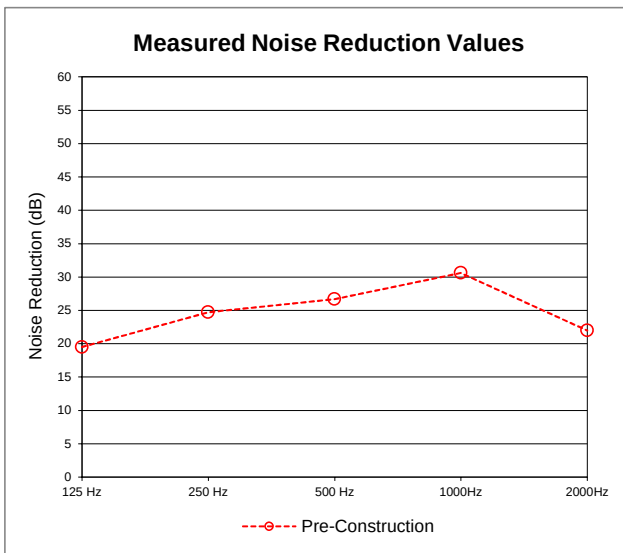

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.1	49.7	51.2	54.3	45.3	56.0
Exterior Measurement (flush)	89.3	84.6	87.9	86.2	82.6	91.6
Exterior Adjusted	83.3	78.6	81.9	80.2	76.6	85.6
Interior Background	40.0	32.3	27.7	20.4	13.9	29.6
Interior Measurement	66.7	55.5	53.0	44.1	37.2	54.2
Interior Adjusted	66.7	55.5	53.0	44.1	37.2	54.2
Noise Reduction	16.6	23.1	28.9	36.1	39.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.7	34.0	36.2	30.5	22.4	40.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.9 dB

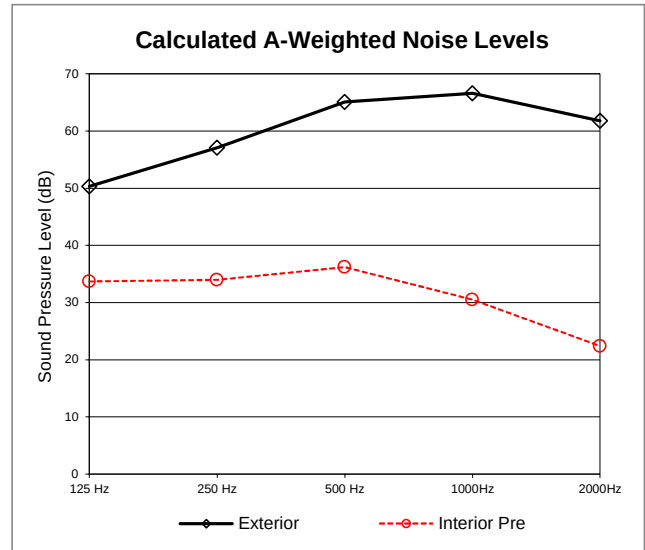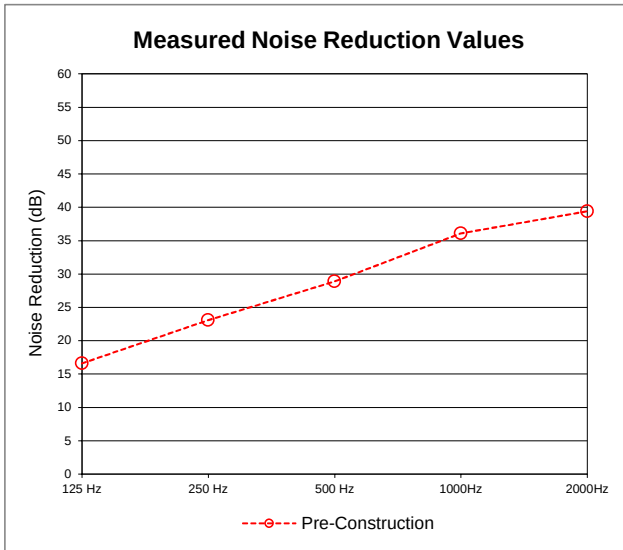



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.4	56.0	53.9	53.4	43.8	56.4
Exterior Measurement (flush)	101.7	100.1	100.0	97.7	93.7	102.9
Exterior Adjusted	95.7	94.1	94.0	91.7	87.7	96.9
Interior Background	38.0	28.0	21.9	17.5	15.9	27.1
Interior Measurement	79.0	70.4	64.2	52.1	47.3	66.5
Interior Adjusted	79.0	70.4	64.2	52.1	47.3	66.5
Noise Reduction	16.7	23.7	29.8	39.6	40.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.6	33.4	35.3	27.0	21.4	39.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.7 dB

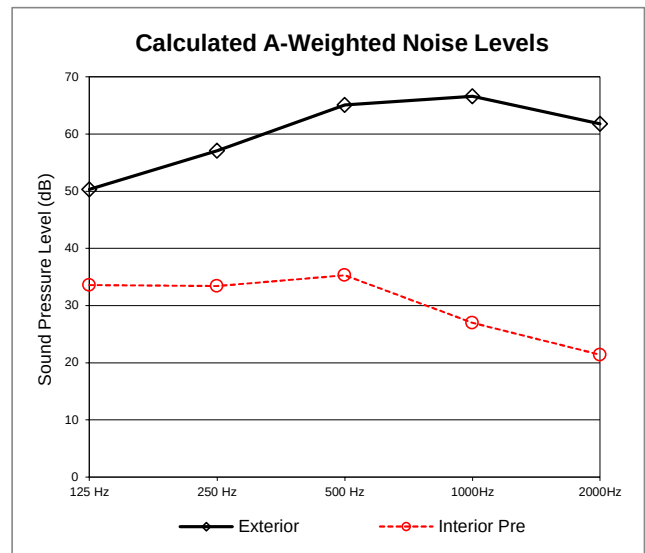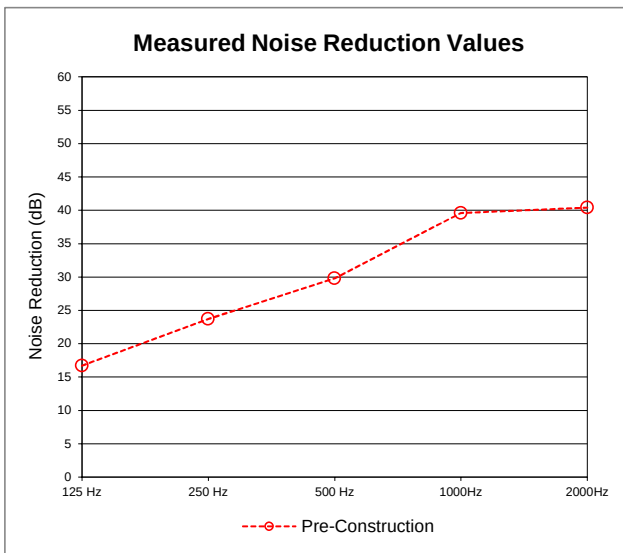



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Sharma
 Address: 11418 14th Ave S
 Local City: Burien

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.7	52.0	50.8	50.9	43.7	53.8
Exterior Measurement (flush)	93.5	94.6	94.2	90.6	86.7	96.5
Exterior Adjusted	87.5	88.6	88.2	84.6	80.7	90.5
Interior Background	40.6	32.2	23.1	15.9	14.2	28.6
Interior Measurement	74.6	66.0	62.8	51.3	40.3	63.5
Interior Adjusted	74.6	66.0	62.8	51.3	40.3	63.5
Noise Reduction	12.9	22.6	25.4	33.3	40.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	37.4	34.5	39.7	33.3	21.4	43.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						27.0 dB

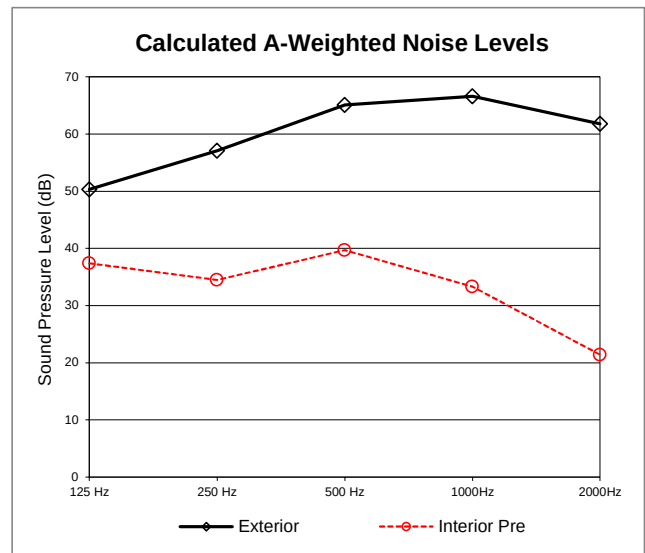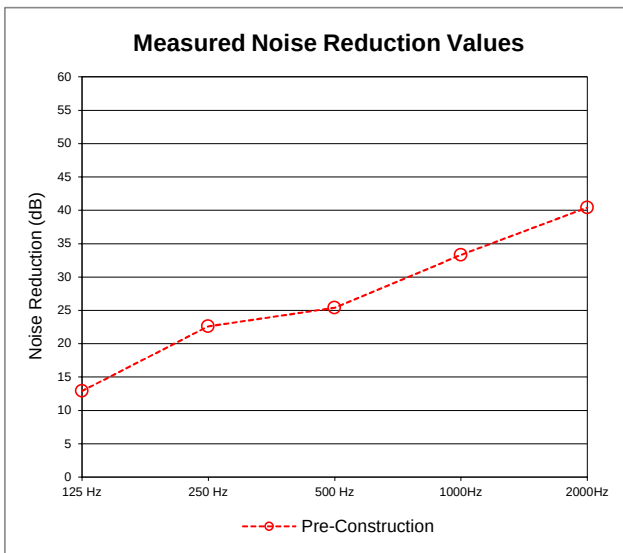

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carbary
 Address: 11510 14th Ave S
 Local City: Burien

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	49.8	47.0	48.6	48.7	39.9	51.4
Exterior Measurement (flush)	89.1	92.5	92.7	89.4	87.0	95.0
Exterior Adjusted	83.1	86.5	86.7	83.4	81.0	89.0
Interior Background	36.5	29.0	22.2	18.0	17.7	27.9
Interior Measurement	66.5	61.3	54.3	45.3	43.1	56.9
Interior Adjusted	66.5	61.3	54.3	45.3	43.1	56.9
Noise Reduction	16.6	25.2	32.4	38.1	37.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.7	31.9	32.7	28.5	23.9	38.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.7 dB

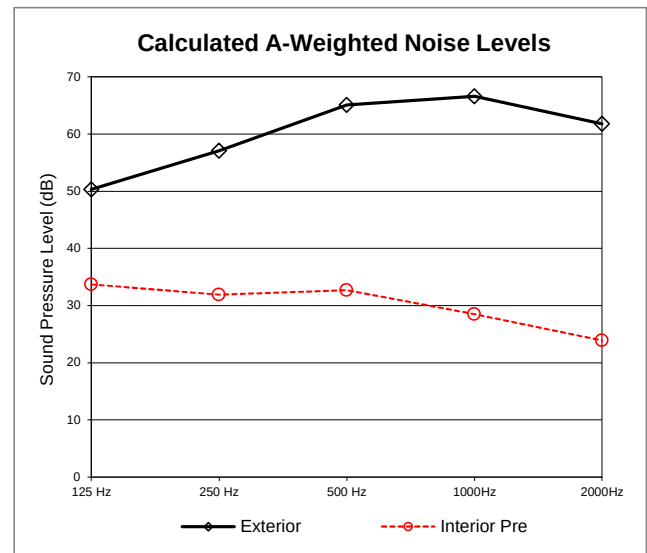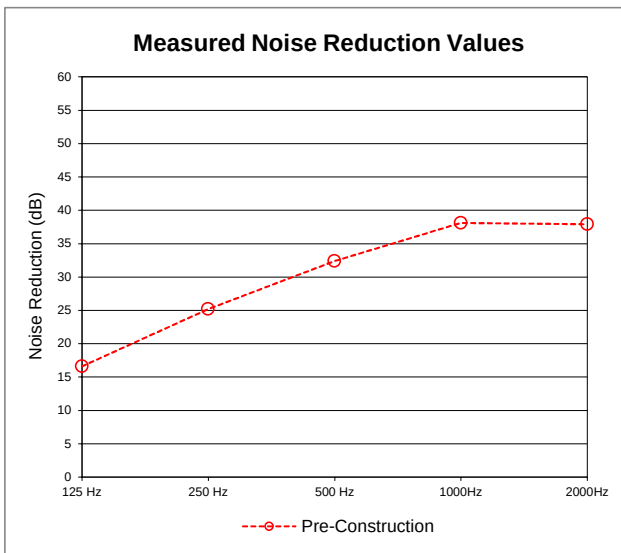

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carbary
 Address: 11510 14th Ave S
 Local City: Burien

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.4	51.6	50.4	48.4	44.4	53.7
Exterior Measurement (flush)	95.7	96.7	96.7	93.9	92.2	99.8
Exterior Adjusted	89.7	90.7	90.7	87.9	86.2	93.8
Interior Background	43.6	40.2	37.5	34.5	31.5	39.9
Interior Measurement	73.0	68.2	64.6	56.7	52.8	65.7
Interior Adjusted	73.0	68.2	64.6	56.7	52.8	65.7
Noise Reduction	16.7	22.5	26.1	31.2	33.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.6	34.6	39.0	35.4	28.4	42.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						27.6 dB

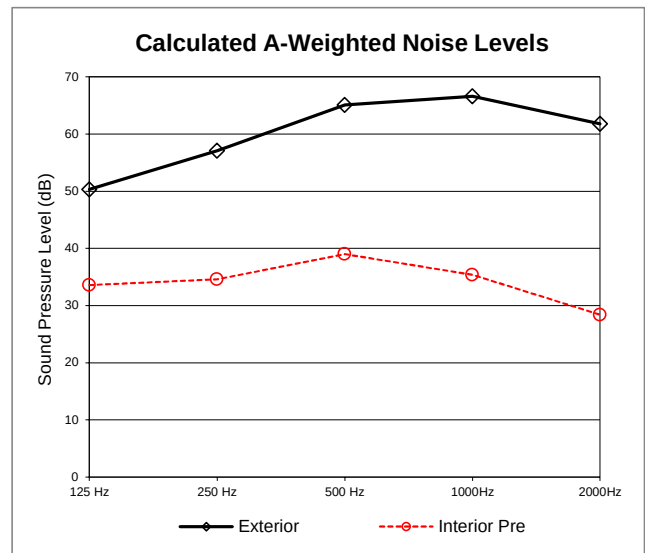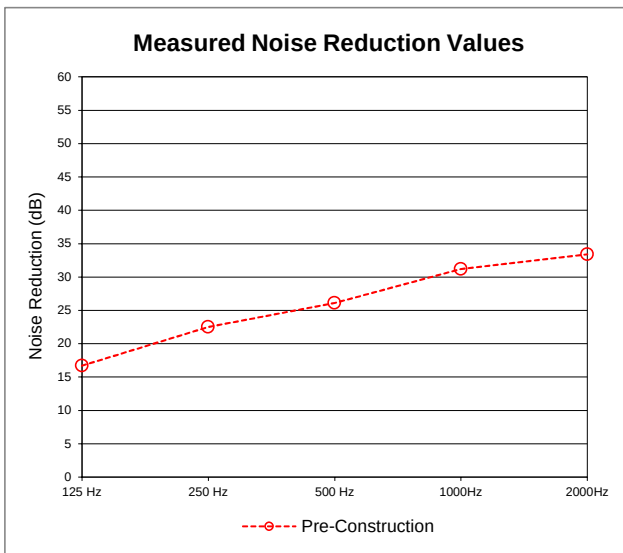



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carbary
 Address: 11510 14th Ave S
 Local City: Burien

Tested Room: Kitchen Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.0	51.9	48.1	48.8	44.9	52.9
Exterior Measurement (flush)	91.7	92.3	93.8	90.6	86.3	96.3
Exterior Adjusted	85.7	86.3	87.8	84.6	80.3	90.3
Interior Background	38.8	31.6	26.0	23.5	21.0	31.0
Interior Measurement	70.4	65.2	64.4	60.1	56.1	66.4
Interior Adjusted	70.4	65.2	64.4	60.1	56.1	66.4
Noise Reduction	15.3	21.1	23.4	24.5	24.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.0	36.0	41.7	42.1	37.6	46.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						23.6 dB

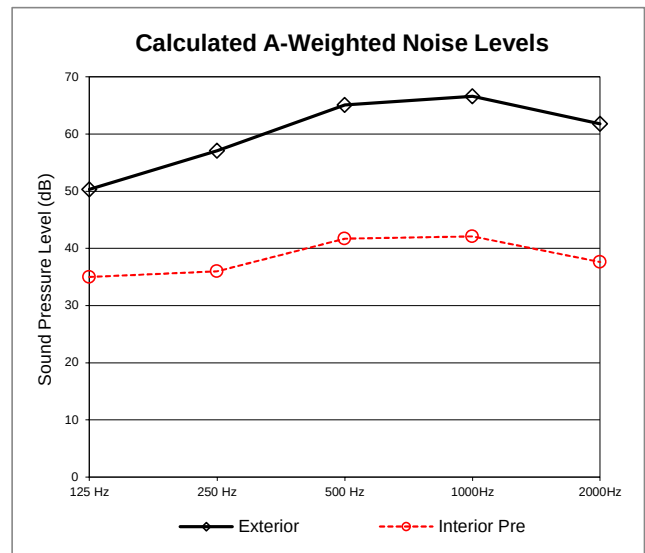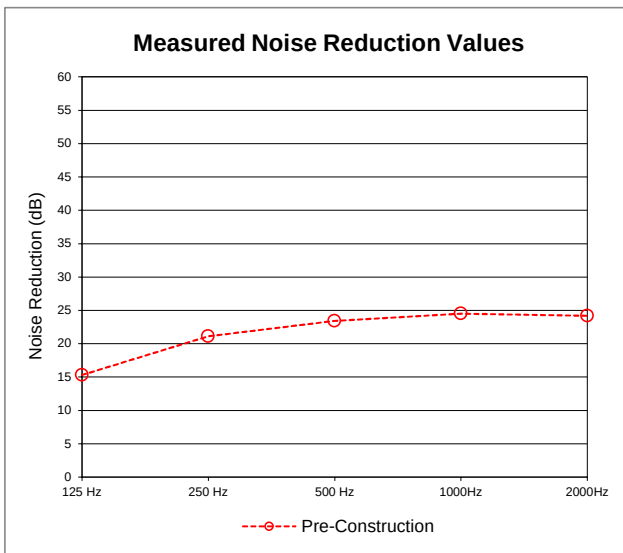

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carbary
 Address: 11510 14th Ave S
 Local City: Burien

Tested Room: Bedroom Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	49.8	47.0	48.6	48.7	39.9	51.4
Exterior Measurement (flush)	97.8	97.8	98.7	96.0	90.8	101.1
Exterior Adjusted	91.8	91.8	92.7	90.0	84.8	95.1
Interior Background	40.3	31.2	23.1	16.8	13.2	32.7
Interior Measurement	65.8	57.5	51.6	44.0	36.2	54.2
Interior Adjusted	65.8	57.5	51.6	44.0	36.2	54.2
Noise Reduction	26.0	34.3	41.1	46.0	48.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	24.3	22.8	24.0	20.6	13.2	29.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						40.7 dB

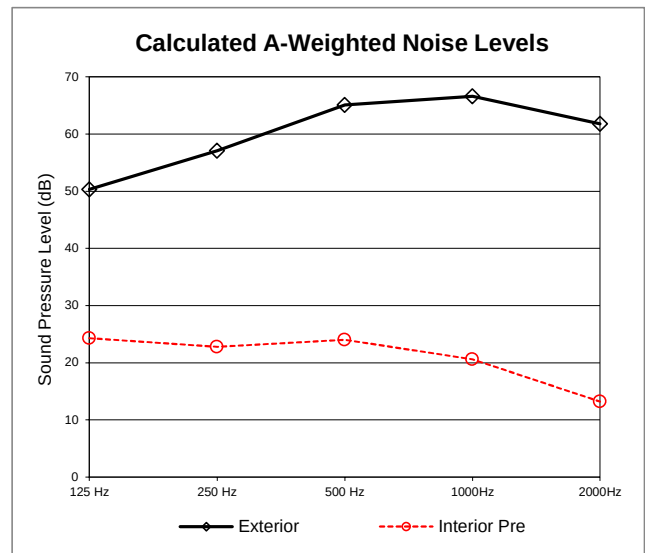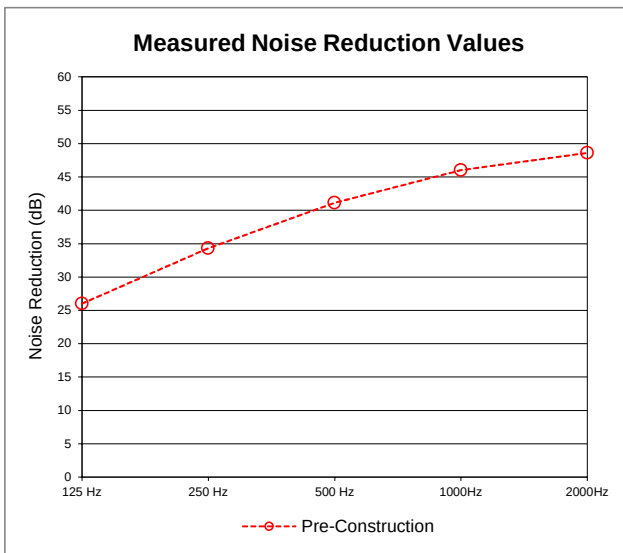



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Living / Dining Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.8	51.2	50.6	54.1	47.5	56.3
Exterior Measurement (flush)	84.0	88.3	86.0	83.5	81.3	89.6
Exterior Adjusted	78.0	82.3	80.0	77.5	75.3	83.6
Interior Background	47.4	39.8	31.4	32.7	26.5	37.8
Interior Measurement	57.9	53.7	48.8	43.1	39.0	51.0
Interior Adjusted	57.5	53.5	48.7	42.7	38.7	50.8
Noise Reduction	20.5	28.8	31.3	34.8	36.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.8	28.3	33.8	31.8	25.2	37.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.3 dB

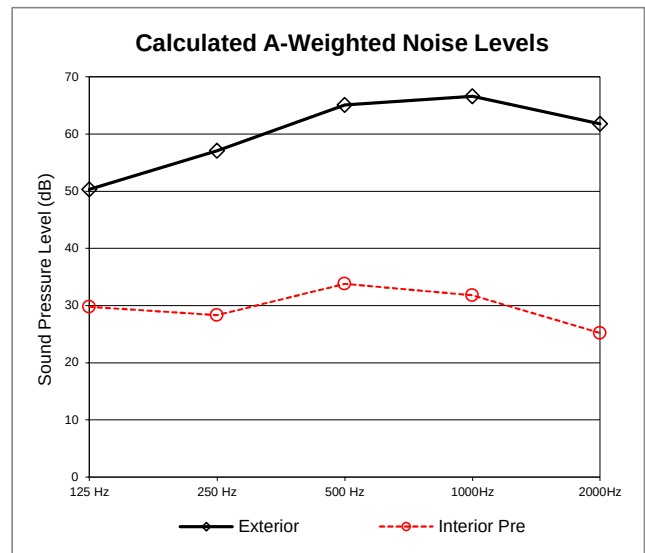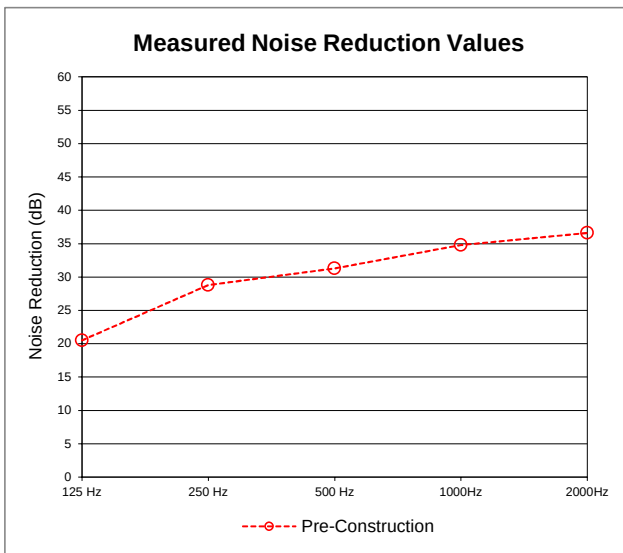



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Living / Dining Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.8	51.2	50.6	54.1	47.5	56.3
Exterior Measurement (flush)	107.9	107.2	104.9	100.1	97.2	107.5
Exterior Adjusted	101.9	101.2	98.9	94.1	91.2	101.5
Interior Background	47.4	39.8	31.4	32.7	26.5	37.8
Interior Measurement	81.0	76.8	71.8	67.3	63.4	74.2
Interior Adjusted	81.0	76.8	71.8	67.3	63.4	74.2
Noise Reduction	20.9	24.4	27.1	26.8	27.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.4	32.7	38.0	39.8	34.0	43.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						26.8 dB

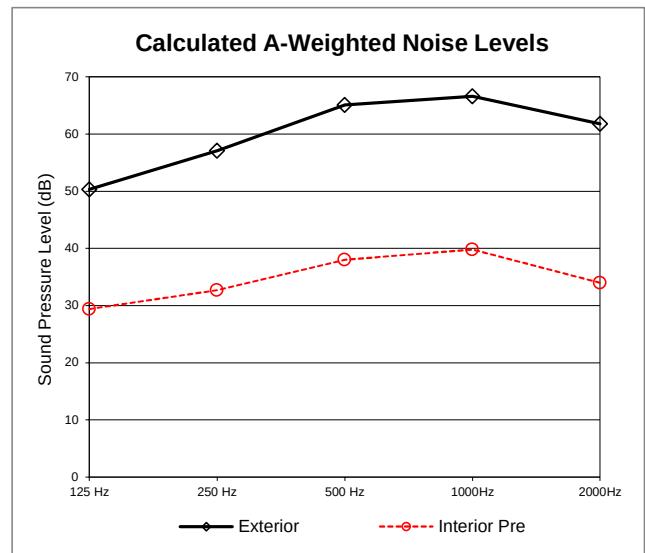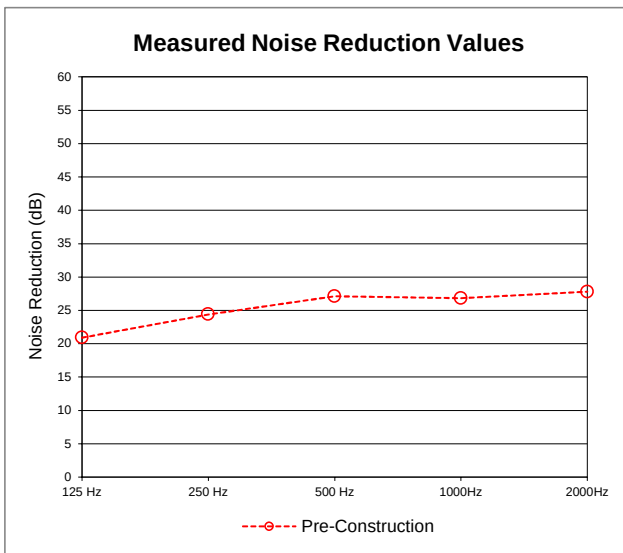



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Family Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	68.8	67.1	63.4	61.7	53.0	65.5
Exterior Measurement (flush)	87.4	83.6	86.2	86.6	79.3	90.0
Exterior Adjusted	81.3	77.5	80.2	80.6	73.3	84.0
Interior Background	50.5	41.3	37.6	27.0	19.8	38.9
Interior Measurement	81.1	73.3	62.5	51.0	53.7	68.6
Interior Adjusted	81.1	73.3	62.5	51.0	53.7	68.6
Noise Reduction	0.2	4.2	17.7	29.6	19.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	50.1	52.9	47.4	37.0	42.2	55.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						14.3 dB

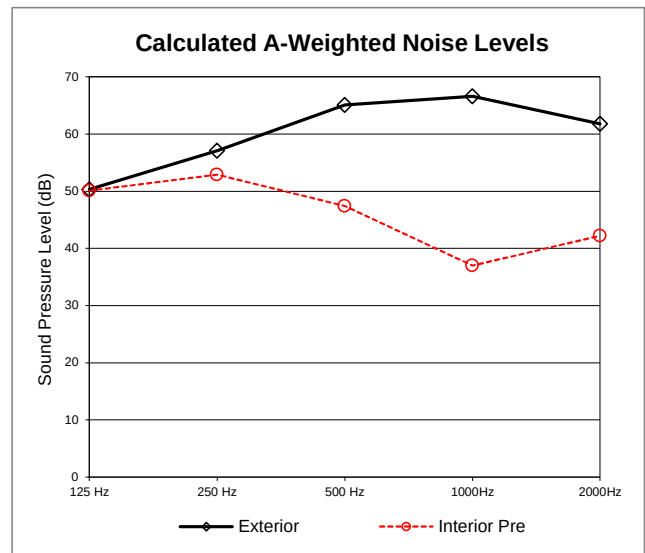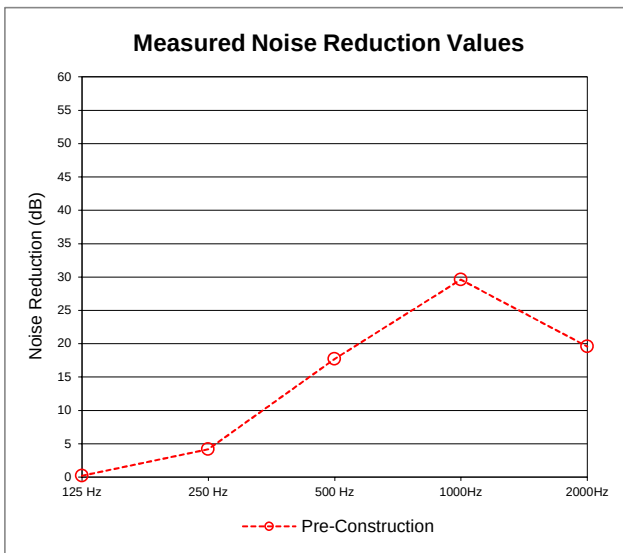



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Family Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	52.5	46.2	46.4	49.1	43.3	52.0
Exterior Measurement (flush)	96.9	96.4	99.5	95.1	92.2	102.0
Exterior Adjusted	90.9	90.4	93.5	89.1	86.2	96.0
Interior Background	50.5	41.3	37.6	27.0	19.8	38.9
Interior Measurement	67.2	61.4	59.6	56.7	53.0	62.3
Interior Adjusted	67.1	61.4	59.6	56.7	53.0	62.3
Noise Reduction	23.8	29.0	33.9	32.4	33.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.5	28.1	31.2	34.2	28.6	37.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.4 dB

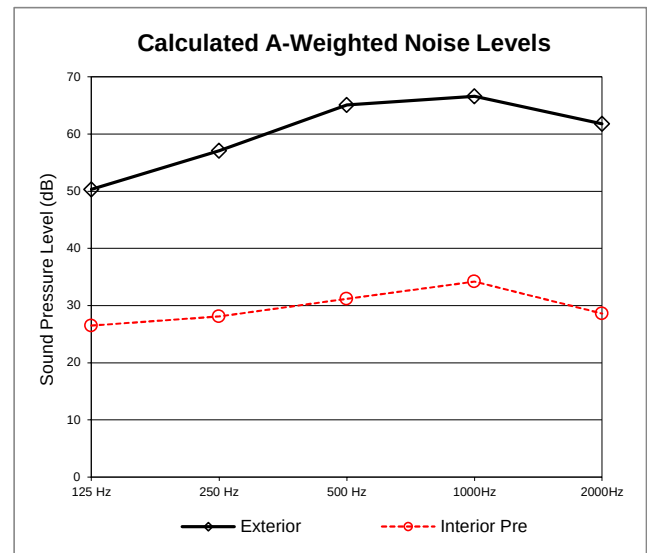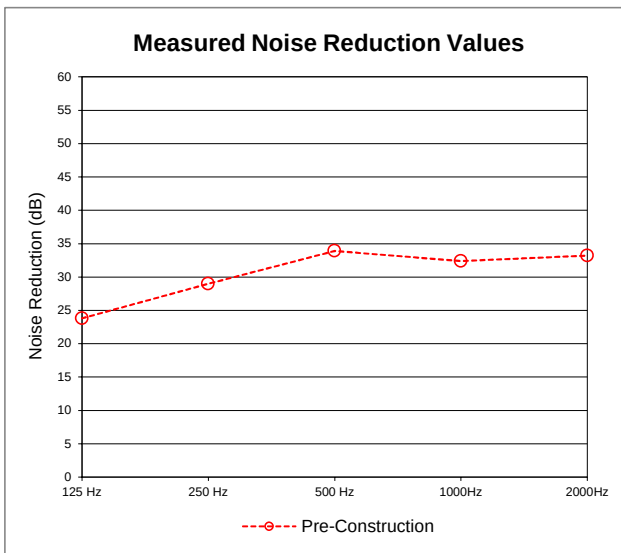



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	52.9	49.1	46.2	46.8	41.4	50.9
Exterior Measurement (flush)	105.9	105.7	102.3	97.7	96.8	105.4
Exterior Adjusted	99.9	99.7	96.3	91.7	90.8	99.4
Interior Background	46.2	42.9	35.3	27.9	24.2	38.1
Interior Measurement	78.5	69.5	60.9	51.9	47.3	65.4
Interior Adjusted	78.5	69.5	60.9	51.9	47.3	65.4
Noise Reduction	21.4	30.2	35.4	39.8	43.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.9	26.9	29.7	26.8	18.3	34.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.6 dB

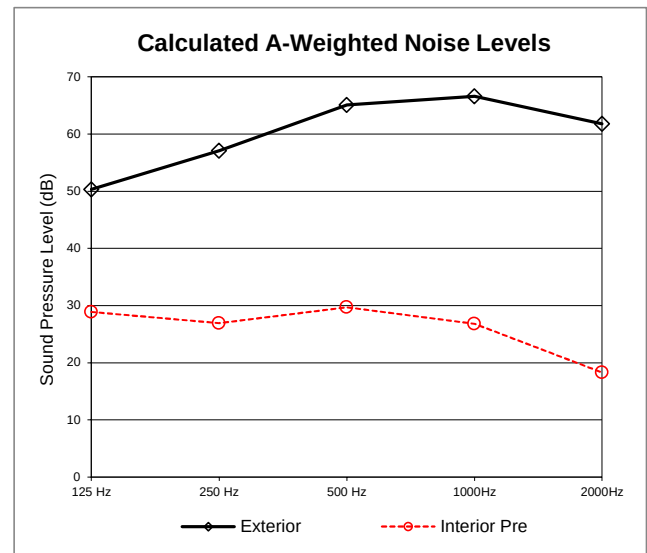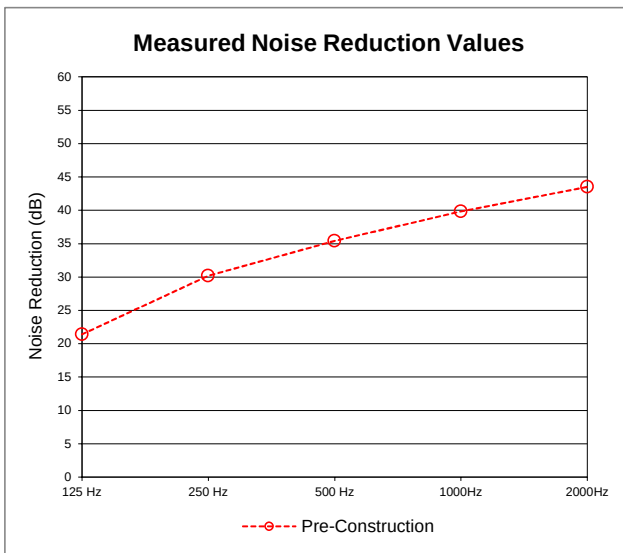



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.0	47.5	48.5	59.0	53.4	61.4
Exterior Measurement (flush)	95.0	94.0	94.8	90.5	88.0	96.8
Exterior Adjusted	89.0	88.0	88.8	84.5	82.0	90.8
Interior Background	41.2	35.8	25.6	20.9	17.3	31.1
Interior Measurement	68.1	62.5	54.5	48.3	39.8	57.7
Interior Adjusted	68.1	62.5	54.5	48.3	39.8	57.7
Noise Reduction	20.9	25.5	34.3	36.2	42.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.4	31.6	30.8	30.4	19.6	36.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.3 dB

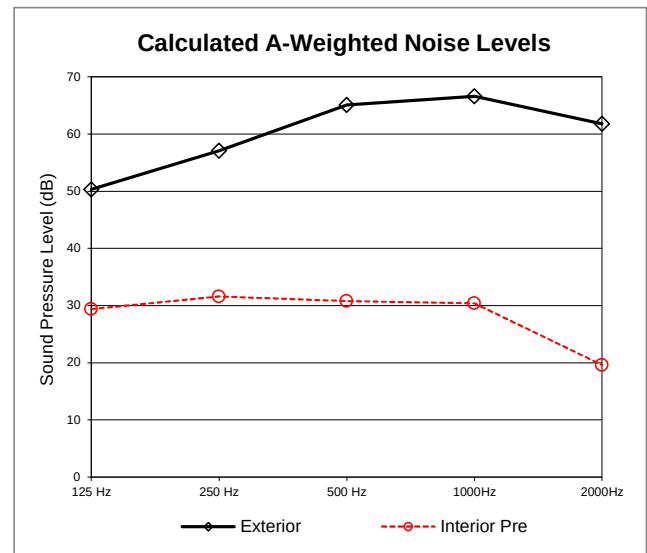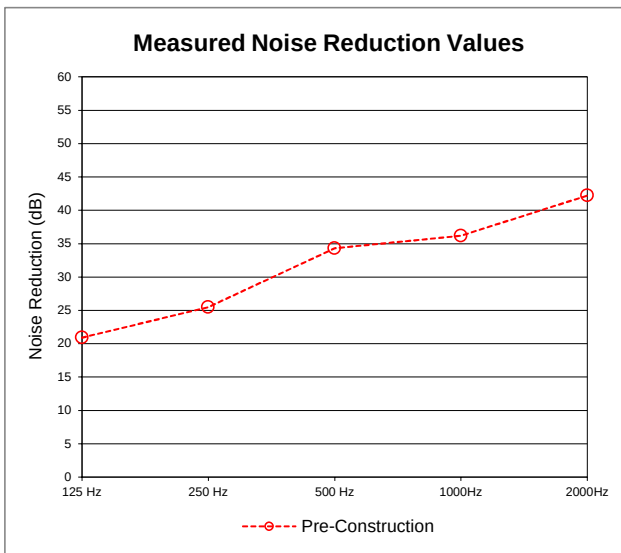

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.7	56.9	53.0	53.5	43.5	56.4
Exterior Measurement (flush)	85.9	87.0	88.3	85.2	83.0	91.3
Exterior Adjusted	79.9	81.0	82.3	79.2	77.0	85.3
Interior Background	41.6	32.0	21.5	21.5	19.9	29.8
Interior Measurement	73.3	66.6	60.0	49.7	43.5	62.3
Interior Adjusted	73.3	66.6	60.0	49.7	43.5	62.3
Noise Reduction	6.6	14.4	22.3	29.5	33.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	43.7	42.7	42.8	37.1	28.3	48.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						21.7 dB

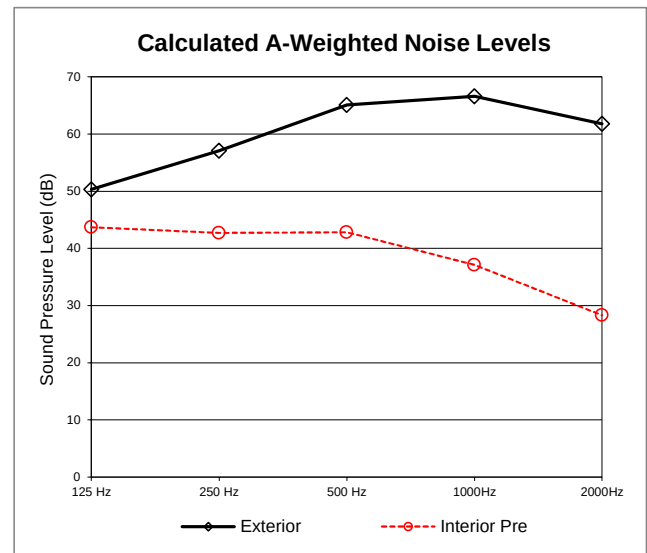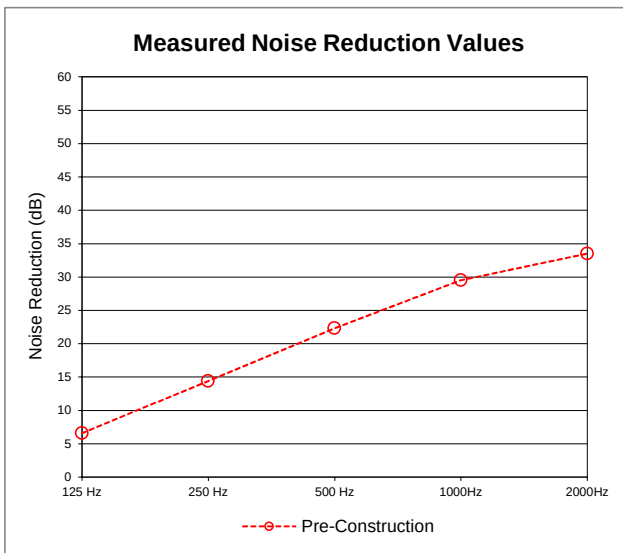



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McDonald
 Address: 21823 14th Ave S
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.7	56.9	53.0	53.5	43.5	56.4
Exterior Measurement (flush)	88.1	88.6	89.0	85.4	82.7	91.3
Exterior Adjusted	82.1	82.6	83.0	79.4	76.7	85.3
Interior Background	49.9	43.7	34.1	27.2	20.6	38.4
Interior Measurement	65.2	58.1	49.5	41.8	36.4	53.6
Interior Adjusted	65.1	57.9	49.4	41.6	36.3	53.5
Noise Reduction	17.0	24.7	33.6	37.8	40.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.3	32.4	31.5	28.8	21.4	37.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.1 dB

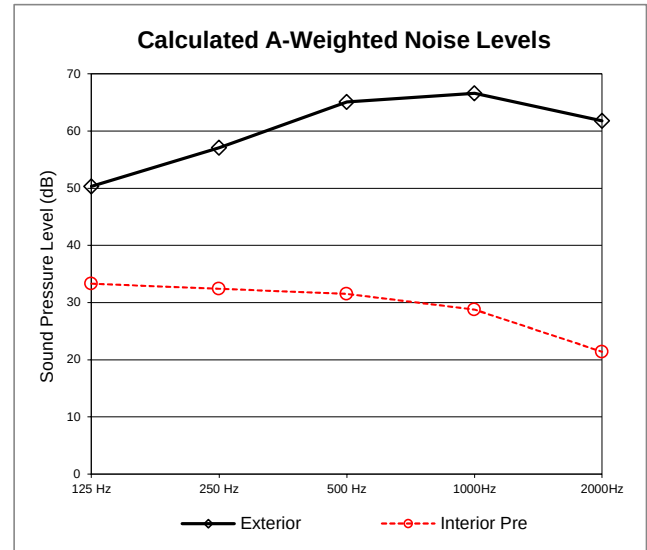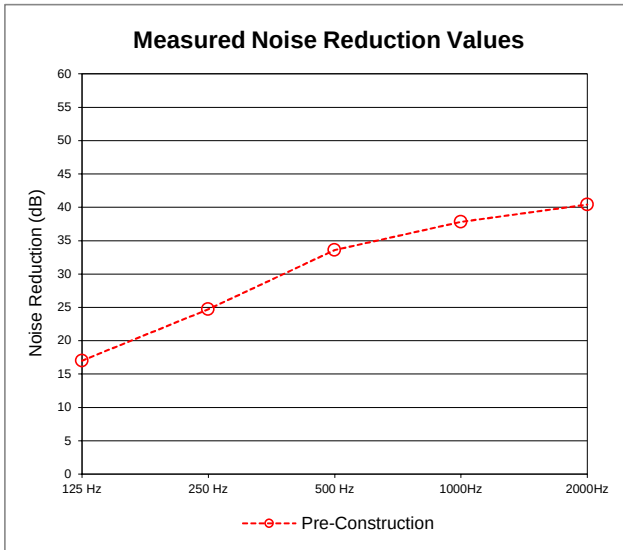

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Living Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.3	57.1	54.2	56.1	48.3	58.5
Exterior Measurement (flush)	108.7	110.1	110.0	105.5	100.1	111.4
Exterior Adjusted	102.7	104.1	104.0	99.5	94.1	105.4
Interior Background	36.2	31.2	24.1	20.4	15.8	27.9
Interior Measurement	75.7	69.0	62.1	49.1	42.4	65.1
Interior Adjusted	75.7	69.0	62.1	49.1	42.4	65.1
Noise Reduction	27.0	35.1	41.9	50.4	51.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	23.3	22.0	23.2	16.2	10.1	28.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						42.0 dB

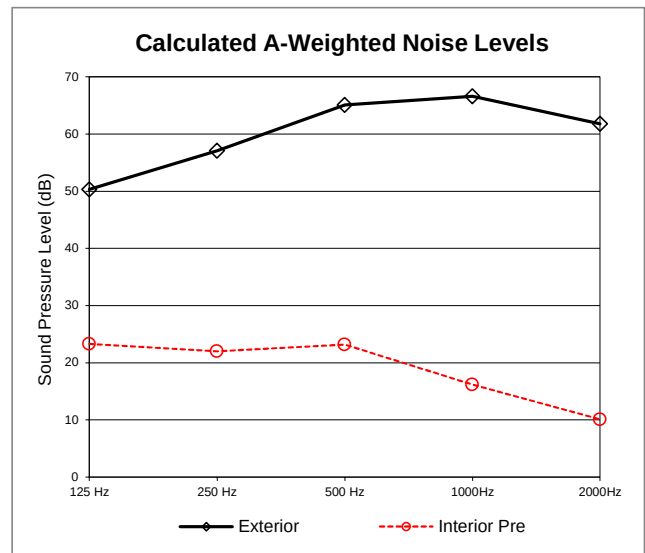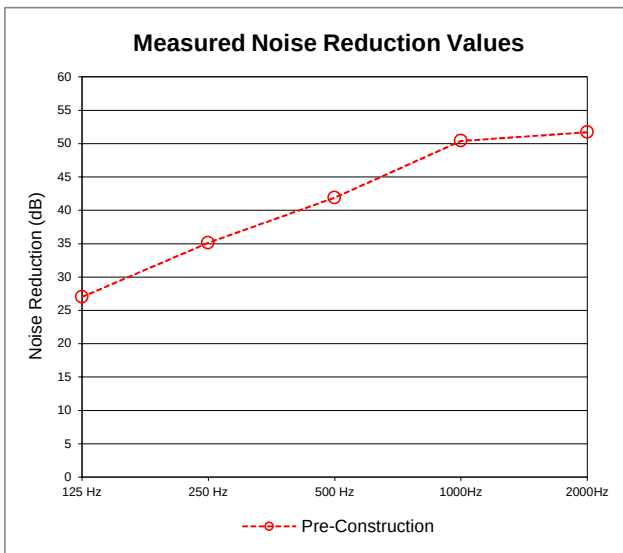



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Living Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.3	57.1	54.2	56.1	48.3	58.5
Exterior Measurement (flush)	100.3	101.7	101.9	98.0	93.5	104.1
Exterior Adjusted	94.3	95.7	95.9	92.0	87.5	98.1
Interior Background	36.2	31.2	24.1	20.4	15.8	27.9
Interior Measurement	73.2	72.6	66.9	55.2	46.2	67.8
Interior Adjusted	73.2	72.6	66.9	55.2	46.2	67.8
Noise Reduction	21.1	23.1	29.0	36.8	41.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.2	34.0	36.1	29.8	20.5	39.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.7 dB

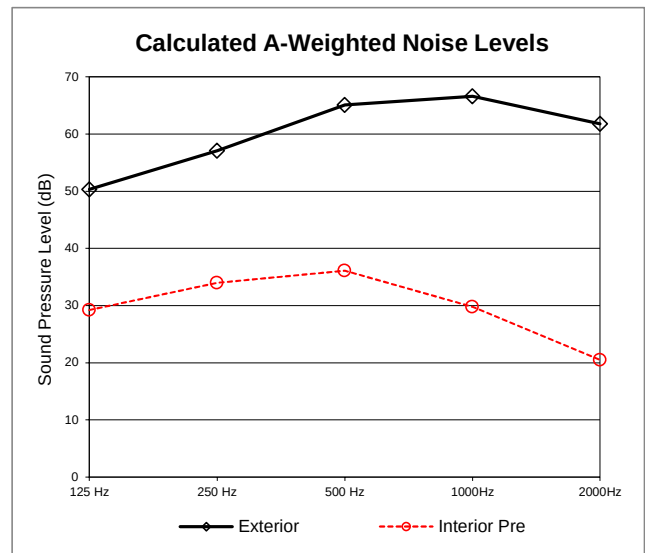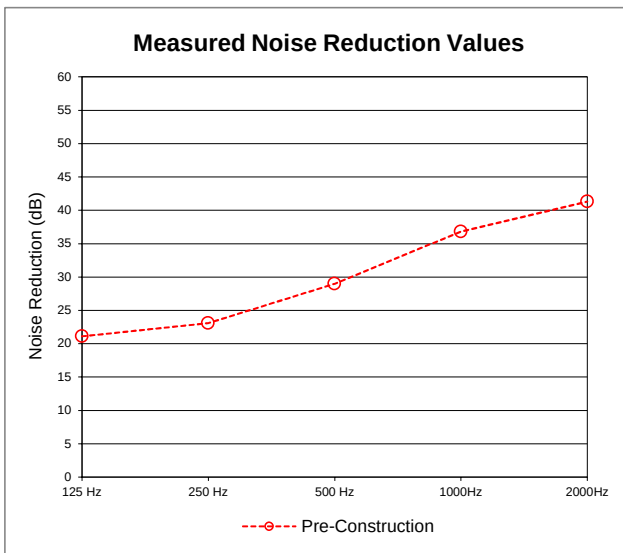

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.9	56.1	52.5	51.9	48.1	56.5
Exterior Measurement (flush)	83.2	87.4	89.0	86.3	83.9	91.6
Exterior Adjusted	77.2	81.4	83.0	80.3	77.9	85.6
Interior Background	34.1	31.2	27.1	25.1	22.1	31.0
Interior Measurement	60.9	58.4	56.4	52.4	49.3	58.6
Interior Adjusted	60.9	58.4	56.4	52.4	49.3	58.6
Noise Reduction	16.3	23.0	26.6	27.9	28.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.0	34.1	38.5	38.7	33.2	43.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						26.6 dB

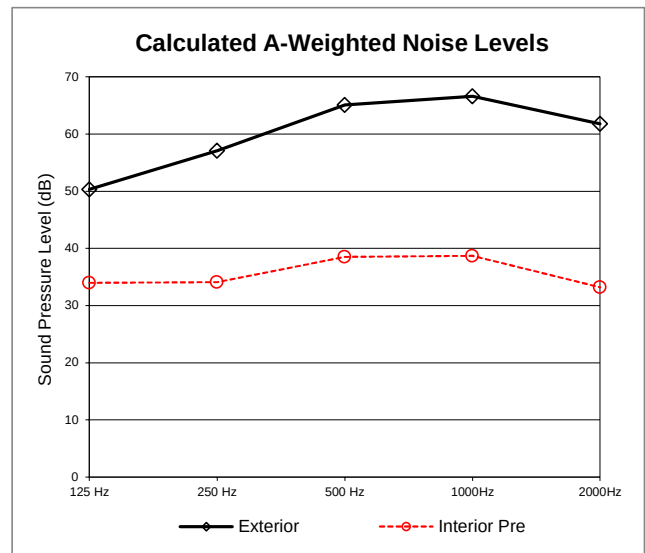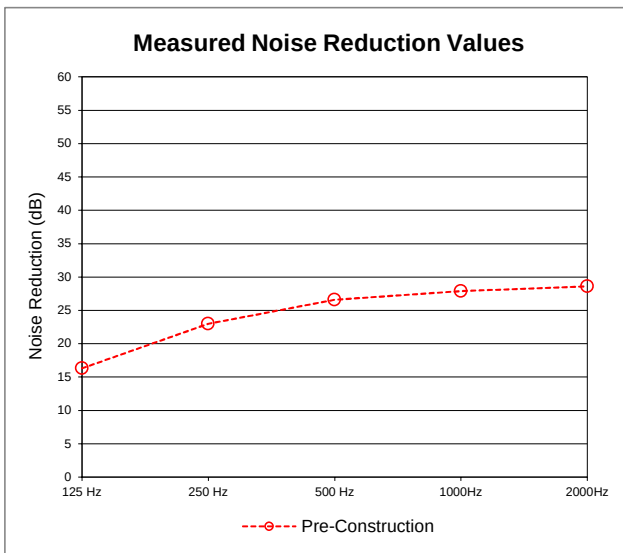



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Kitchenette Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.5	57.1	57.8	56.4	50.0	59.9
Exterior Measurement (flush)	94.2	95.4	94.5	92.2	88.9	97.5
Exterior Adjusted	88.2	89.4	88.5	86.2	82.9	91.5
Interior Background	38.3	32.2	30.4	27.8	24.3	33.5
Interior Measurement	67.2	64.6	64.4	61.8	61.6	68.5
Interior Adjusted	67.2	64.6	64.4	61.8	61.6	68.5
Noise Reduction	21.0	24.8	24.1	24.4	21.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.3	32.3	41.0	42.2	40.5	46.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						23.7 dB

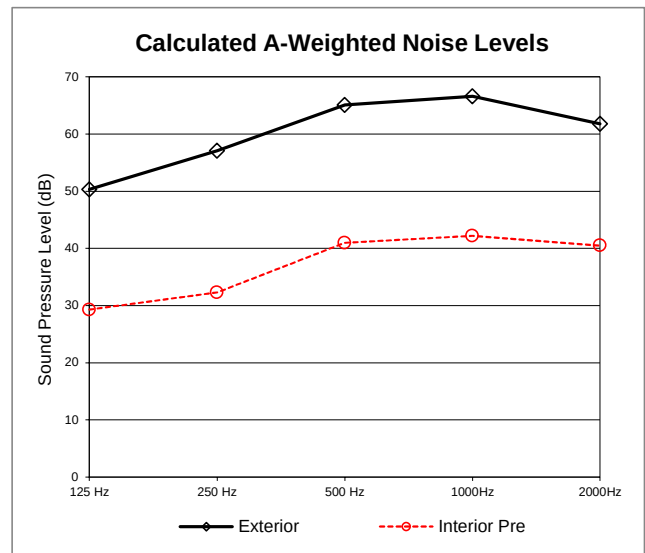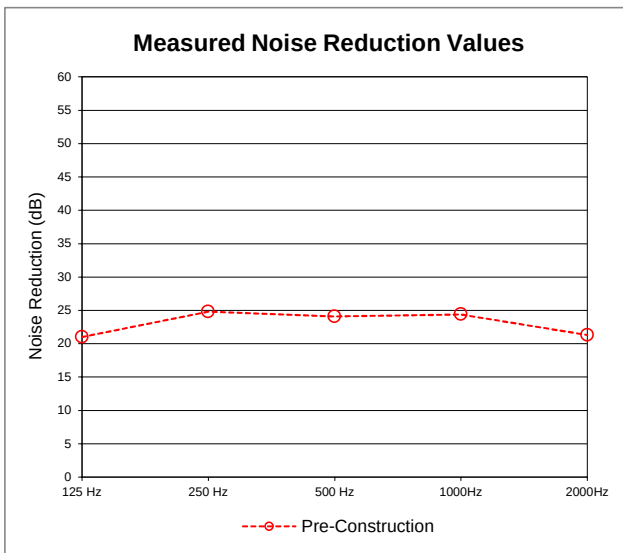

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.9	57.5	54.8	52.6	53.0	59.0
Exterior Measurement (flush)	94.0	93.5	94.7	91.2	88.6	96.8
Exterior Adjusted	88.0	87.5	88.7	85.2	82.6	90.8
Interior Background	34.3	27.6	22.1	16.1	14.3	26.2
Interior Measurement	65.3	64.3	59.0	47.6	41.6	59.4
Interior Adjusted	65.3	64.3	59.0	47.6	41.6	59.4
Noise Reduction	22.7	23.2	29.7	37.6	41.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.6	33.9	35.4	29.0	20.8	38.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.3 dB

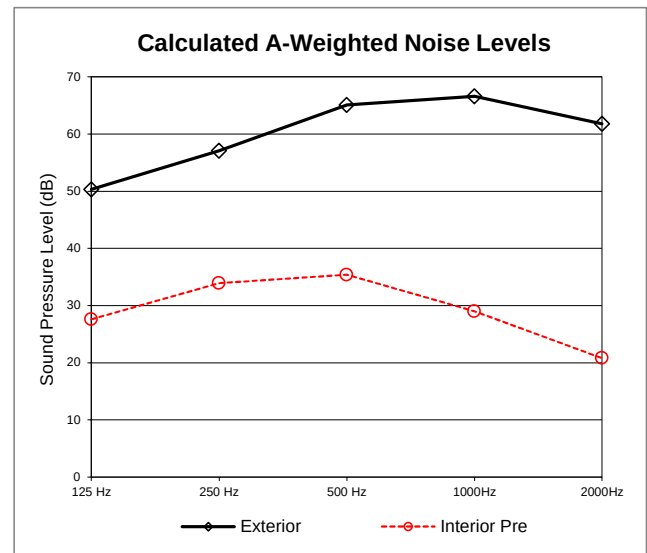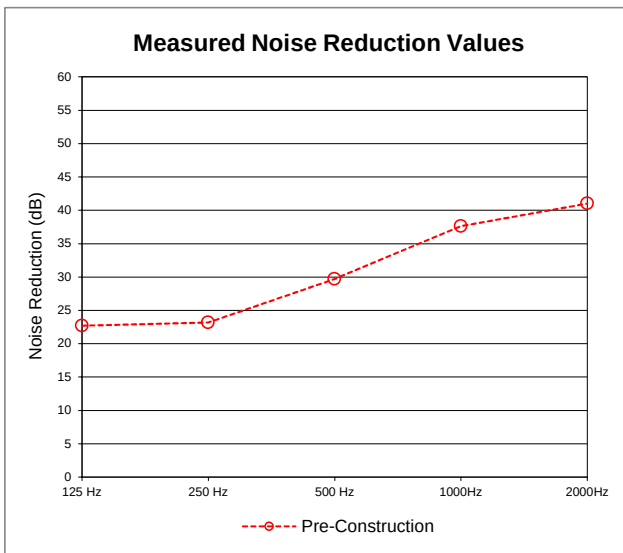

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.2	59.8	57.4	57.1	51.4	60.7
Exterior Measurement (flush)	92.5	92.2	92.6	86.0	82.2	92.9
Exterior Adjusted	86.5	86.2	86.6	80.0	76.2	86.9
Interior Background	34.2	31.4	26.1	21.1	19.2	29.3
Interior Measurement	67.5	61.5	56.1	41.3	29.4	57.1
Interior Adjusted	67.5	61.5	56.1	41.3	29.0	57.1
Noise Reduction	19.0	24.7	30.5	38.7	47.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.3	32.4	34.6	27.9	14.6	38.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.8 dB

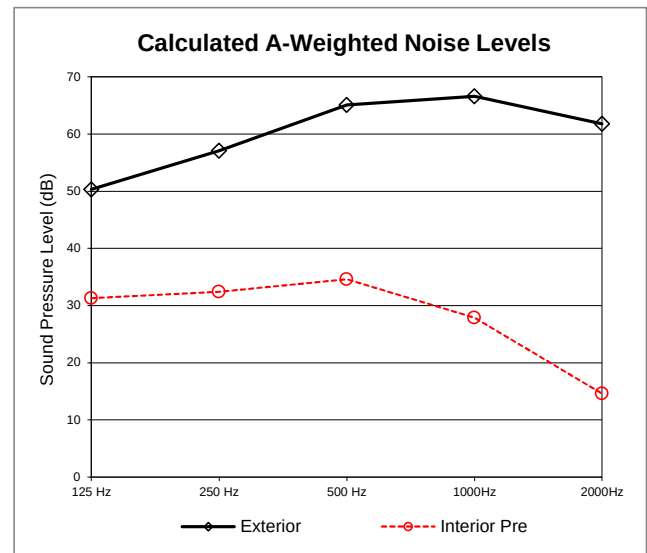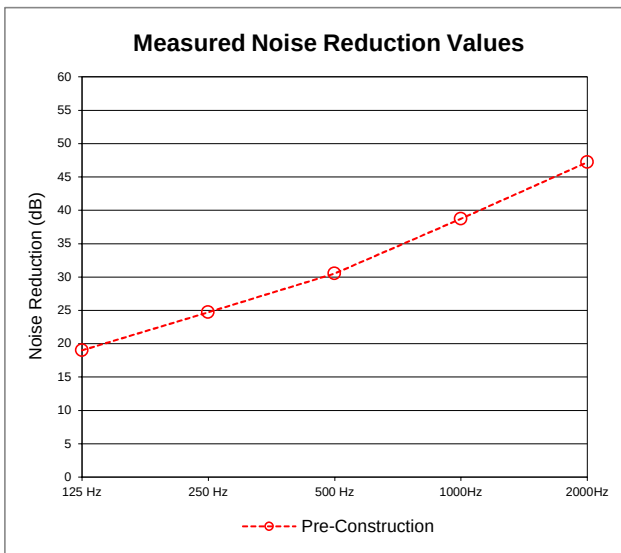

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Bedroom 3 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 0 of 2

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	52.6	54.2	52.4	53.6	47.7	56.8
Exterior Measurement (flush)	99.4	101.5	102.4	98.9	95.6	104.9
Exterior Adjusted	93.4	95.5	96.4	92.9	89.6	98.9
Interior Background	36.3	30.6	25.3	26.5	26.4	33.0
Interior Measurement	72.2	67.2	64.4	54.0	48.2	64.3
Interior Adjusted	72.2	67.2	64.4	54.0	48.2	64.3
Noise Reduction	21.2	28.3	32.0	38.9	41.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.1	28.8	33.1	27.7	20.4	36.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.7 dB

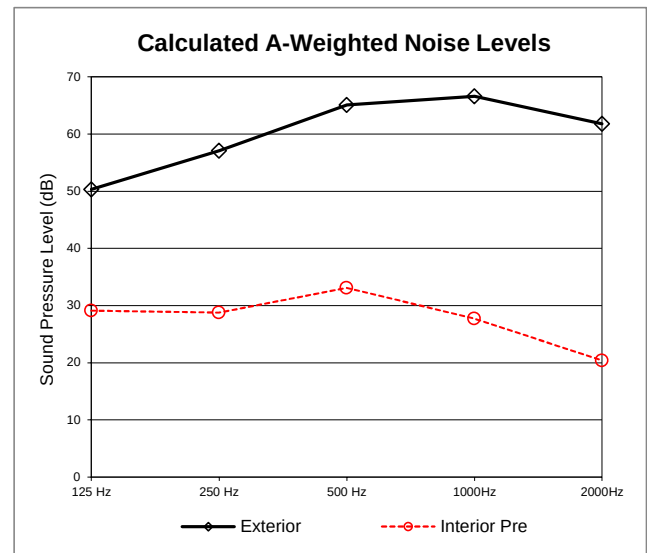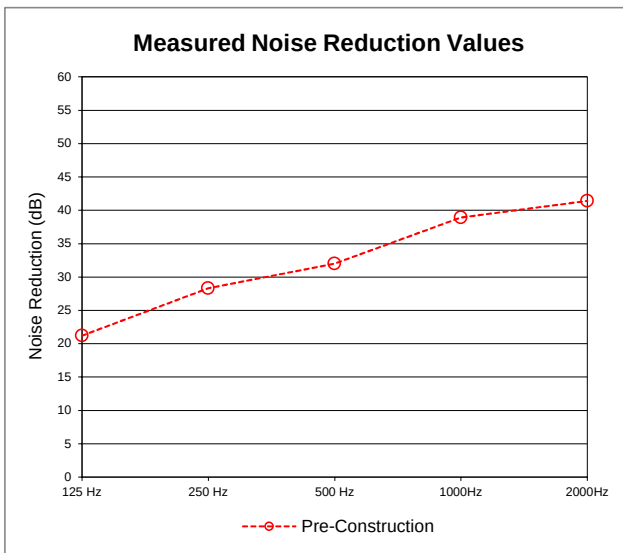

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Bedroom 3 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 0 of 2

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	52.6	54.2	52.4	53.6	47.7	56.8
Exterior Measurement (flush)	101.8	98.6	100.6	96.2	91.9	102.6
Exterior Adjusted	95.8	92.6	94.6	90.2	85.9	96.6
Interior Background	36.3	30.6	25.3	26.5	26.4	33.0
Interior Measurement	77.2	71.2	66.1	59.1	56.6	68.0
Interior Adjusted	77.2	71.2	66.1	59.1	56.6	68.0
Noise Reduction	18.6	21.4	28.5	31.1	29.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.7	35.7	36.6	35.5	32.5	41.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.2 dB

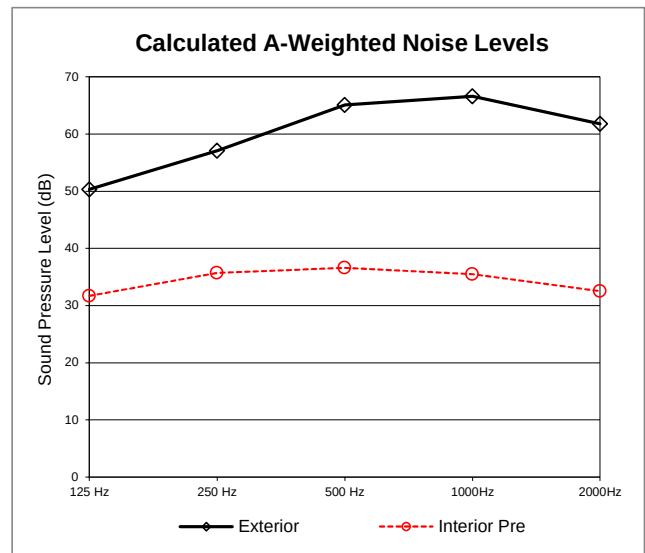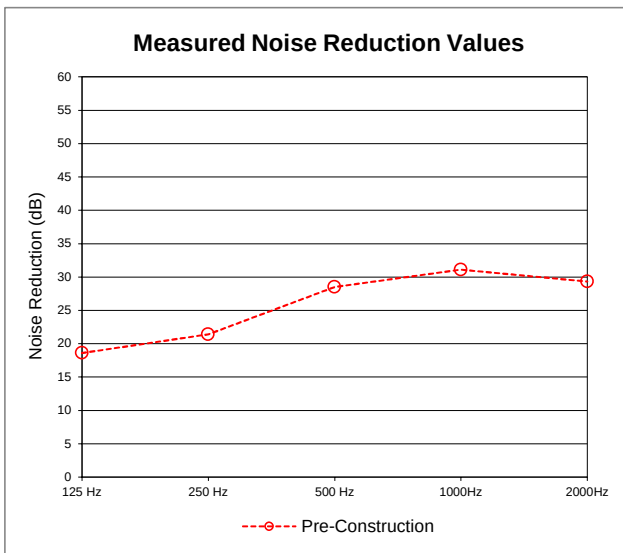



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zuluaga
 Address: 10106 16th Ave S
 Local City: Seattle

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.0	53.0	52.3	52.1	49.2	57.2
Exterior Measurement (flush)	93.0	92.3	92.8	88.1	83.6	94.0
Exterior Adjusted	87.0	86.3	86.8	82.1	77.6	88.0
Interior Background	39.4	34.3	27.5	20.7	16.0	30.2
Interior Measurement	65.8	60.5	57.1	43.2	32.5	56.9
Interior Adjusted	65.8	60.5	57.1	43.2	32.4	56.9
Noise Reduction	21.2	25.8	29.7	38.9	45.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.1	31.3	35.4	27.7	16.6	38.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.0 dB

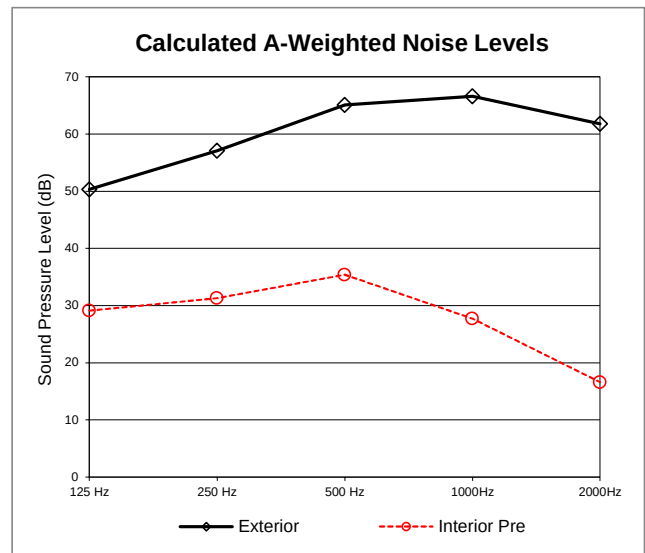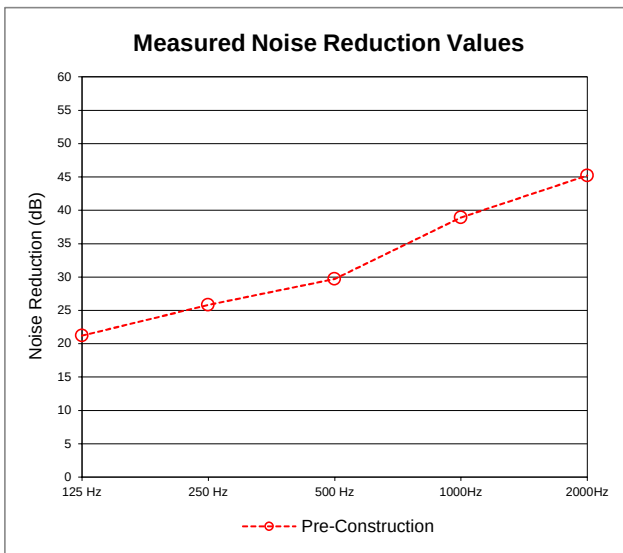



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.0	53.8	51.6	48.0	41.5	53.2
Exterior Measurement (flush)	95.7	95.5	95.0	93.6	91.4	99.5
Exterior Adjusted	89.7	89.5	89.0	87.6	85.4	93.5
Interior Background	41.9	37.4	32.4	27.4	23.2	34.5
Interior Measurement	71.3	70.6	61.2	54.0	46.6	64.4
Interior Adjusted	71.3	70.6	61.2	54.0	46.6	64.4
Noise Reduction	18.4	18.9	27.8	33.6	38.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.9	38.2	37.3	33.0	23.0	42.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.0 dB

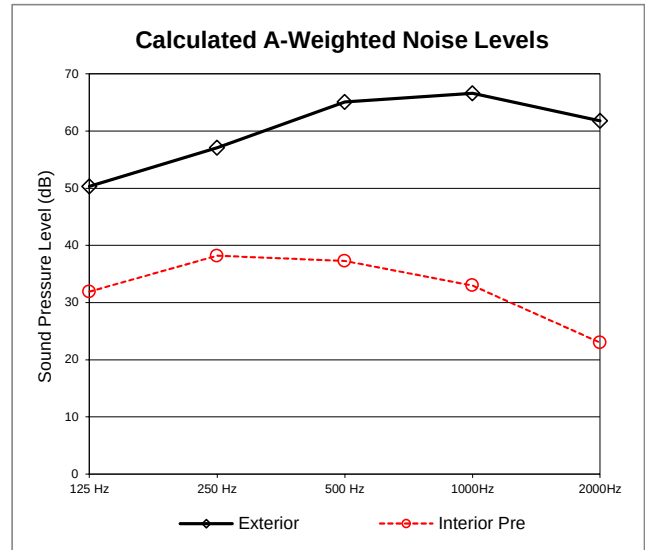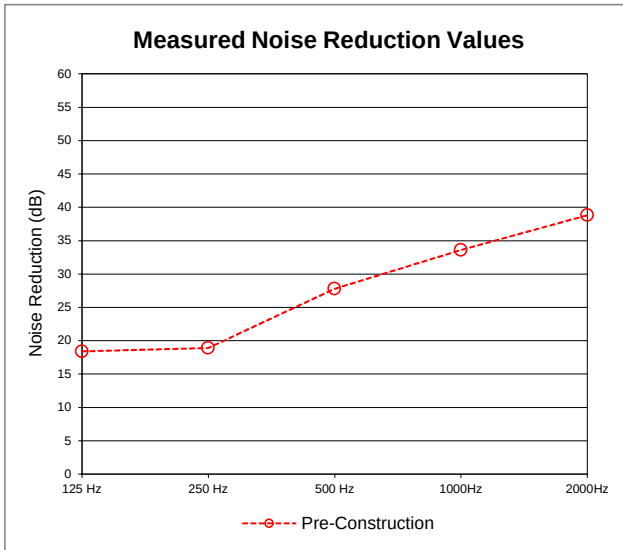



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.3	54.1	49.7	47.8	40.3	52.9
Exterior Measurement (flush)	90.4	91.4	93.7	90.5	89.1	96.8
Exterior Adjusted	84.4	85.4	87.7	84.5	83.1	90.8
Interior Background	35.7	26.8	17.3	13.8	16.1	25.5
Interior Measurement	64.2	58.0	52.4	48.8	46.1	56.0
Interior Adjusted	64.2	58.0	52.4	48.8	46.1	56.0
Noise Reduction	20.2	27.4	35.3	35.7	37.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.1	29.7	29.8	30.9	24.8	36.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.5 dB

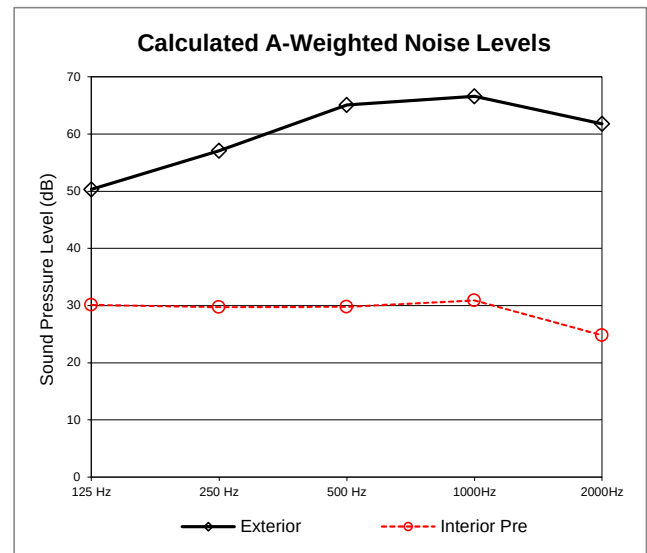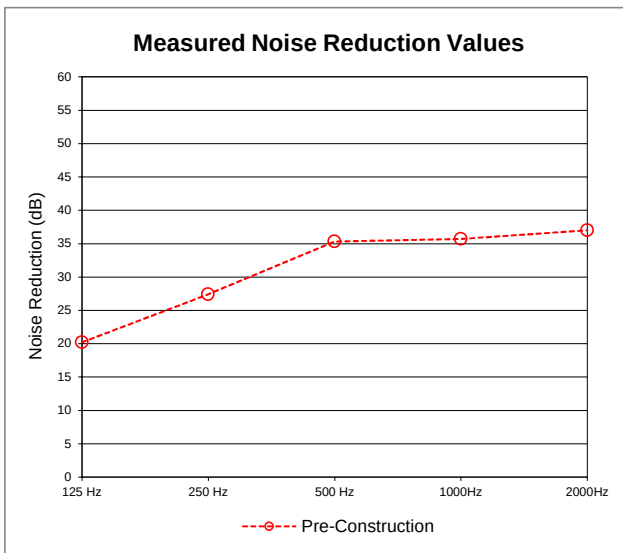

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.1	52.2	49.4	46.1	40.0	51.1
Exterior Measurement (flush)	89.2	85.7	90.0	85.6	82.7	91.4
Exterior Adjusted	83.2	79.7	84.0	79.6	76.7	85.4
Interior Background	39.1	39.6	38.6	31.8	25.1	38.2
Interior Measurement	63.6	51.8	51.5	43.9	39.0	52.6
Interior Adjusted	63.6	51.5	51.3	43.6	38.8	52.4
Noise Reduction	19.6	28.2	32.7	36.0	37.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.7	28.9	32.4	30.6	23.9	37.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.9 dB

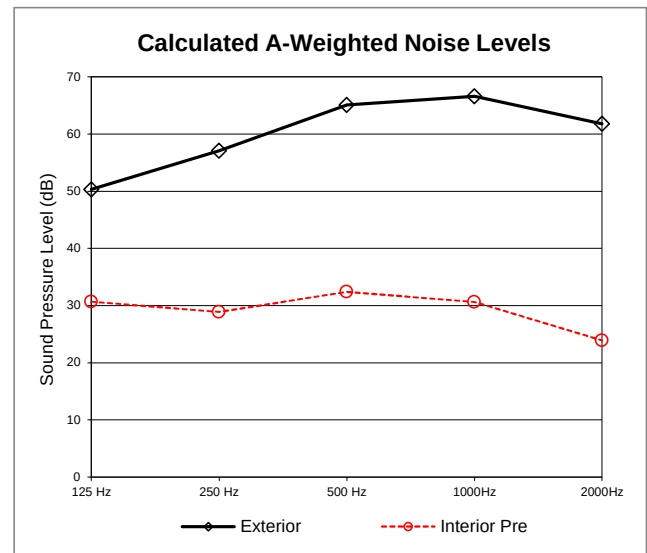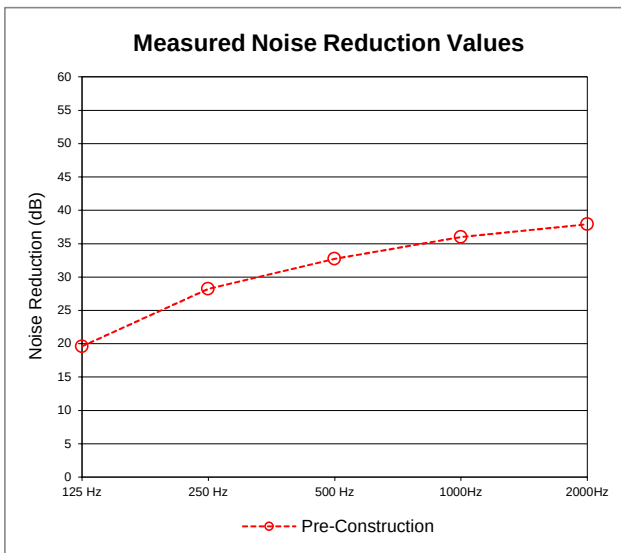



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.1	52.2	49.4	46.1	40.0	51.1
Exterior Measurement (flush)	93.6	90.2	91.3	86.7	80.7	92.0
Exterior Adjusted	87.6	84.2	85.3	80.7	74.7	86.0
Interior Background	39.6	34.3	23.4	18.4	16.4	29.4
Interior Measurement	64.6	51.5	48.2	40.7	36.2	51.9
Interior Adjusted	64.6	51.4	48.2	40.7	36.2	51.9
Noise Reduction	23.0	32.8	37.1	40.0	38.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.3	24.3	28.0	26.6	23.3	33.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.8 dB

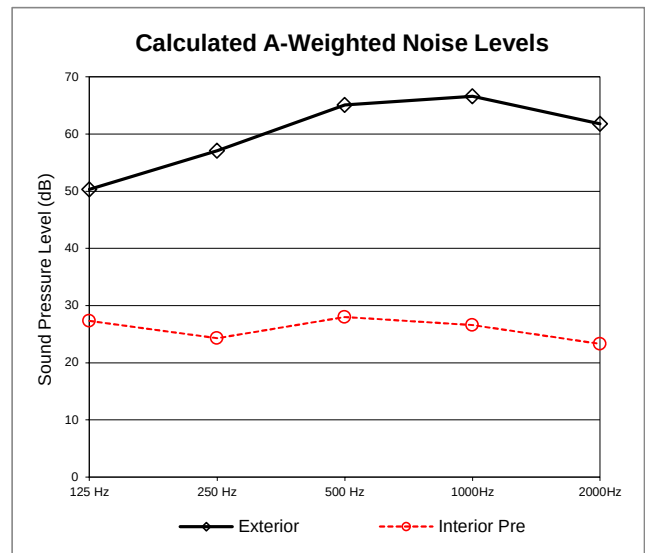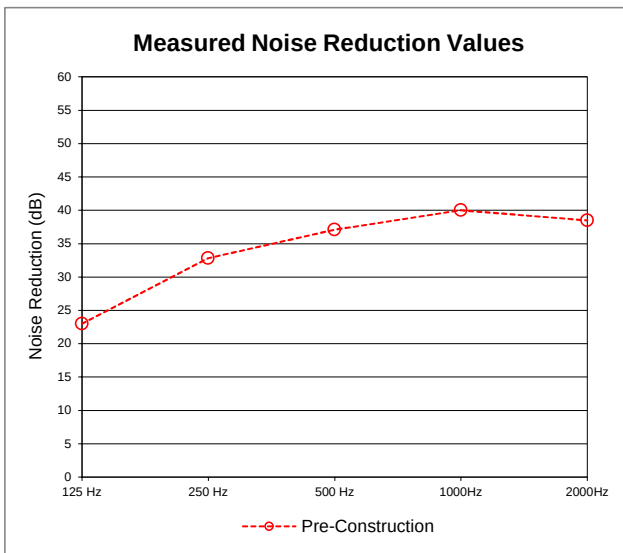

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.0	53.8	51.6	48.0	41.5	53.2
Exterior Measurement (flush)	93.2	90.0	91.2	89.1	84.6	94.2
Exterior Adjusted	87.2	84.0	85.2	83.1	78.6	88.2
Interior Background	36.3	30.5	26.9	23.4	22.2	30.4
Interior Measurement	66.1	58.4	52.8	43.7	36.9	55.1
Interior Adjusted	66.1	58.4	52.8	43.7	36.8	55.1
Noise Reduction	21.1	25.6	32.4	39.4	41.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.2	31.5	32.7	27.2	20.0	36.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.3 dB

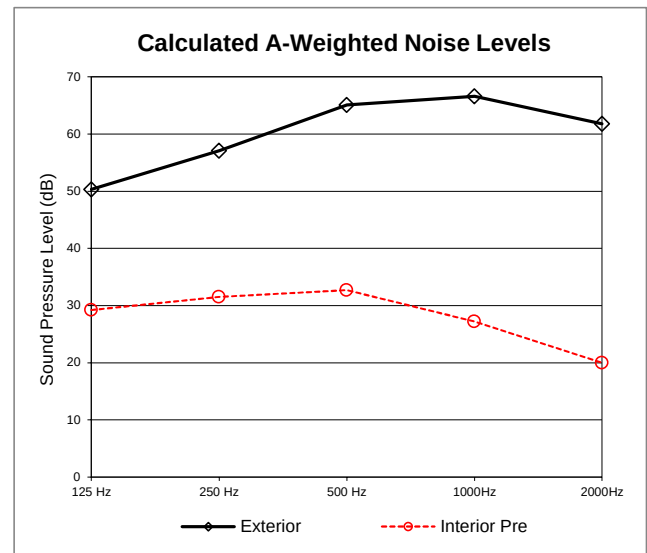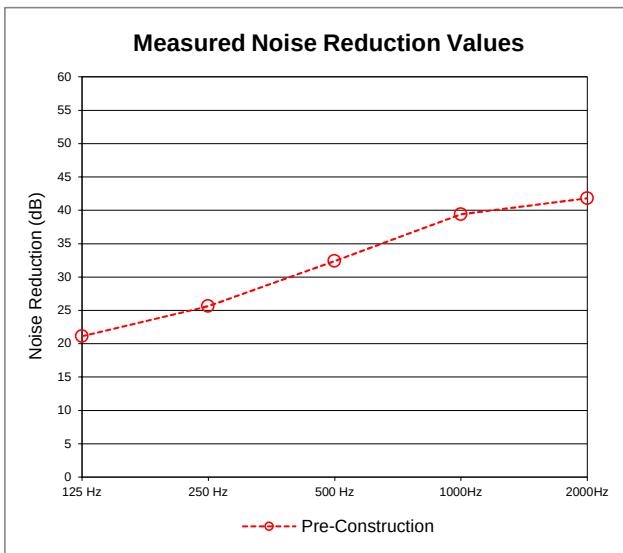



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.0	53.8	51.6	48.0	41.5	53.2
Exterior Measurement (flush)	94.3	92.5	94.8	92.2	88.4	97.7
Exterior Adjusted	88.3	86.5	88.8	86.2	82.4	91.7
Interior Background	40.5	34.3	28.9	20.2	15.8	30.9
Interior Measurement	67.6	58.8	53.8	47.0	39.1	56.1
Interior Adjusted	67.6	58.8	53.8	47.0	39.1	56.1
Noise Reduction	20.7	27.7	35.0	39.2	43.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.6	29.4	30.1	27.4	18.5	35.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.7 dB

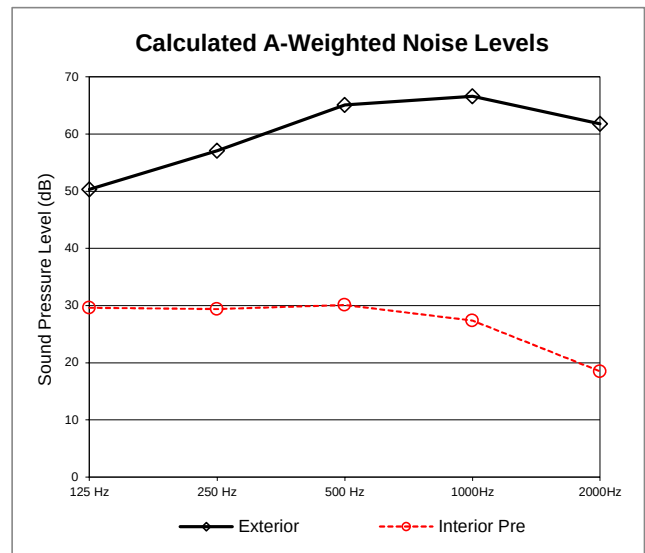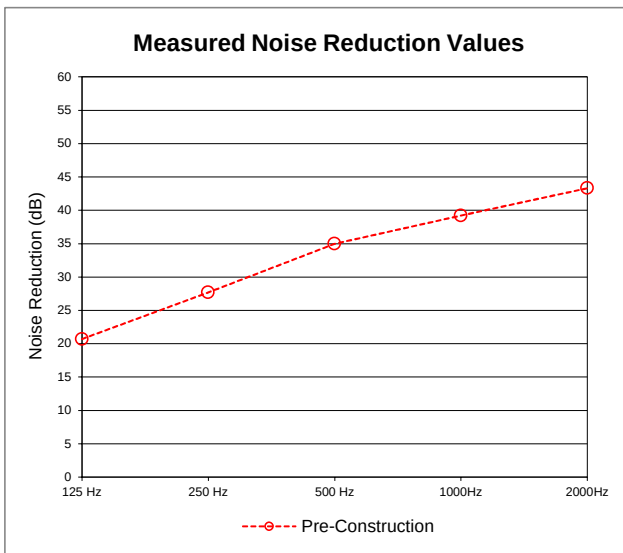

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	51.5	47.8	44.0	44.9	39.3	49.0
Exterior Measurement (flush)	91.8	92.5	94.6	90.9	86.9	96.4
Exterior Adjusted	85.8	86.5	88.6	84.9	80.9	90.4
Interior Background	31.4	28.2	24.8	18.0	16.2	26.6
Interior Measurement	63.8	54.1	49.5	39.3	34.5	51.8
Interior Adjusted	63.8	54.1	49.5	39.3	34.4	51.8
Noise Reduction	22.0	32.4	39.1	45.6	46.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.3	24.7	26.0	21.0	15.3	31.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						38.2 dB

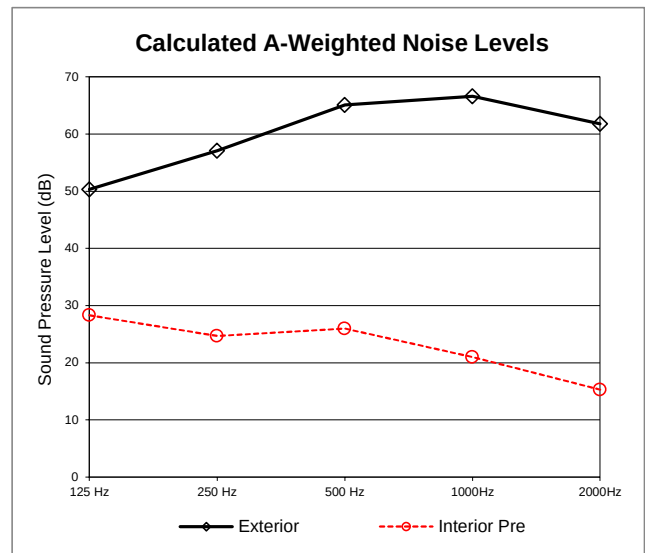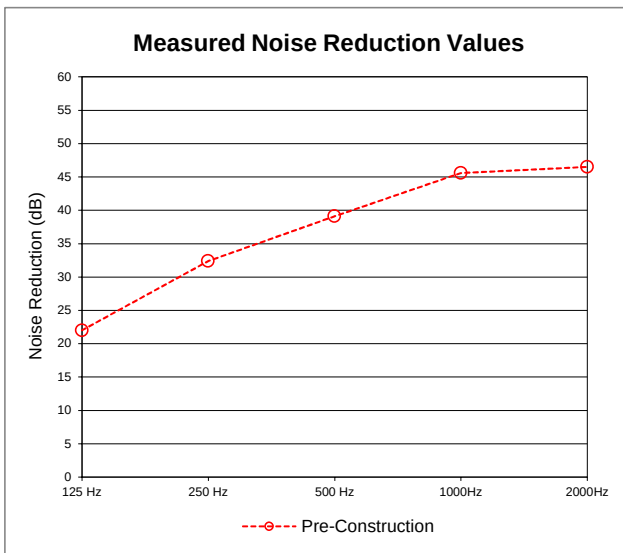



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gauthier
 Address: 22459 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 5 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.6	59.4	58.0	53.0	44.5	58.3
Exterior Measurement (flush)	105.9	105.7	106.6	101.1	97.2	107.1
Exterior Adjusted	99.9	99.7	100.6	95.1	91.2	101.1
Interior Background	36.6	25.2	15.7	10.7	11.5	24.1
Interior Measurement	72.1	61.0	53.2	44.0	36.1	58.1
Interior Adjusted	72.1	61.0	53.2	44.0	36.1	58.1
Noise Reduction	27.8	38.7	47.4	51.1	55.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	22.5	18.4	17.7	15.5	6.7	25.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						44.6 dB

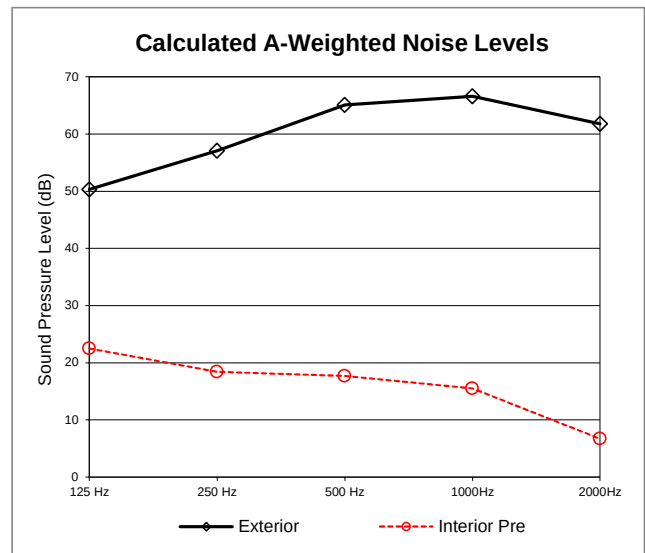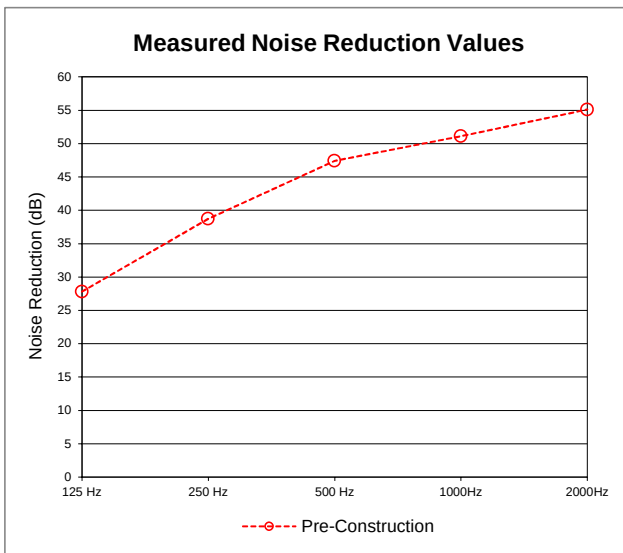

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.0	53.1	49.3	45.7	33.1	51.3
Exterior Measurement (flush)	84.7	90.0	90.1	86.5	84.5	93.0
Exterior Adjusted	78.7	84.0	84.1	80.5	78.5	87.0
Interior Background	38.7	35.8	28.4	22.3	20.0	31.8
Interior Measurement	60.1	56.8	51.4	42.6	35.0	52.5
Interior Adjusted (roof)	61.1	57.8	52.4	43.6	35.9	53.5
Noise Reduction	17.6	26.2	31.7	36.9	42.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.7	30.9	33.4	29.7	19.2	38.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.0 dB

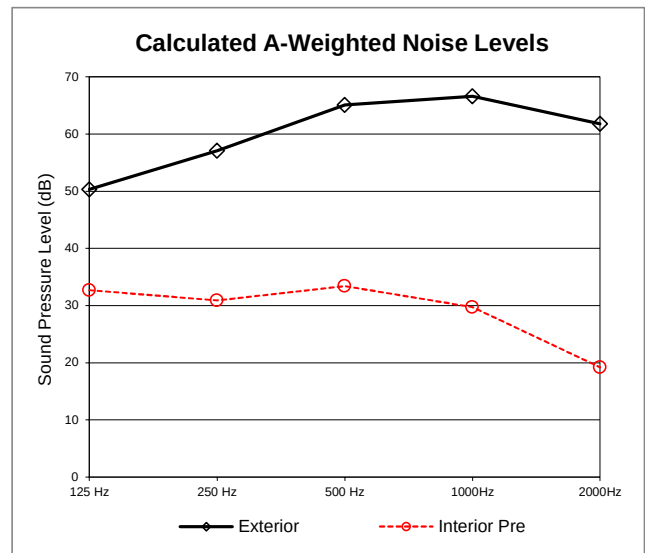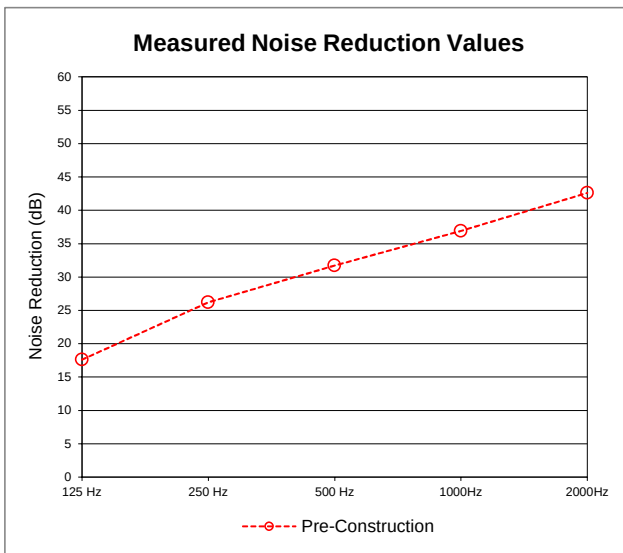

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	68.3	59.0	55.6	56.1	50.7	59.9
Exterior Measurement (flush)	91.5	89.9	91.7	88.1	86.2	94.9
Exterior Adjusted	85.5	83.9	85.7	82.1	80.2	88.9
Interior Background	34.4	27.8	13.6	12.7	10.7	24.0
Interior Measurement	63.8	55.5	51.2	42.8	35.4	52.5
Interior Adjusted	63.8	55.5	51.2	42.8	35.4	52.5
Noise Reduction	21.7	28.4	34.5	39.3	44.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.6	28.7	30.6	27.3	17.0	35.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.9 dB

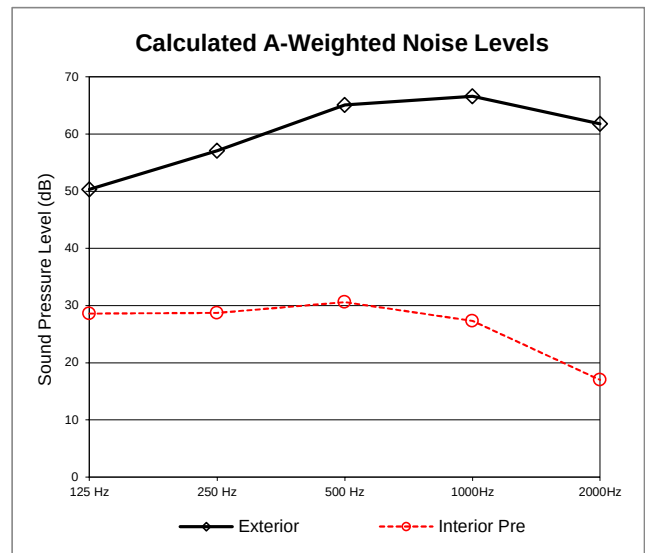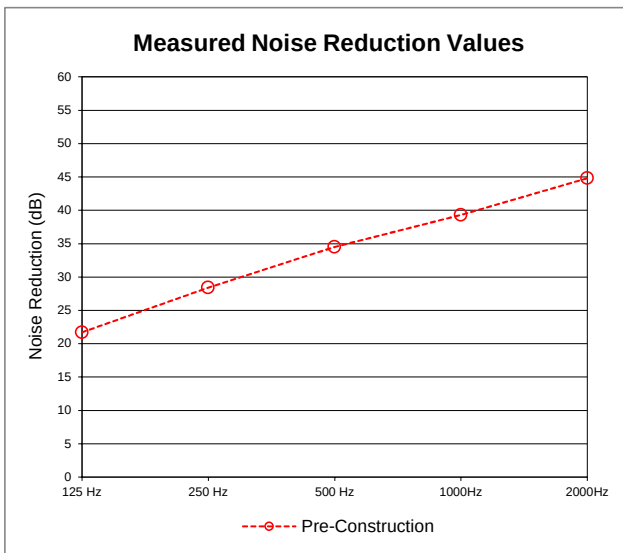



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.0	53.1	49.3	45.7	33.1	51.3
Exterior Measurement (flush)	90.9	87.6	90.8	88.8	87.5	95.8
Exterior Adjusted	84.9	81.6	84.8	82.8	81.5	89.8
Interior Background	34.4	27.8	13.6	12.7	10.7	24.0
Interior Measurement	65.8	56.2	51.8	43.5	38.1	54.0
Interior Adjusted	65.8	56.2	51.8	43.5	38.1	54.0
Noise Reduction	19.1	25.4	33.0	39.3	43.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.2	31.7	32.1	27.3	18.4	37.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.0 dB

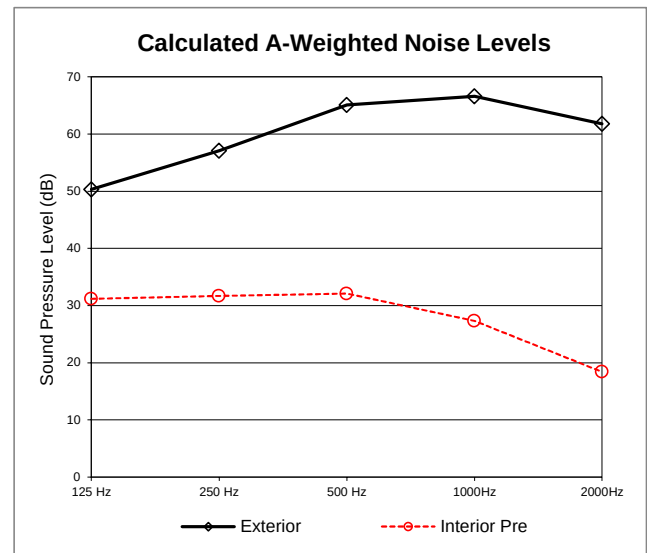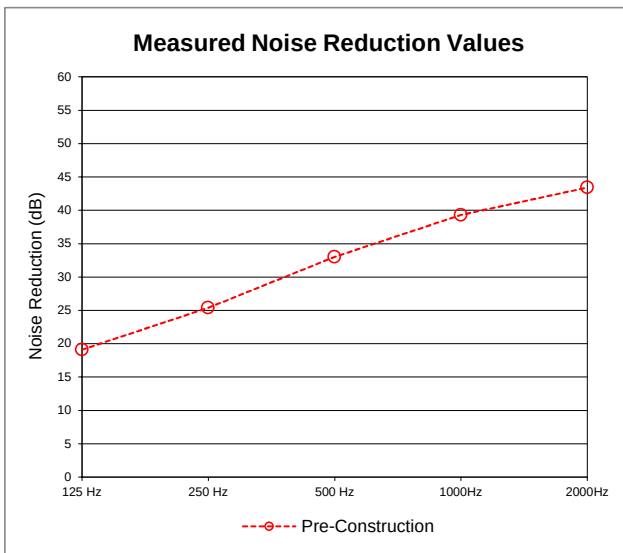

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	68.3	59.0	55.6	56.1	50.7	59.9
Exterior Measurement (flush)	93.2	92.9	94.4	90.8	87.0	96.7
Exterior Adjusted	87.2	86.9	88.4	84.8	81.0	90.7
Interior Background	40.0	36.6	31.3	26.0	19.3	33.1
Interior Measurement	68.1	61.9	56.9	49.1	40.6	58.2
Interior Adjusted (roof)	69.1	62.9	57.9	50.1	41.6	59.2
Noise Reduction	18.1	24.0	30.5	34.7	39.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.2	33.1	34.6	31.9	22.4	39.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.8 dB

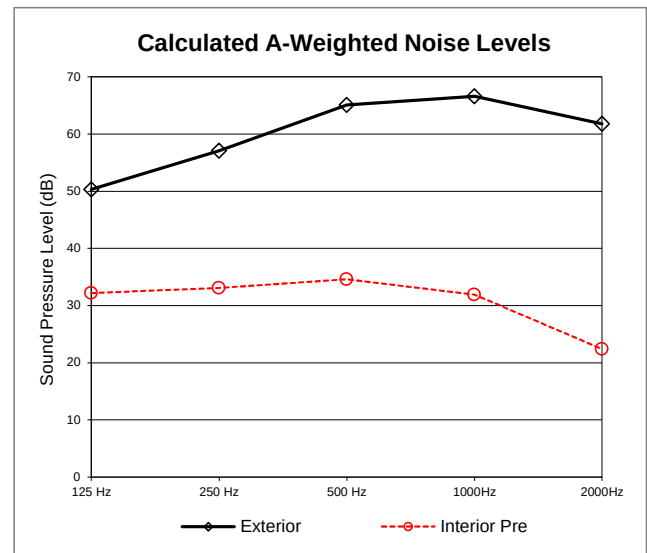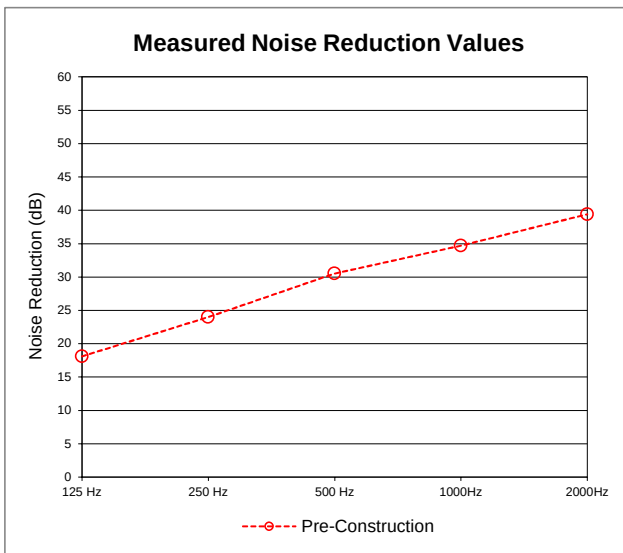



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.0	53.1	49.3	45.7	33.1	51.3
Exterior Measurement (flush)	84.2	89.1	87.9	85.4	82.7	92.1
Exterior Adjusted	78.2	83.1	81.9	79.4	76.7	86.1
Interior Background	40.0	36.6	31.3	26.0	19.3	33.1
Interior Measurement	60.6	57.3	52.1	43.8	35.3	53.1
Interior Adjusted (roof)	61.6	58.3	53.1	44.7	36.2	54.1
Noise Reduction	16.6	24.8	28.8	34.7	40.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.7	32.3	36.3	31.9	21.3	40.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.0 dB

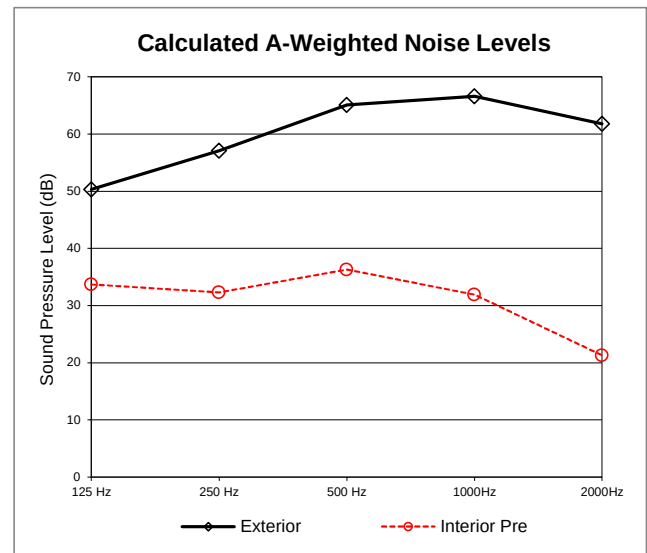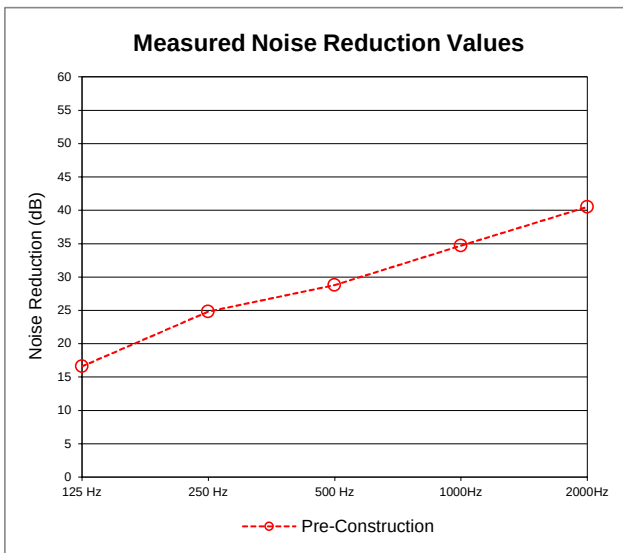



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.0	50.8	49.3	43.4	36.1	49.6
Exterior Measurement (flush)	93.6	97.1	96.7	92.1	88.8	99.0
Exterior Adjusted	87.6	91.1	90.7	86.1	82.8	93.0
Interior Background	29.4	19.6	10.2	9.9	12.6	21.4
Interior Measurement	63.7	58.0	50.3	40.3	34.7	53.1
Interior Adjusted (roof)	64.7	59.0	51.3	41.3	35.7	54.1
Noise Reduction	22.9	32.1	39.4	44.8	47.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.4	25.0	25.7	21.8	14.7	31.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						38.5 dB

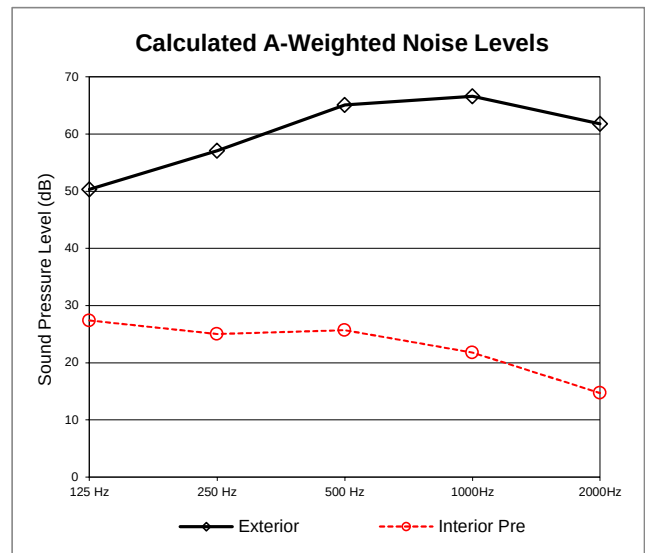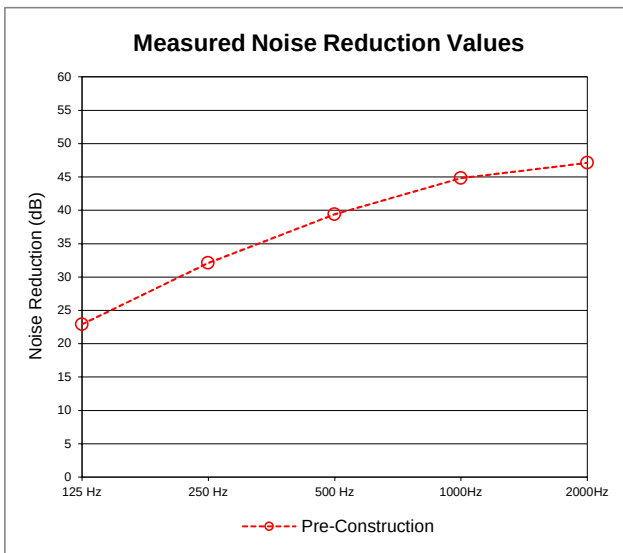

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.8	52.1	49.8	47.3	33.7	51.5
Exterior Measurement (flush)	91.1	89.9	91.9	88.1	85.6	95.1
Exterior Adjusted	85.1	83.9	85.9	82.1	79.6	89.1
Interior Background	38.0	29.2	21.1	15.3	13.2	26.4
Interior Measurement	67.0	60.6	53.5	44.3	39.5	56.1
Interior Adjusted (roof)	68.0	61.6	54.5	45.3	40.5	57.1
Noise Reduction	17.1	22.3	31.4	36.8	39.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.2	34.8	33.7	29.8	22.7	39.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.7 dB

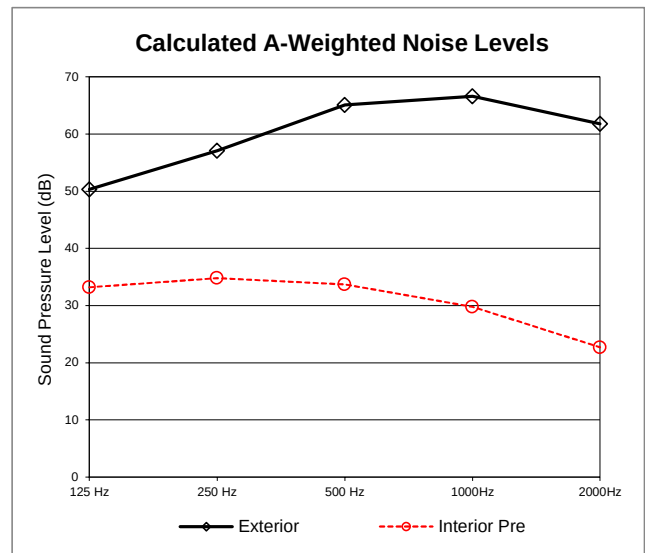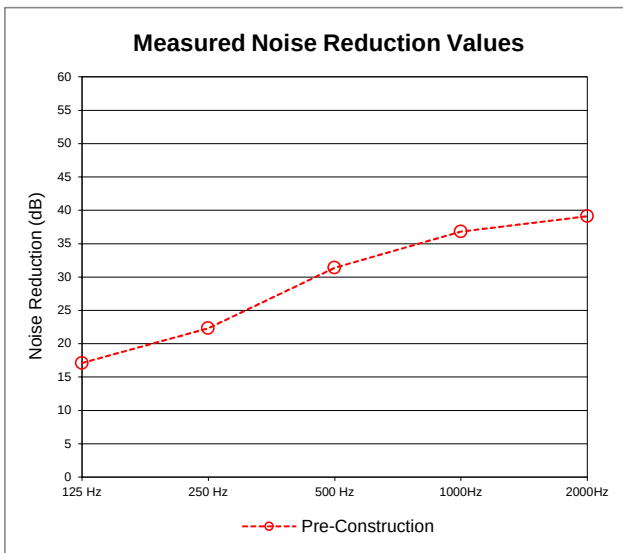

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Stanley
 Address: 22620 16th Ave S
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.8	52.1	49.8	47.3	33.7	51.5
Exterior Measurement (flush)	92.0	90.7	92.2	88.6	88.2	96.1
Exterior Adjusted	86.0	84.7	86.2	82.6	82.2	90.1
Interior Background	39.4	30.1	29.3	26.4	24.2	32.9
Interior Measurement	67.6	60.7	54.8	46.0	39.2	56.9
Interior Adjusted	67.6	60.7	54.8	46.0	39.1	56.9
Noise Reduction	18.4	24.0	31.4	36.6	43.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.9	33.1	33.7	30.0	18.7	38.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.5 dB

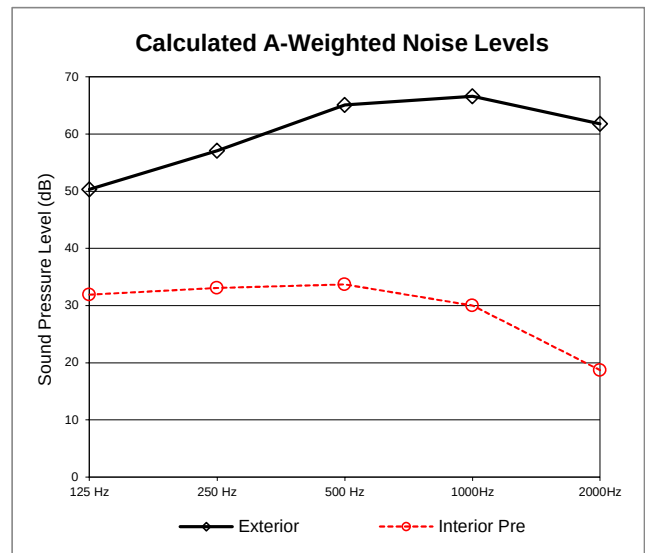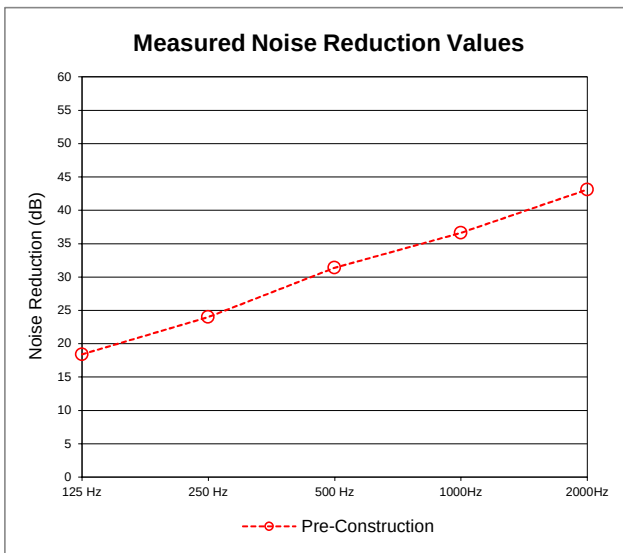



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Living / Dining Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	65.0	62.7	58.1	52.8	47.0	59.4
Exterior Measurement (flush)	80.6	81.2	84.8	82.0	82.0	88.2
Exterior Adjusted	74.5	75.1	78.8	76.0	76.0	82.2
Interior Background	32.5	26.1	21.9	21.9	18.6	27.4
Interior Measurement	59.8	49.8	45.2	39.0	38.3	48.9
Interior Adjusted	59.8	49.8	45.2	38.9	38.3	48.9
Noise Reduction	14.7	25.3	33.6	37.1	37.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.6	31.8	31.5	29.5	24.1	38.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.1 dB

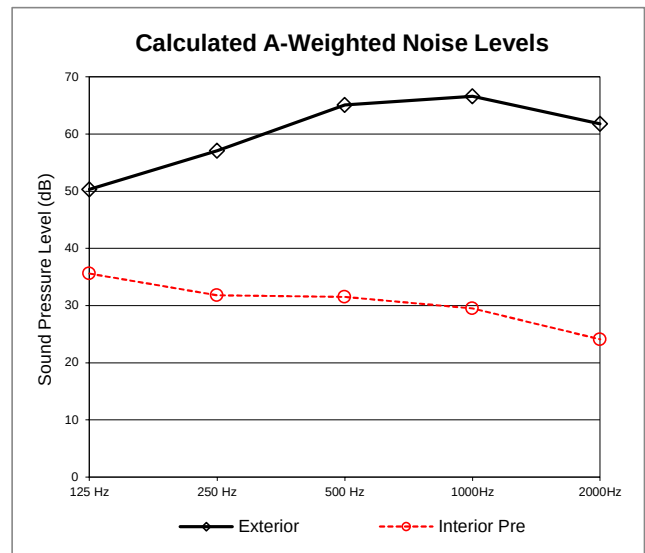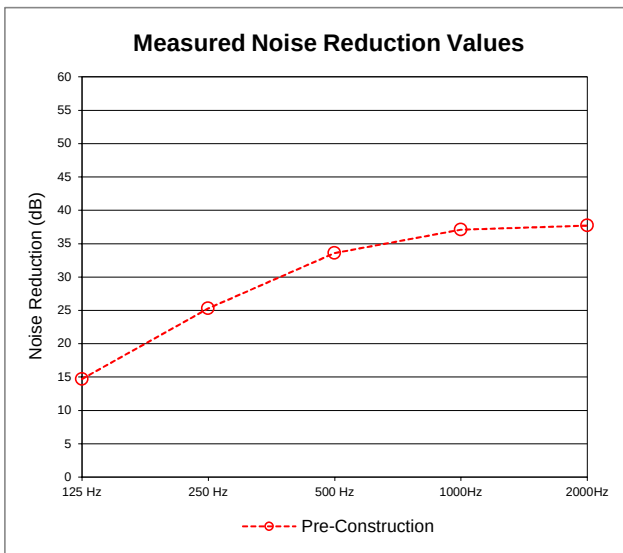

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Living / Dining Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.1	58.9	59.7	60.5	51.9	62.8
Exterior Measurement (flush)	87.0	88.8	89.9	87.0	84.3	92.8
Exterior Adjusted	81.0	82.8	83.9	81.0	78.3	86.8
Interior Background	32.5	26.1	21.9	21.9	18.6	27.4
Interior Measurement	61.0	57.2	51.0	44.2	43.2	53.6
Interior Adjusted	61.0	57.2	51.0	44.2	43.2	53.6
Noise Reduction	20.0	25.6	32.9	36.8	35.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.3	31.5	32.2	29.8	26.7	37.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.5 dB

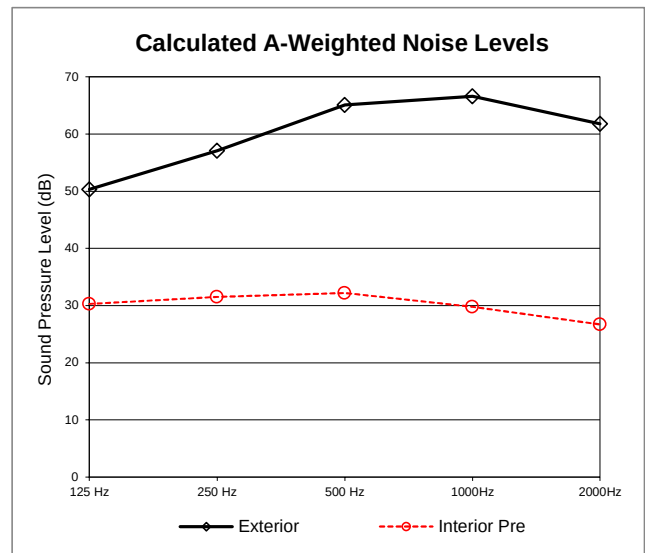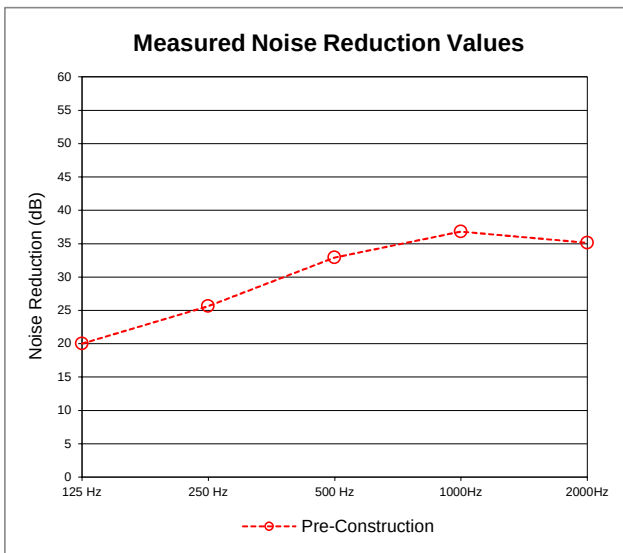

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	57.5	54.0	53.6	42.7	56.7
Exterior Measurement (flush)	89.3	87.8	91.1	88.0	84.4	93.5
Exterior Adjusted	83.3	81.8	85.1	82.0	78.4	87.5
Interior Background	33.4	35.2	29.0	26.2	20.3	32.0
Interior Measurement	62.6	57.8	52.1	46.2	41.0	54.5
Interior Adjusted	62.6	57.8	52.1	46.2	41.0	54.5
Noise Reduction	20.7	24.0	33.0	35.8	37.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.6	33.1	32.1	30.8	24.4	37.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.2 dB

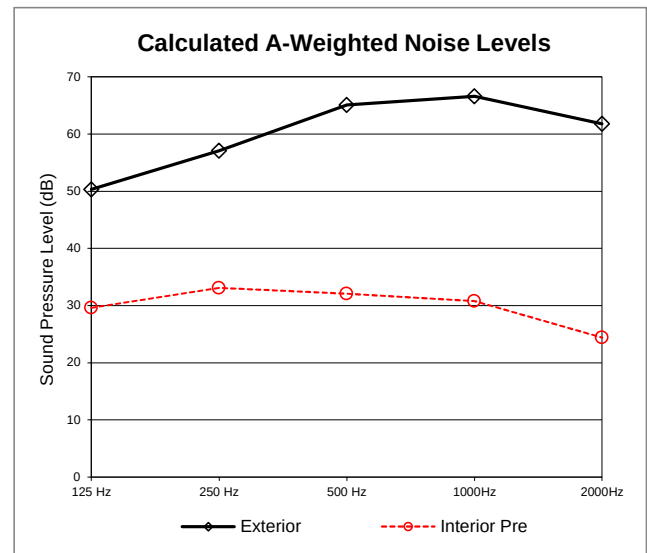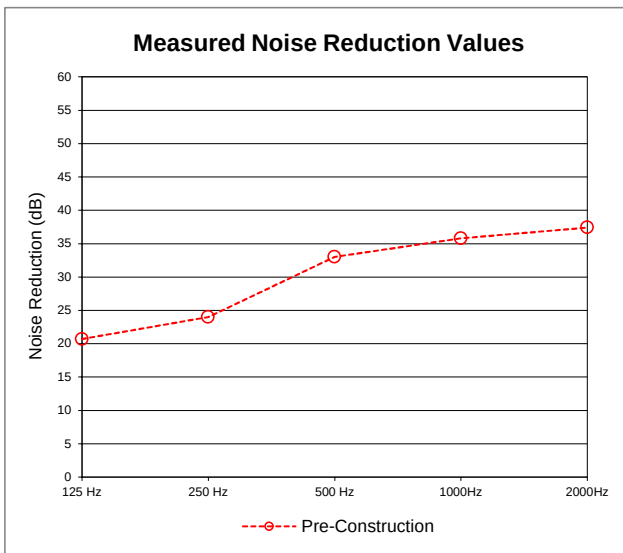



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	65.0	62.7	58.1	52.8	47.0	59.4
Exterior Measurement (flush)	84.5	81.7	85.6	82.3	81.6	88.9
Exterior Adjusted	78.5	75.6	79.6	76.3	75.6	82.9
Interior Background	41.1	34.2	29.4	29.8	29.9	37.0
Interior Measurement	56.5	50.9	48.0	41.0	39.9	49.9
Interior Adjusted	56.4	50.8	47.9	40.7	39.4	49.7
Noise Reduction	22.1	24.8	31.7	35.6	36.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.2	32.3	33.4	31.0	25.6	37.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.1 dB

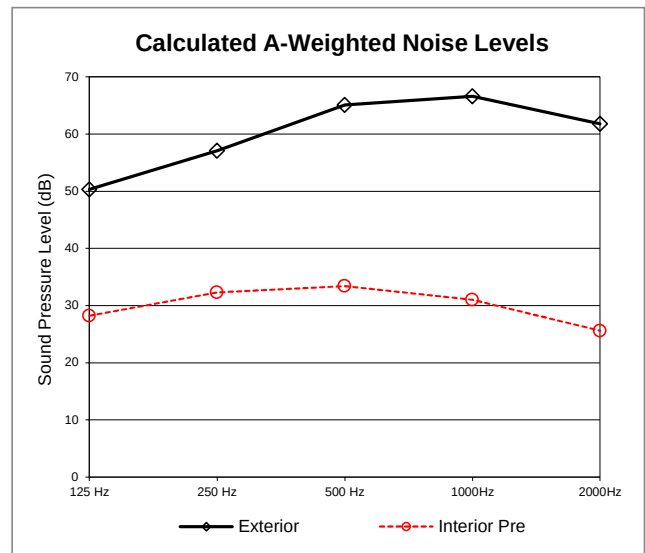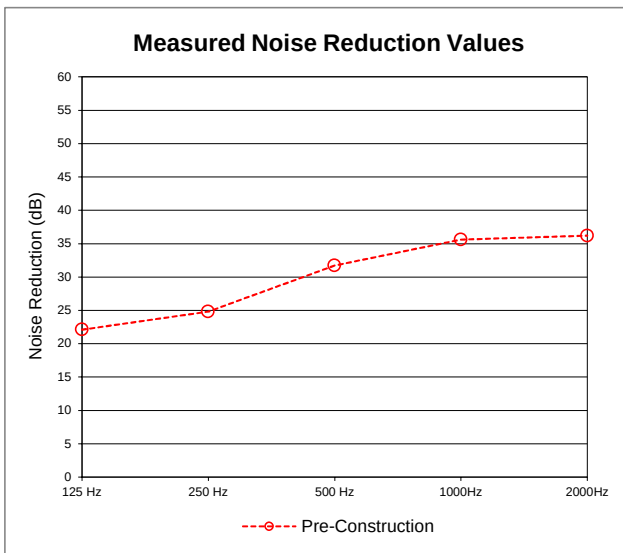



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.4	53.0	49.3	49.3	44.1	53.1
Exterior Measurement (flush)	97.5	97.8	97.5	92.8	89.4	99.2
Exterior Adjusted	91.5	91.8	91.5	86.8	83.4	93.2
Interior Background	47.3	38.2	31.1	23.4	20.7	35.2
Interior Measurement	73.5	59.8	54.2	43.4	37.2	58.5
Interior Adjusted	73.5	59.8	54.2	43.4	37.1	58.5
Noise Reduction	18.0	32.0	37.3	43.4	46.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.3	25.1	27.8	23.2	15.5	34.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.4 dB

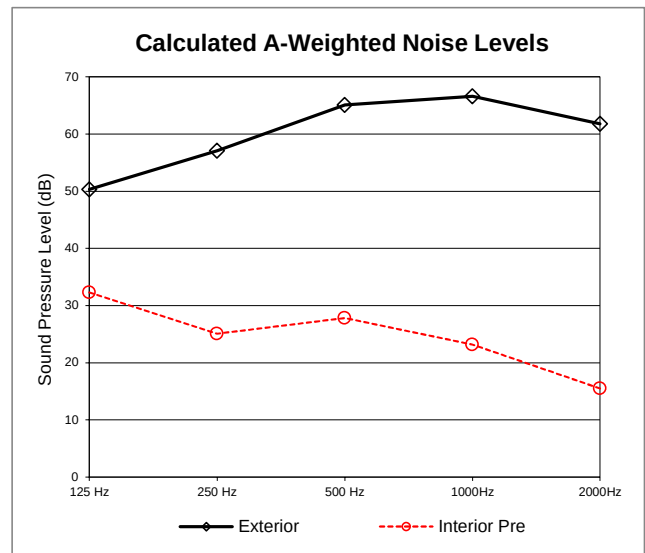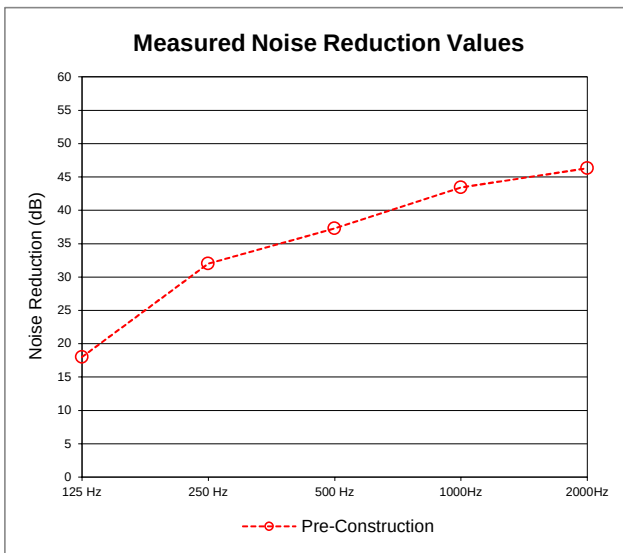



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.1	58.9	59.7	60.5	51.9	62.8
Exterior Measurement (flush)	92.5	91.1	92.8	88.1	85.0	94.1
Exterior Adjusted	86.5	85.1	86.8	82.1	79.0	88.1
Interior Background	47.3	38.2	31.1	23.4	20.7	35.2
Interior Measurement	64.8	57.0	51.2	42.7	40.4	53.8
Interior Adjusted	64.7	56.9	51.2	42.6	40.4	53.7
Noise Reduction	21.8	28.2	35.6	39.5	38.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.5	28.9	29.5	27.1	23.2	34.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.1 dB

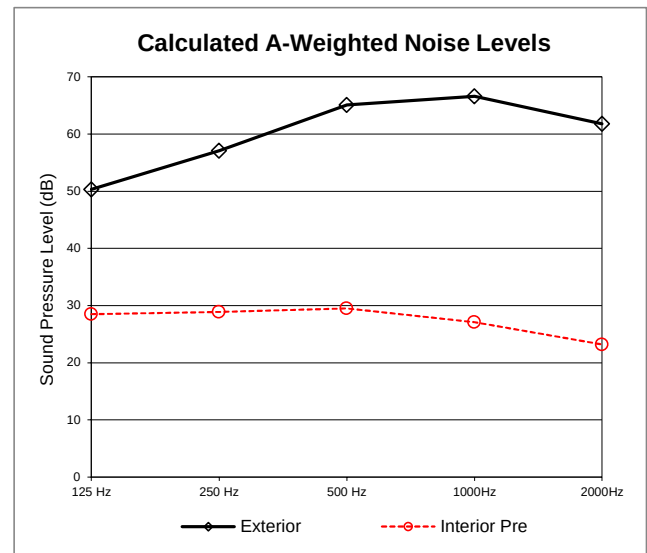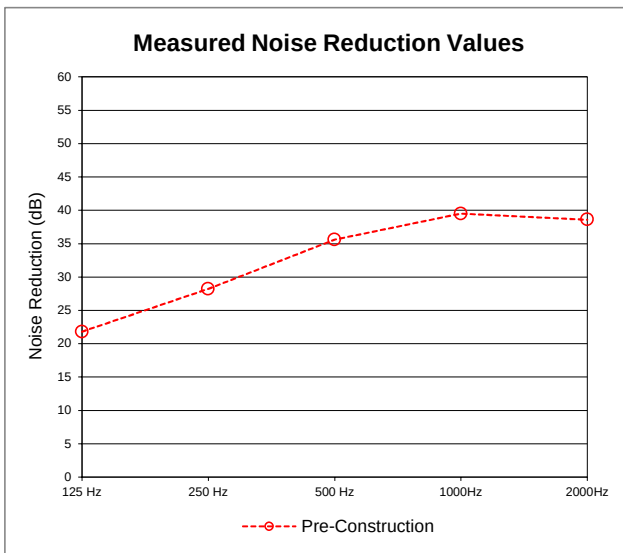



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	51.7	51.1	45.3	46.2	40.9	49.8
Exterior Measurement (flush)	91.8	94.0	94.5	91.9	87.4	97.0
Exterior Adjusted	85.8	88.0	88.5	85.9	81.4	91.0
Interior Background	48.2	36.1	28.3	21.0	17.7	34.3
Interior Measurement	62.5	53.8	49.9	43.7	43.6	52.8
Interior Adjusted	62.3	53.7	49.9	43.7	43.6	52.7
Noise Reduction	23.5	34.3	38.6	42.2	37.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.8	22.8	26.5	24.4	24.0	32.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						37.8 dB

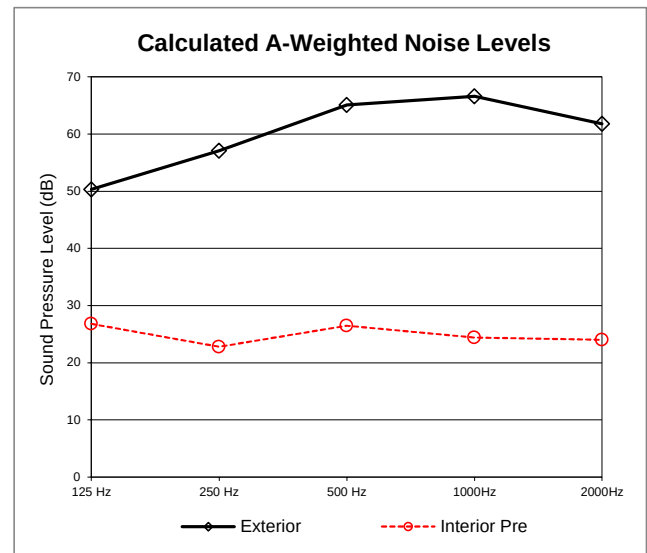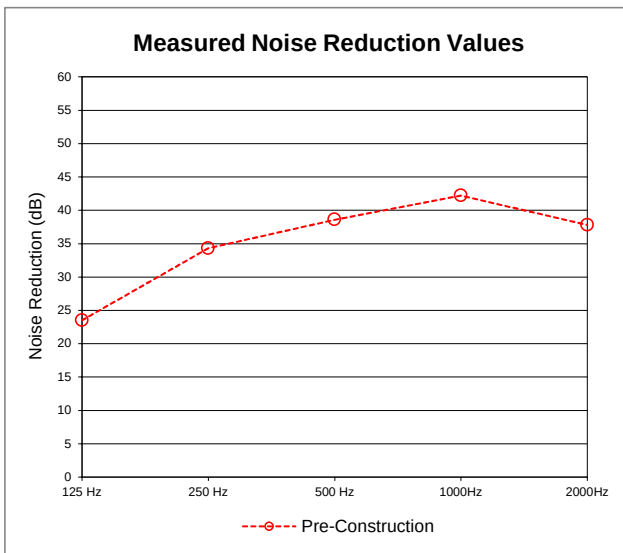

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	51.7	51.1	45.3	46.2	40.9	49.8
Exterior Measurement (flush)	93.5	95.4	96.1	93.1	88.8	98.3
Exterior Adjusted	87.5	89.4	90.1	87.1	82.8	92.3
Interior Background	34.3	27.9	20.8	22.7	22.3	30.4
Interior Measurement	59.7	56.9	48.0	38.9	34.4	51.4
Interior Adjusted	59.7	56.9	48.0	38.8	34.1	51.4
Noise Reduction	27.8	32.5	42.1	48.3	48.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	22.5	24.6	23.0	18.3	13.1	28.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.2 dB

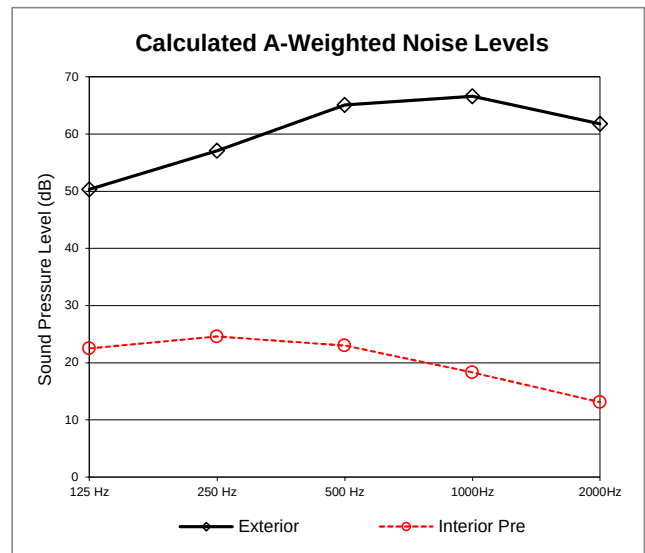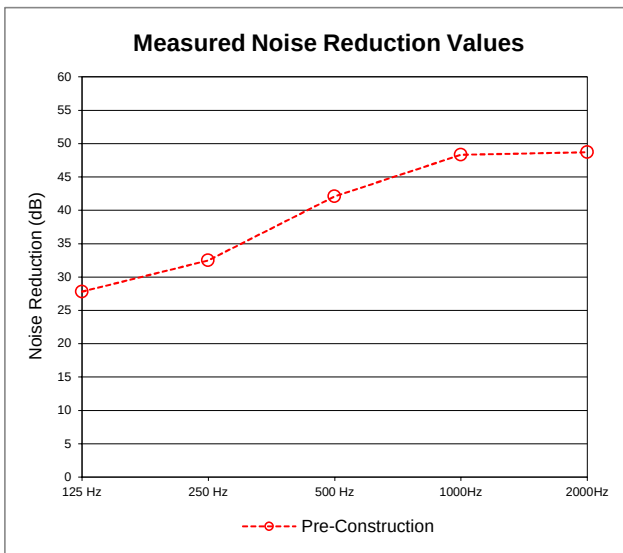

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 4 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.4	53.0	49.3	49.3	44.1	53.1
Exterior Measurement (flush)	97.4	97.0	97.2	93.2	93.3	100.4
Exterior Adjusted	91.4	91.0	91.2	87.2	87.3	94.4
Interior Background	41.9	33.6	27.1	21.9	19.0	31.1
Interior Measurement	70.3	57.4	49.2	40.4	34.3	55.5
Interior Adjusted	70.3	57.4	49.2	40.3	34.2	55.5
Noise Reduction	21.1	33.6	42.0	46.9	53.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.2	23.5	23.1	19.7	8.7	31.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						38.7 dB

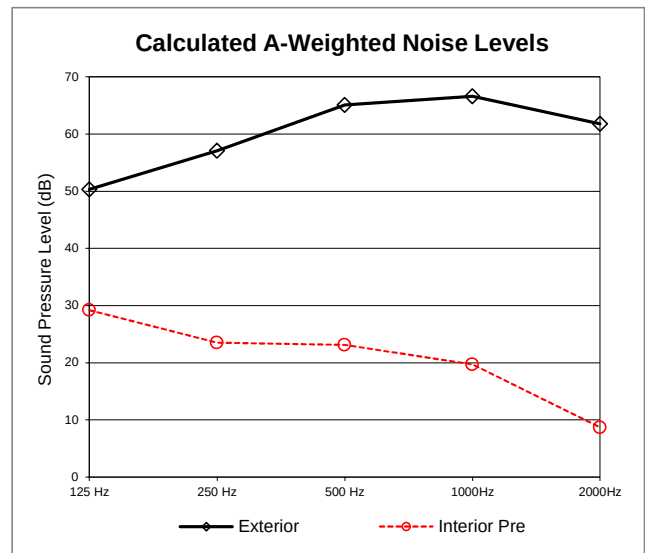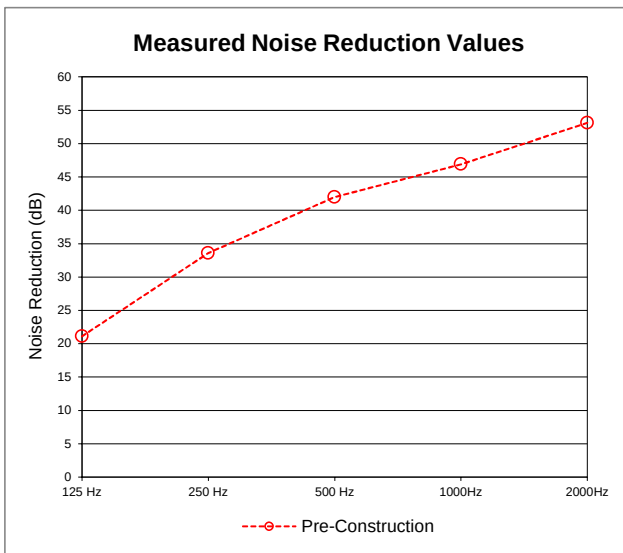

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 4 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	57.5	54.0	53.6	42.7	56.7
Exterior Measurement (flush)	92.0	89.3	91.2	89.2	84.5	94.2
Exterior Adjusted	86.0	83.3	85.2	83.2	78.5	88.2
Interior Background	41.9	33.6	27.1	21.9	19.0	31.1
Interior Measurement	66.2	57.3	50.7	42.2	39.4	54.5
Interior Adjusted	66.2	57.3	50.7	42.2	39.4	54.5
Noise Reduction	19.8	26.0	34.5	41.0	39.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.5	31.1	30.6	25.6	22.7	36.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.9 dB

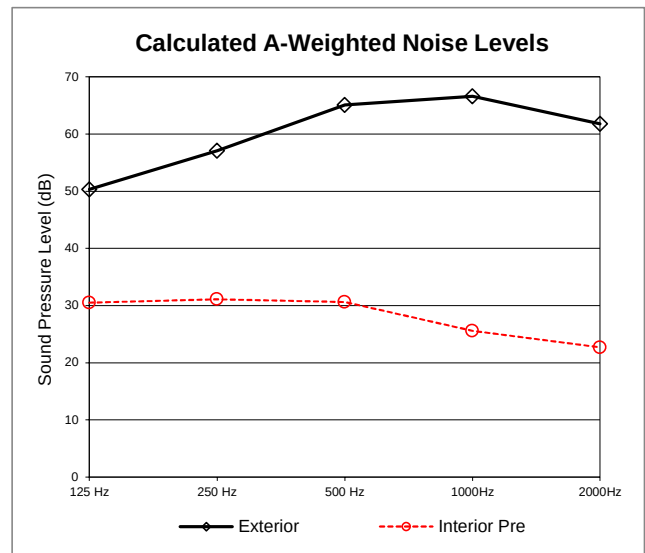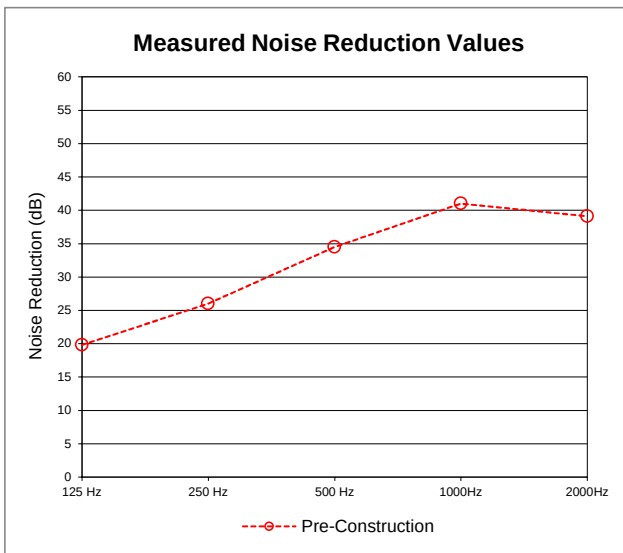

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Betelhem
 Address: 23249 17th PI S
 Local City: Des Moines

Tested Room: Bedroom 5 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.3	54.4	51.1	51.4	44.0	54.5
Exterior Measurement (flush)	101.6	104.3	102.7	98.6	97.6	105.7
Exterior Adjusted	95.6	98.3	96.7	92.6	91.6	99.7
Interior Background	35.0	29.3	19.0	13.4	13.0	24.9
Interior Measurement	79.0	65.5	59.0	50.2	43.4	64.0
Interior Adjusted	79.0	65.5	59.0	50.2	43.4	64.0
Noise Reduction	16.6	32.8	37.7	42.4	48.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.7	24.3	27.4	24.2	13.6	35.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.6 dB

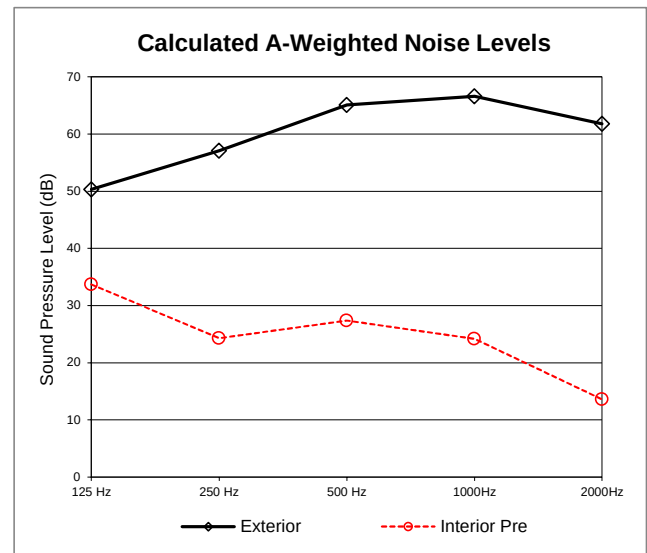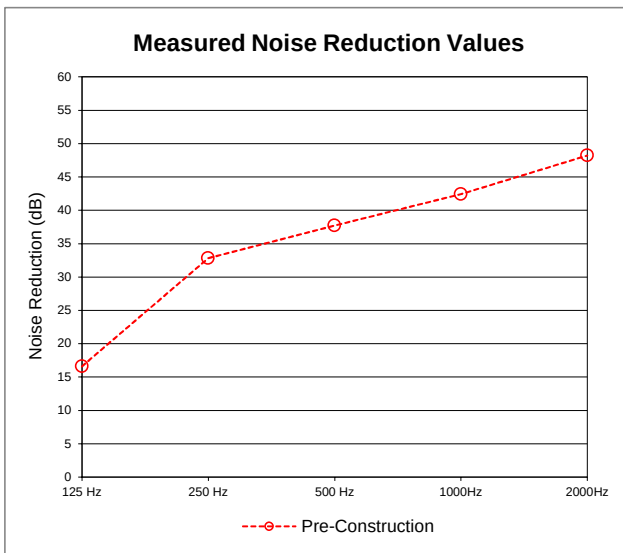

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Living Room Façade 1
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	48.9	46.4	45.1	38.1	49.2
Exterior Measurement (flush)	99.6	98.3	99.2	94.1	90.5	100.1
Exterior Adjusted	93.6	92.3	93.2	88.1	84.5	94.1
Interior Background	42.0	38.6	32.2	31.4	30.1	37.4
Interior Measurement	64.5	56.7	53.7	45.6	37.4	54.5
Interior Adjusted	64.5	56.6	53.7	45.4	36.5	54.4
Noise Reduction	29.1	35.7	39.5	42.7	48.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	21.2	21.4	25.6	23.9	13.8	29.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						40.4 dB

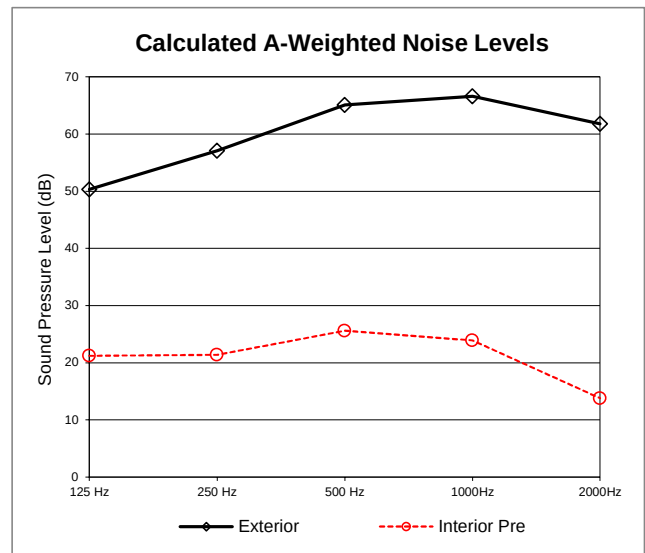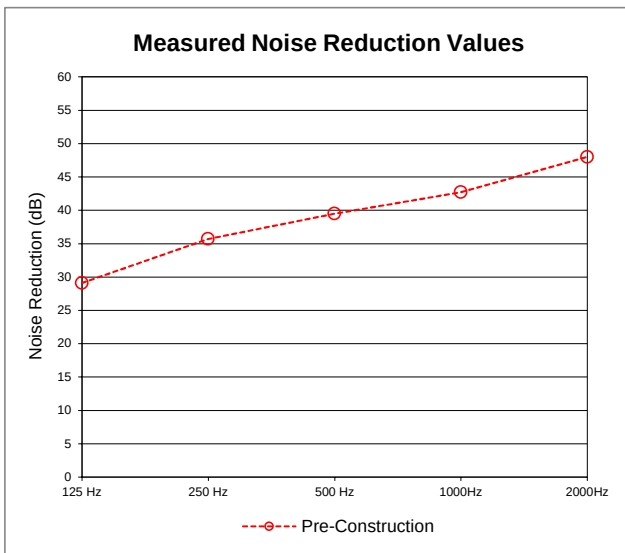

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Living Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	48.9	46.4	45.1	38.1	49.2
Exterior Measurement (flush)	91.7	89.7	90.9	86.2	82.1	91.9
Exterior Adjusted	85.7	83.7	84.9	80.2	76.1	85.9
Interior Background	42.0	38.6	32.2	31.4	30.1	37.4
Interior Measurement	63.2	52.9	50.6	43.5	38.1	52.3
Interior Adjusted	63.2	52.7	50.5	43.2	37.4	52.2
Noise Reduction	22.5	31.0	34.4	37.0	38.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.8	26.1	30.7	29.6	23.1	35.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.8 dB

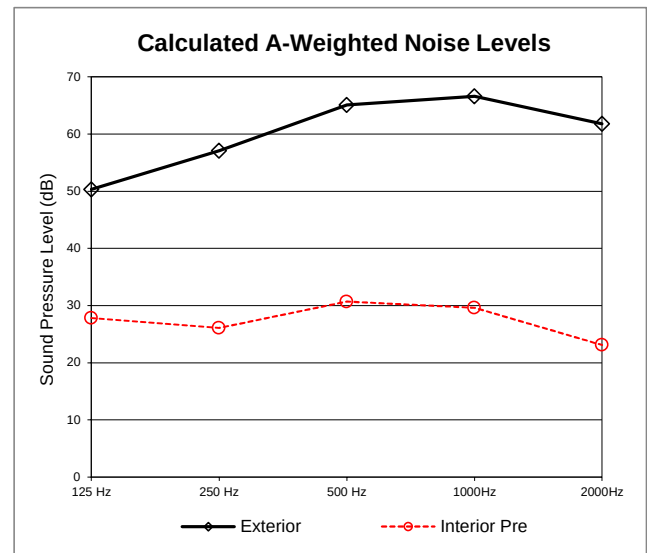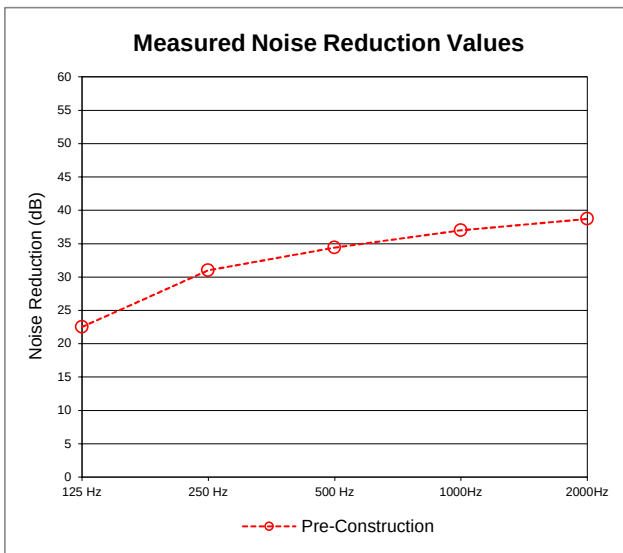

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Family Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.7	53.7	51.9	50.3	42.0	54.1
Exterior Measurement (flush)	92.0	89.2	89.1	87.1	81.9	91.5
Exterior Adjusted	86.0	83.2	83.1	81.1	75.9	85.5
Interior Background	40.7	34.4	27.3	20.8	16.4	30.6
Interior Measurement	55.2	47.1	41.3	33.9	30.2	44.2
Interior Adjusted	55.0	46.9	41.1	33.7	30.0	44.0
Noise Reduction	31.0	36.3	42.0	47.4	45.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	19.3	20.8	23.1	19.2	15.9	27.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						42.7 dB

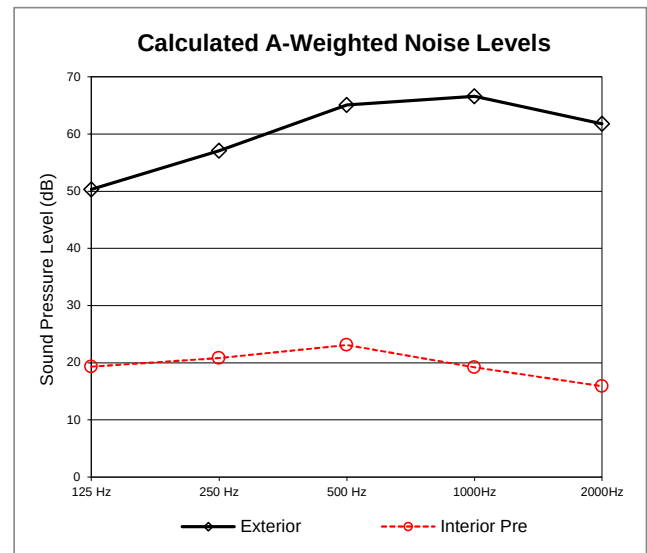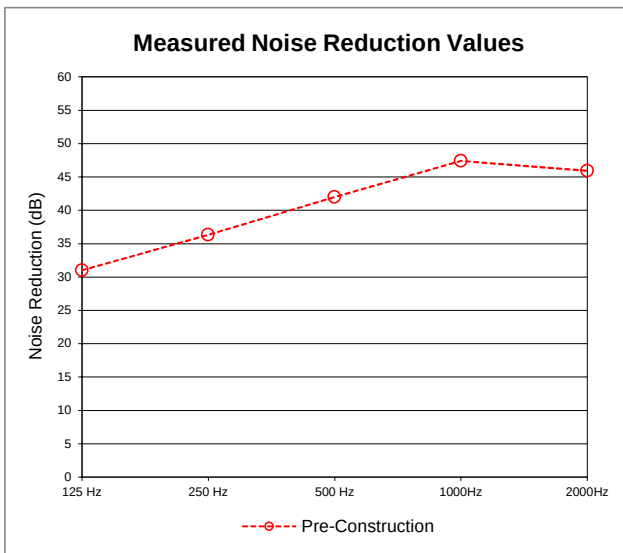



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	48.9	46.4	45.1	38.1	49.2
Exterior Measurement (flush)	98.8	97.2	100.0	94.2	89.0	100.2
Exterior Adjusted	92.8	91.2	94.0	88.2	83.0	94.2
Interior Background	36.7	33.4	27.6	24.0	22.7	31.6
Interior Measurement	65.9	55.3	59.2	55.5	48.6	60.1
Interior Adjusted	65.9	55.3	59.2	55.5	48.6	60.1
Noise Reduction	26.9	35.9	34.8	32.7	34.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	23.4	21.2	30.3	33.9	27.4	36.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.5 dB

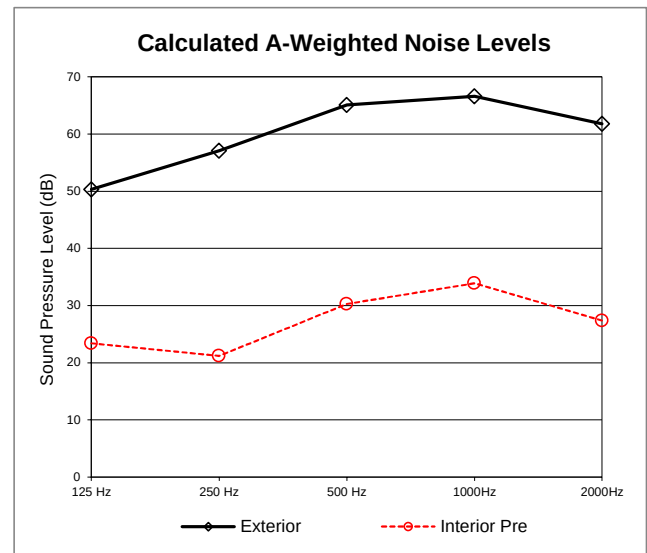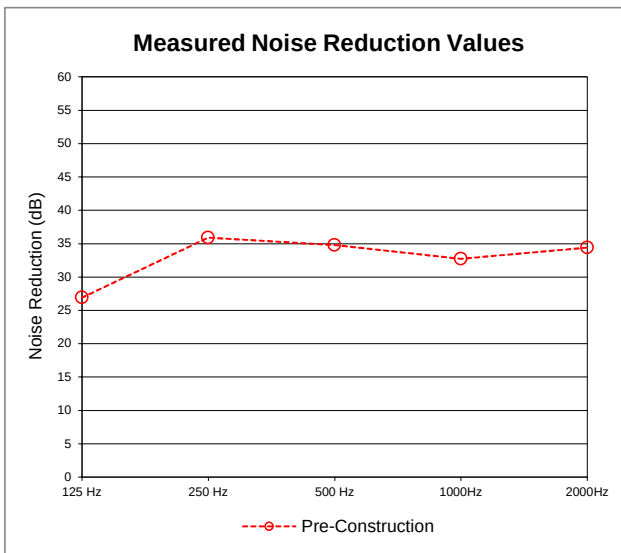

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Dining / Kitchen Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.4	55.6	57.0	52.2	43.4	57.2
Exterior Measurement (flush)	95.8	95.9	96.9	92.8	88.5	98.2
Exterior Adjusted	89.8	89.9	90.9	86.8	82.5	92.2
Interior Background	44.8	39.4	36.6	30.2	27.7	37.8
Interior Measurement	69.5	67.3	64.1	55.0	53.7	65.1
Interior Adjusted	69.5	67.3	64.1	55.0	53.7	65.1
Noise Reduction	20.3	22.6	26.8	31.8	28.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.0	34.5	38.3	34.8	33.0	41.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.1 dB

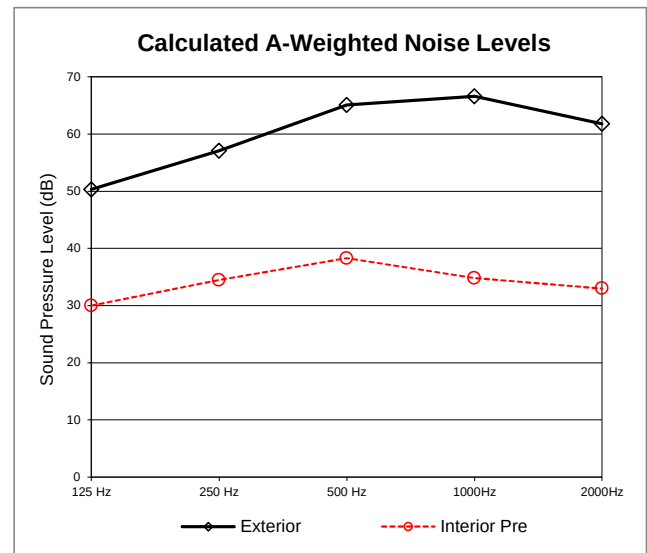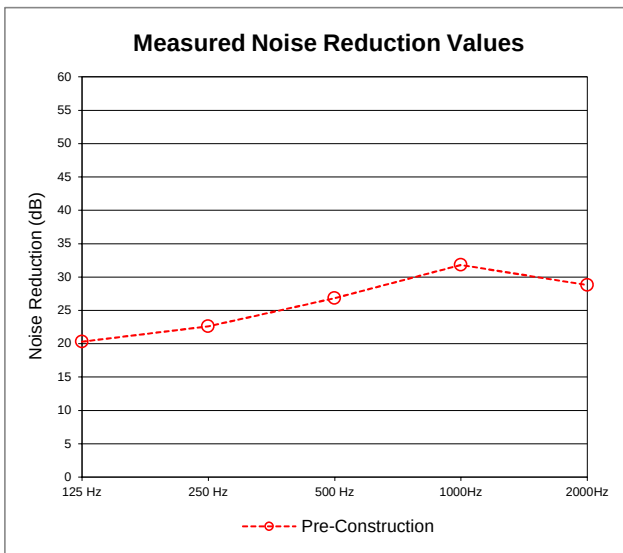

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Dining / Kitchen Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.7	53.7	51.9	50.3	42.0	54.1
Exterior Measurement (flush)	88.8	92.3	93.0	88.9	88.1	94.8
Exterior Adjusted	82.8	86.3	87.0	82.9	82.1	88.8
Interior Background	44.8	39.4	36.6	30.2	27.7	37.8
Interior Measurement	63.2	57.6	58.4	49.0	46.0	57.7
Interior Adjusted	63.1	57.5	58.4	48.9	45.9	57.7
Noise Reduction	19.7	28.8	28.6	34.0	36.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.6	28.3	36.5	32.6	25.6	39.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.7 dB

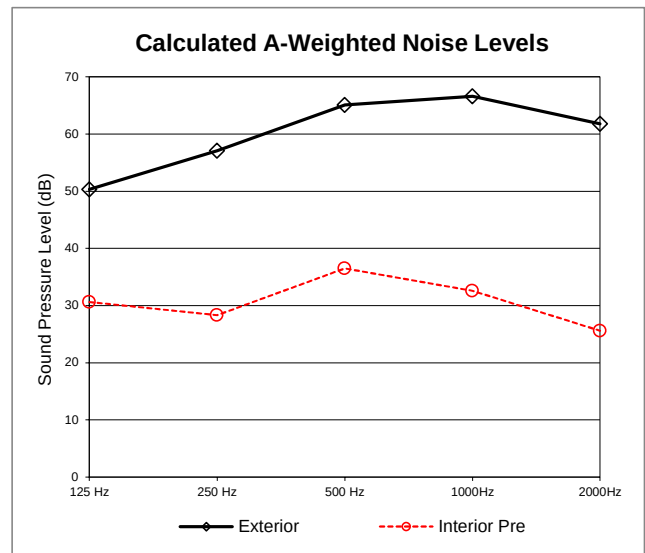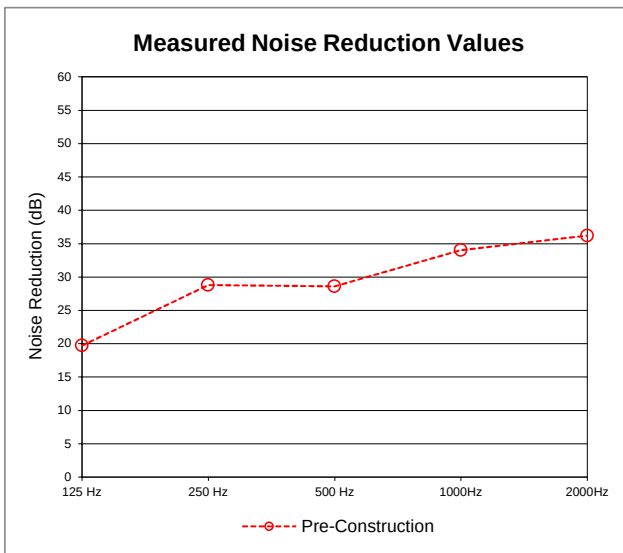

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Bedroom 1 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.0	51.5	50.3	49.2	42.7	53.0
Exterior Measurement (flush)	98.2	96.6	97.3	92.5	89.4	98.5
Exterior Adjusted	92.2	90.6	91.3	86.5	83.4	92.5
Interior Background	40.8	39.4	32.6	24.8	19.7	34.8
Interior Measurement	61.0	55.5	51.3	44.8	39.9	52.7
Interior Adjusted	61.0	55.4	51.2	44.8	39.9	52.6
Noise Reduction	31.2	35.2	40.1	41.7	43.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	19.1	21.9	25.0	24.9	18.3	29.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						40.3 dB

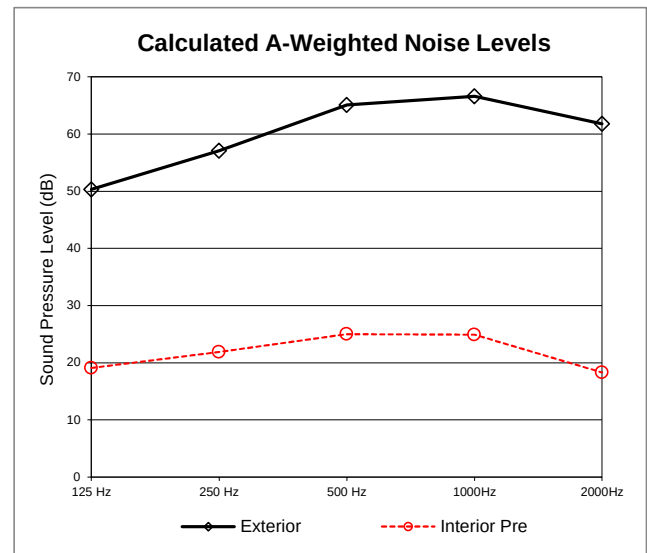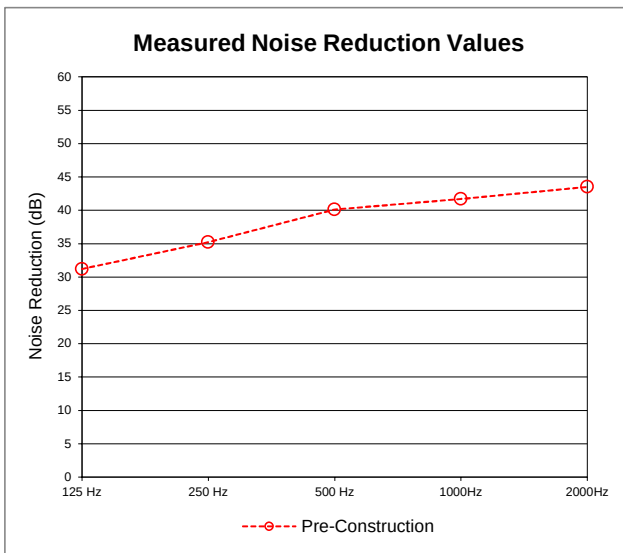

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Bedroom 1 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.0	51.5	50.3	49.2	42.7	53.0
Exterior Measurement (flush)	104.5	103.0	103.2	95.1	91.9	103.0
Exterior Adjusted	98.5	97.0	97.2	89.1	85.9	97.0
Interior Background	40.8	39.4	32.6	24.8	19.7	34.8
Interior Measurement	71.1	59.7	56.8	42.2	36.5	58.6
Interior Adjusted	71.1	59.7	56.8	42.1	36.4	58.6
Noise Reduction	27.4	37.3	40.4	47.0	49.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	22.9	19.8	24.7	19.6	12.3	28.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.6 dB

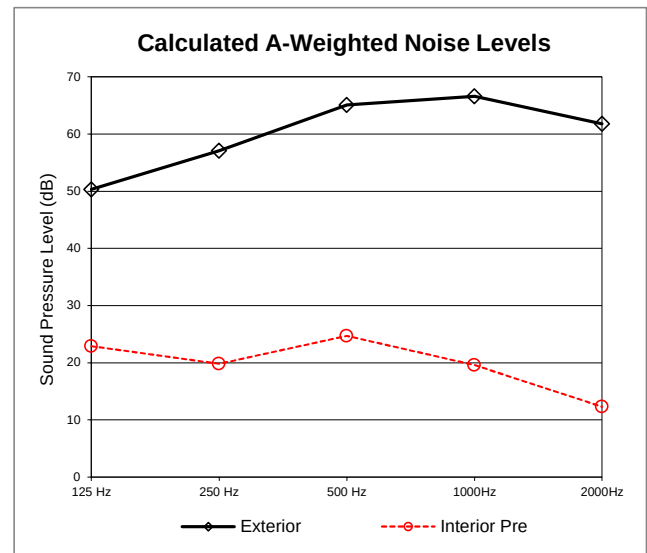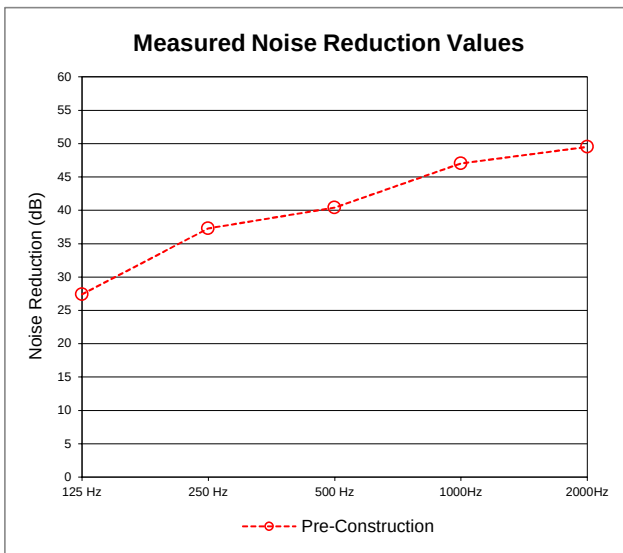

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Bedroom 2 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.2	55.3	52.1	47.3	41.9	53.5
Exterior Measurement (flush)	106.9	103.3	103.2	96.3	91.1	103.5
Exterior Adjusted	100.9	97.3	97.2	90.3	85.1	97.5
Interior Background	39.5	34.9	30.5	29.5	26.9	35.0
Interior Measurement	68.9	58.7	53.8	44.6	39.2	56.2
Interior Adjusted	68.9	58.7	53.8	44.5	38.9	56.2
Noise Reduction	32.0	38.6	43.4	45.8	46.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	18.3	18.5	21.7	20.8	15.6	26.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						43.5 dB

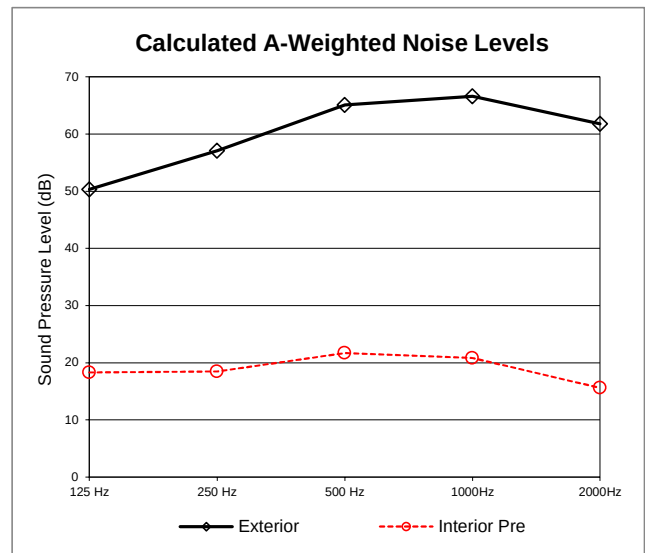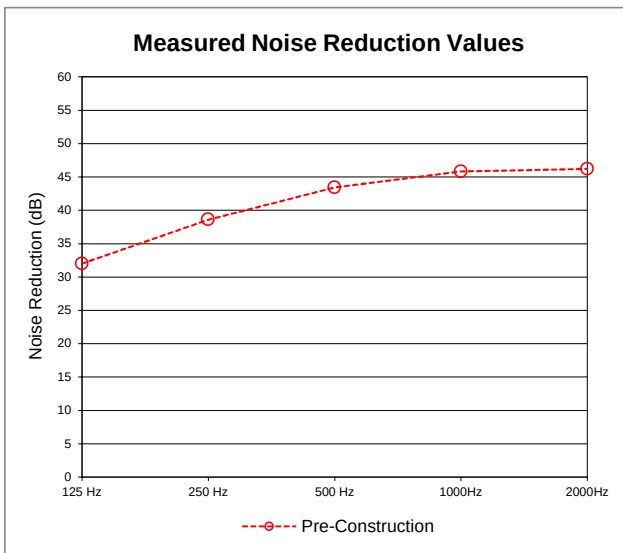



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Bedroom 2 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.2	55.3	52.1	47.3	41.9	53.5
Exterior Measurement (flush)	102.5	101.7	102.2	96.0	91.4	102.5
Exterior Adjusted	96.5	95.7	96.2	90.0	85.4	96.5
Interior Background	39.5	34.9	30.5	29.5	26.9	35.0
Interior Measurement	67.0	56.9	53.2	43.7	39.6	55.5
Interior Adjusted	67.0	56.9	53.2	43.5	39.4	55.5
Noise Reduction	29.5	38.8	43.0	46.5	46.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	20.8	18.3	22.1	20.1	15.8	26.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						43.1 dB

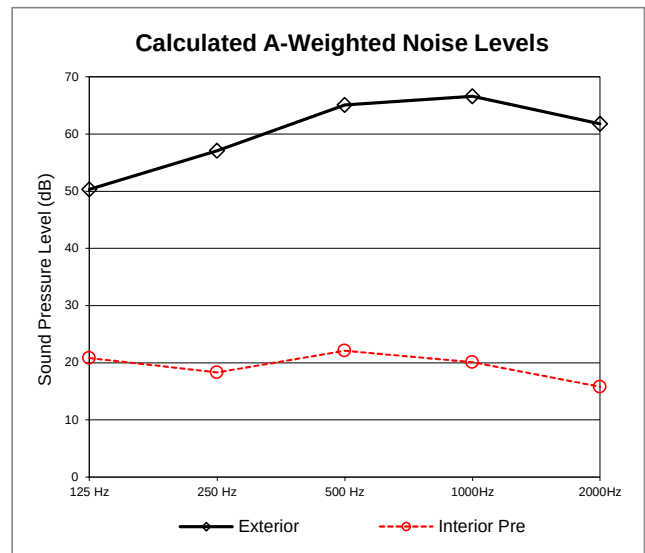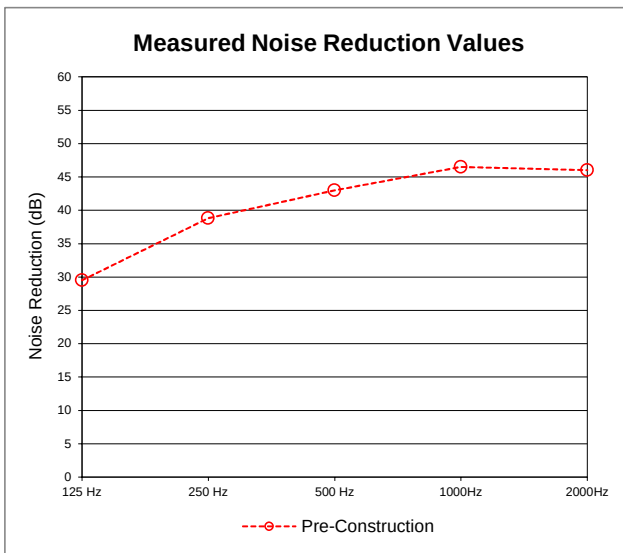



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Bedroom 3 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.0	51.5	50.3	49.2	42.7	53.0
Exterior Measurement (flush)	95.3	97.8	97.7	93.2	88.3	98.8
Exterior Adjusted	89.3	91.8	91.7	87.2	82.3	92.8
Interior Background	36.9	31.1	23.2	17.4	16.6	27.8
Interior Measurement	59.3	53.2	48.0	40.2	33.8	49.9
Interior Adjusted	59.3	53.2	48.0	40.2	33.7	49.9
Noise Reduction	30.0	38.6	43.7	47.0	48.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	20.3	18.5	21.4	19.6	13.2	26.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						43.7 dB

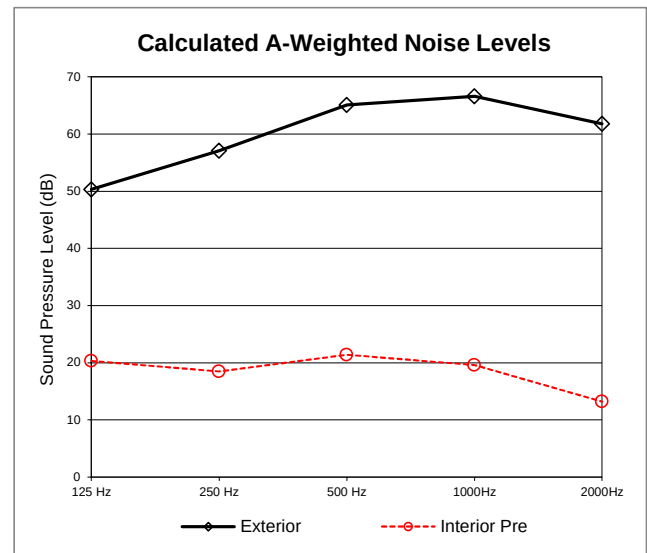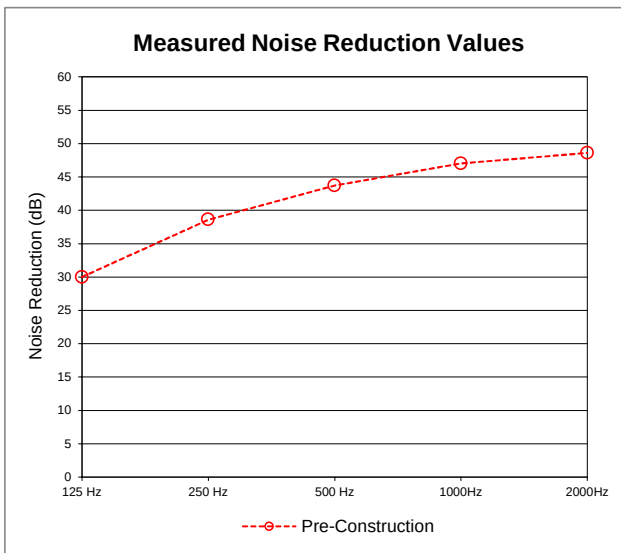



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Engstrum
 Address: 10457 19th Ave S
 Local City: Seattle

Tested Room: Bedroom 3 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.0	51.5	50.3	49.2	42.7	53.0
Exterior Measurement (flush)	107.8	106.3	107.3	101.3	99.0	108.1
Exterior Adjusted	101.8	100.3	101.3	95.3	93.0	102.1
Interior Background	36.9	31.1	23.2	17.4	16.6	27.8
Interior Measurement	72.1	63.4	59.8	52.8	48.3	61.4
Interior Adjusted	72.1	63.4	59.8	52.8	48.3	61.4
Noise Reduction	29.7	36.9	41.5	42.5	44.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	20.6	20.2	23.6	24.1	17.1	28.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.2 dB

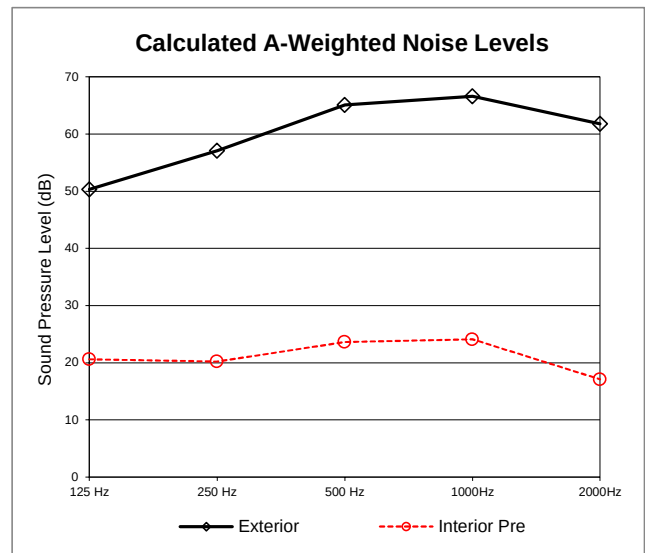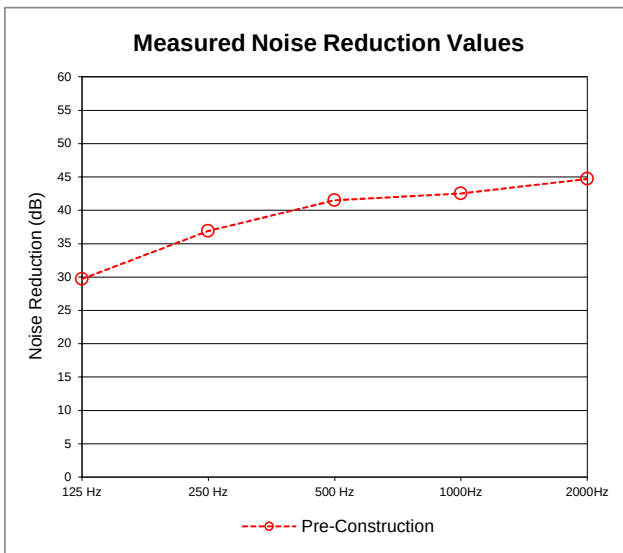



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Living / Dining Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	61.3	56.6	54.9	53.7	51.0	58.7
Exterior Measurement (flush)	89.6	93.1	94.5	90.8	87.2	96.1
Exterior Adjusted	83.6	87.1	88.5	84.8	81.2	90.1
Interior Background	32.1	27.4	21.1	19.3	16.9	25.8
Interior Measurement	63.7	62.0	62.3	59.6	54.8	64.8
Interior Adjusted	63.7	62.0	62.3	59.6	54.8	64.8
Noise Reduction	19.9	25.1	26.2	25.2	26.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.4	32.0	38.9	41.4	35.4	44.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						25.6 dB

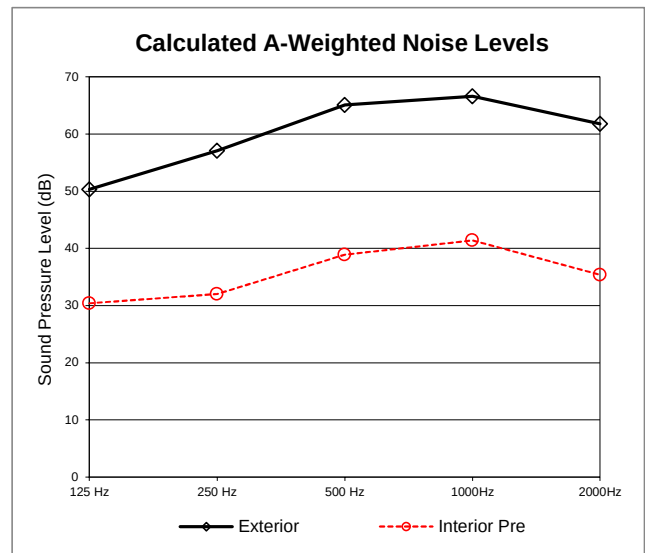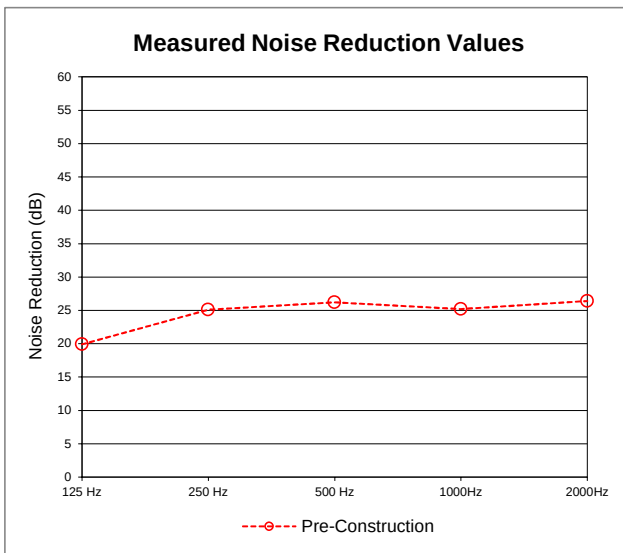



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Kitchen Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.8	56.5	52.7	51.4	46.7	56.0
Exterior Measurement (flush)	105.4	103.8	104.0	98.2	95.0	104.9
Exterior Adjusted	99.4	97.8	98.0	92.2	89.0	98.9
Interior Background	39.9	39.0	38.9	32.4	28.2	38.9
Interior Measurement	80.1	71.8	65.9	56.1	50.3	68.0
Interior Adjusted	80.1	71.8	65.9	56.1	50.3	68.0
Noise Reduction	19.3	26.0	32.1	36.1	38.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.0	31.1	33.0	30.5	23.1	37.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.3 dB

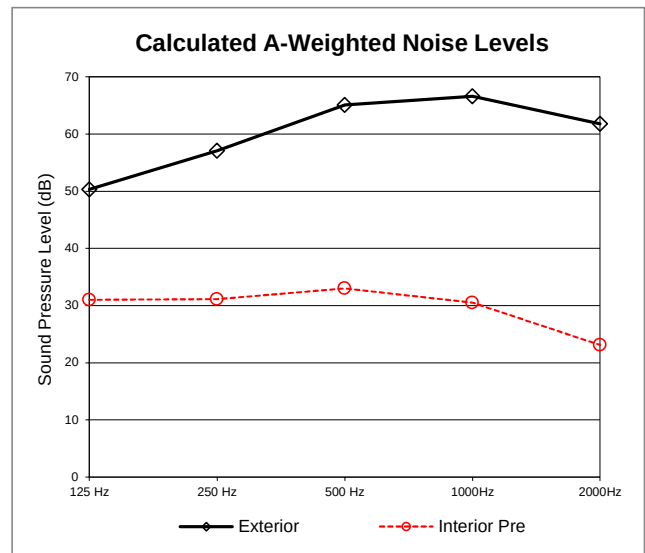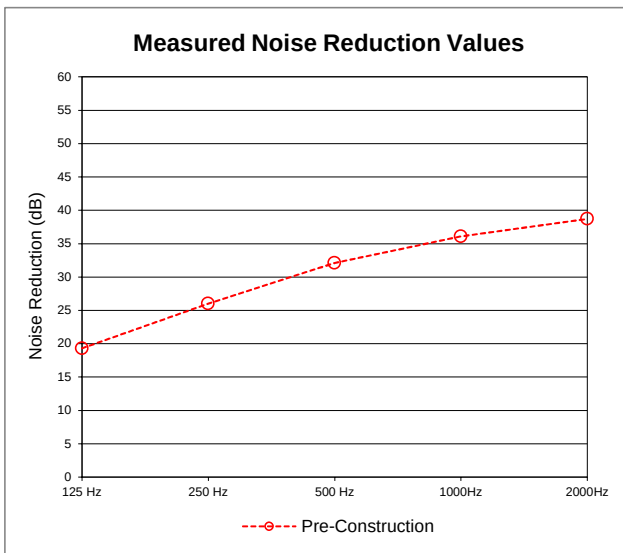



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Kitchen Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	61.3	56.6	54.9	53.7	51.0	58.7
Exterior Measurement (flush)	99.3	97.0	99.1	93.9	89.7	99.7
Exterior Adjusted	93.3	91.0	93.1	87.9	83.7	93.7
Interior Background	39.9	39.0	38.9	32.4	28.2	38.9
Interior Measurement	76.6	70.8	70.3	64.1	66.2	73.1
Interior Adjusted	76.6	70.8	70.3	64.1	66.2	73.1
Noise Reduction	16.7	20.2	22.8	23.8	17.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.6	36.9	42.3	42.8	44.3	48.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						21.5 dB

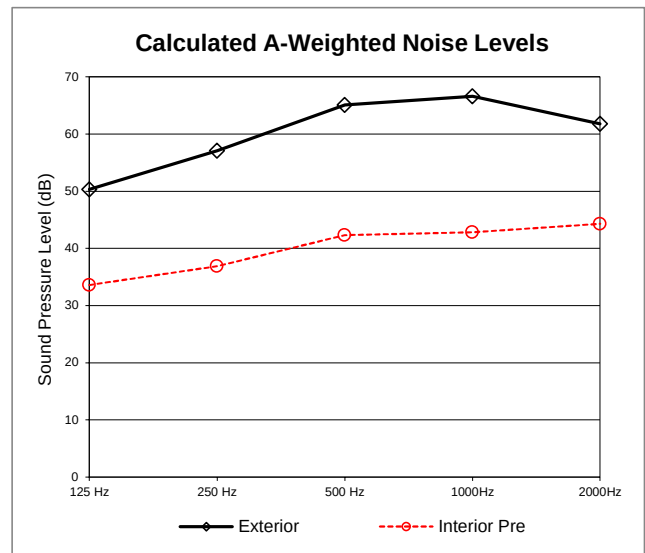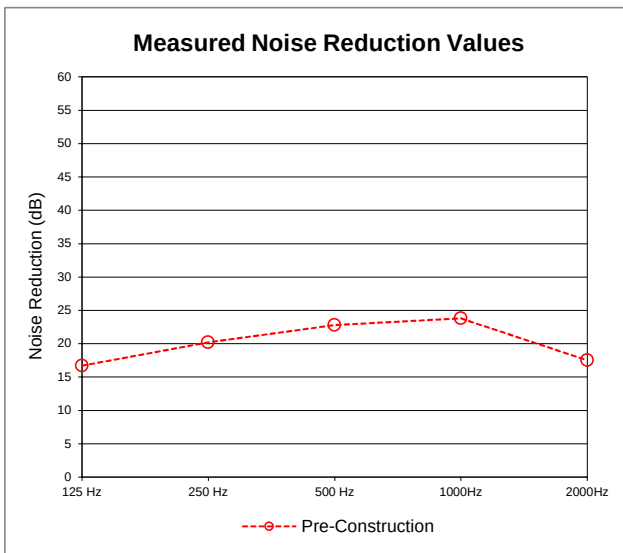



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	61.3	56.6	54.9	53.7	51.0	58.7
Exterior Measurement (flush)	86.0	86.5	90.5	83.9	81.6	91.0
Exterior Adjusted	80.0	80.5	84.5	77.9	75.6	85.0
Interior Background	41.2	41.0	38.8	34.1	29.6	39.9
Interior Measurement	60.0	55.4	54.0	46.6	38.5	53.9
Interior Adjusted	59.9	55.2	53.9	46.3	37.9	53.7
Noise Reduction	20.1	25.3	30.6	31.6	37.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.2	31.8	34.5	35.0	24.1	39.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.6 dB

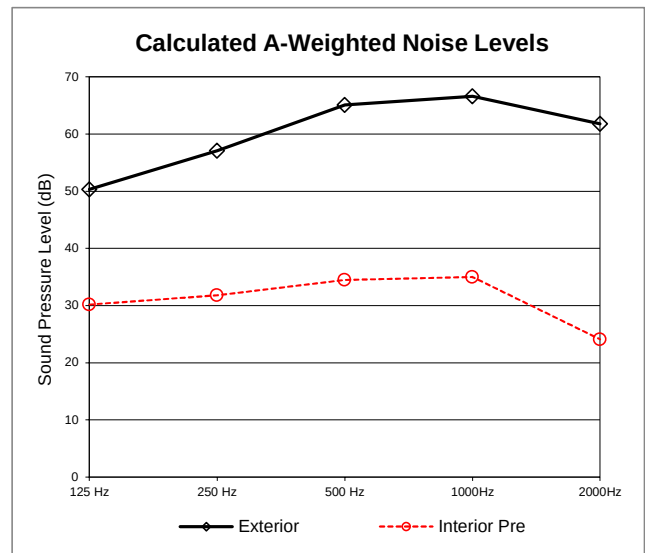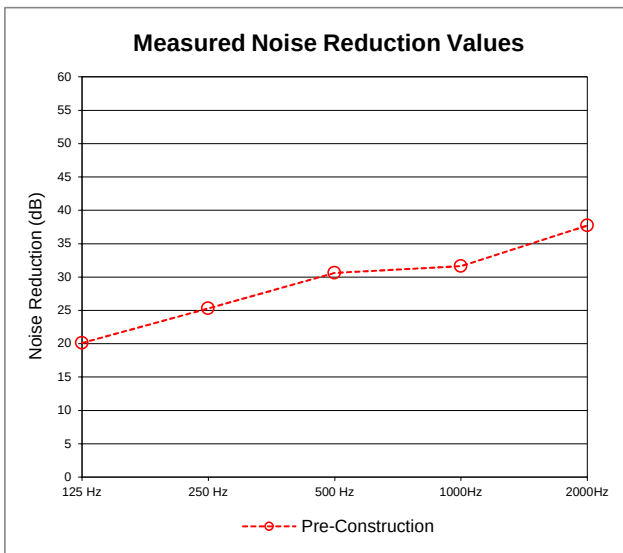

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.9	51.6	53.6	50.5	45.9	54.9
Exterior Measurement (flush)	96.1	93.9	94.9	91.6	88.4	97.0
Exterior Adjusted	90.1	87.9	88.9	85.6	82.4	91.0
Interior Background	31.4	25.3	23.3	19.1	17.3	26.2
Interior Measurement	66.4	62.3	56.1	47.0	40.3	57.5
Interior Adjusted	66.4	62.3	56.1	47.0	40.3	57.5
Noise Reduction	23.7	25.6	32.8	38.6	42.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.6	31.5	32.3	28.0	19.7	36.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.7 dB

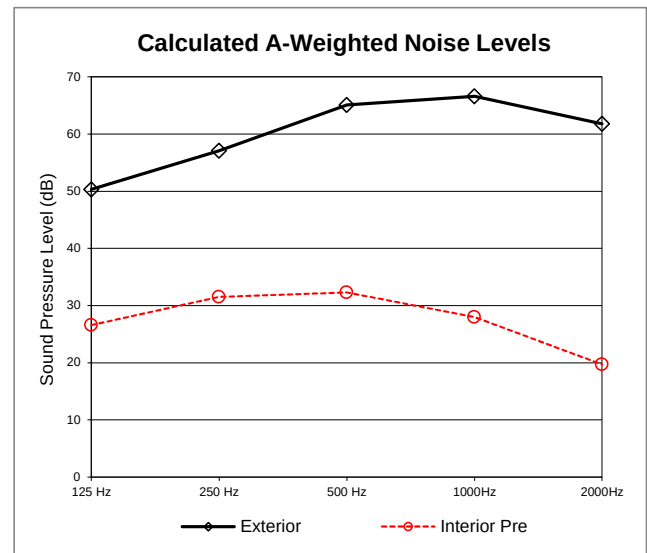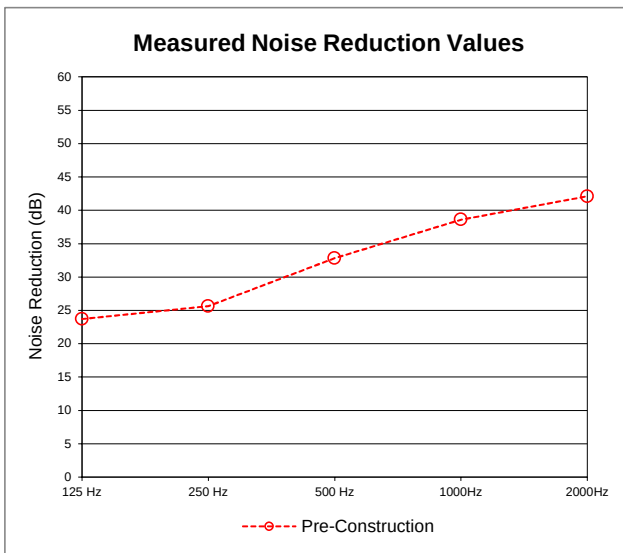

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.1	54.9	51.1	51.4	47.3	55.5
Exterior Measurement (flush)	88.2	87.0	87.0	81.9	77.9	88.3
Exterior Adjusted	82.2	81.0	81.0	75.9	71.9	82.3
Interior Background	37.8	33.4	24.0	20.8	19.7	29.4
Interior Measurement	61.5	59.9	54.8	48.0	46.8	57.0
Interior Adjusted	61.5	59.9	54.8	48.0	46.8	57.0
Noise Reduction	20.7	21.1	26.2	27.9	25.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.6	36.0	38.9	38.7	36.7	43.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						26.1 dB

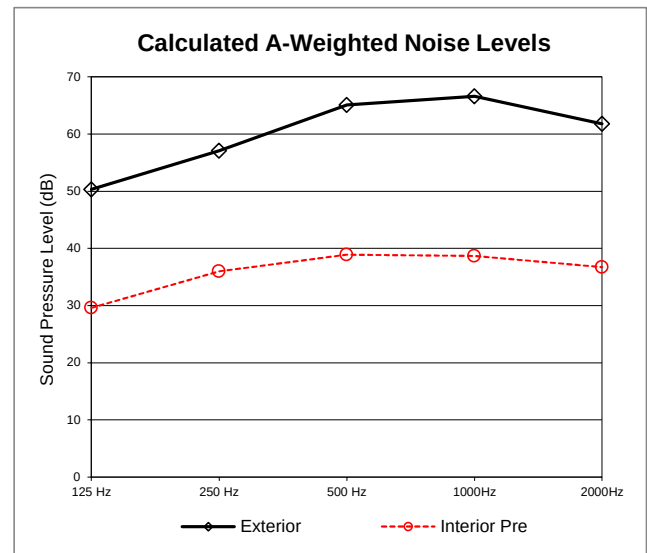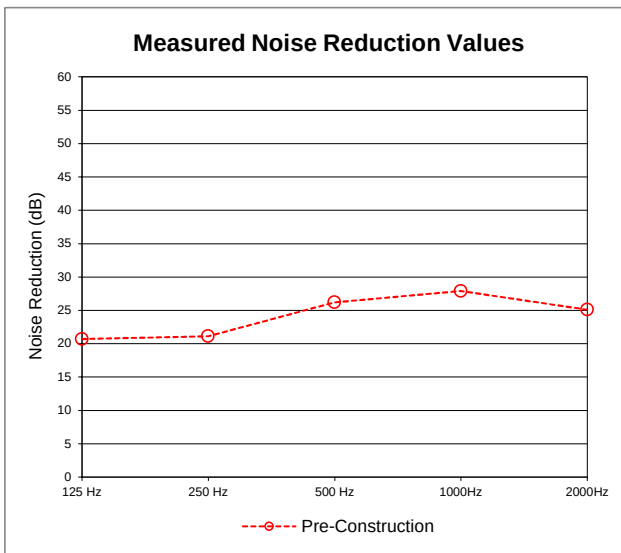



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tiemens
 Address: 10422 20th Ave S
 Local City: Seattle

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.9	51.6	53.6	50.5	45.9	54.9
Exterior Measurement (flush)	89.6	93.1	94.5	90.8	87.2	96.1
Exterior Adjusted	83.6	87.1	88.5	84.8	81.2	90.1
Interior Background	32.1	27.4	21.1	19.3	16.9	25.8
Interior Measurement	63.7	62.0	62.3	59.6	54.8	64.8
Interior Adjusted	63.7	62.0	62.3	59.6	54.8	64.8
Noise Reduction	19.9	25.1	26.2	25.2	26.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.4	32.0	38.9	41.4	35.4	44.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						25.6 dB

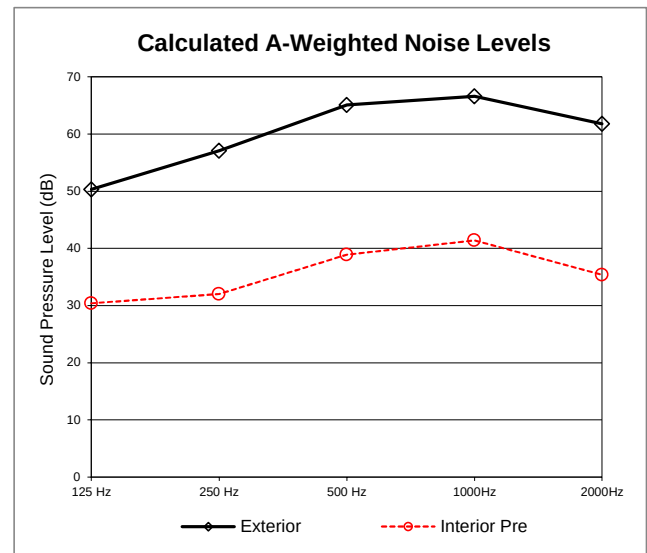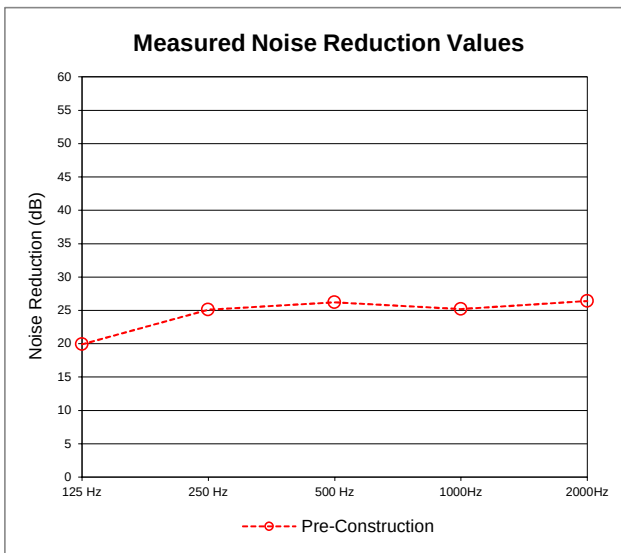



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Nguyen
 Address: 11248 20th Ave S
 Local City: Burien

Tested Room: Living / Dining Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.2	52.6	51.0	49.1	42.1	52.9
Exterior Measurement (flush)	87.7	89.6	92.1	87.5	82.1	92.7
Exterior Adjusted	81.7	83.6	86.1	81.5	76.1	86.7
Interior Background	35.1	27.2	23.4	21.6	18.5	27.9
Interior Measurement	61.2	54.8	51.5	48.2	45.4	55.2
Interior Adjusted	61.2	54.8	51.5	48.2	45.4	55.2
Noise Reduction	20.5	28.8	34.6	33.3	30.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.8	28.3	30.5	33.3	31.1	37.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.1 dB

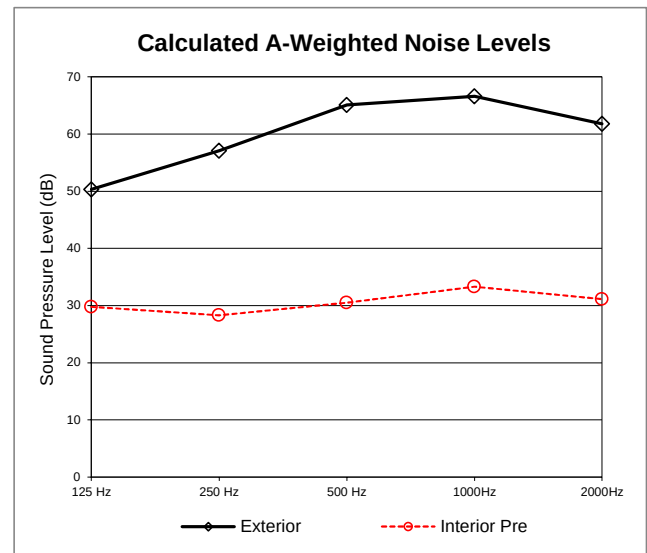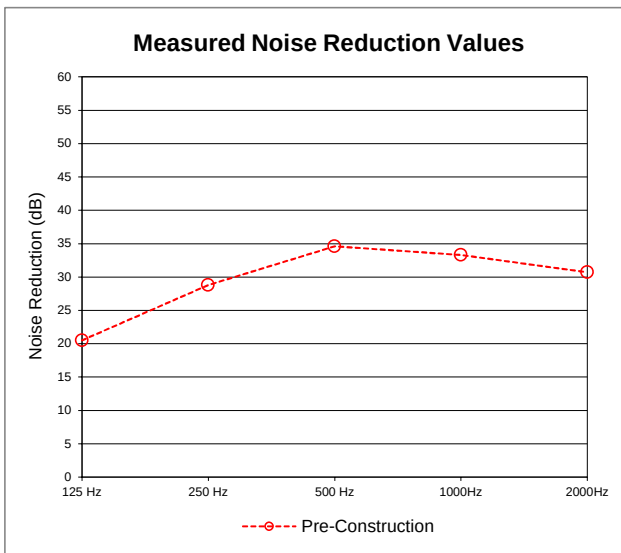



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Nguyen
 Address: 11248 20th Ave S
 Local City: Burien

Tested Room: Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.0	63.7	62.0	59.9	52.8	63.7
Exterior Measurement (flush)	100.9	99.5	100.9	95.5	91.5	101.6
Exterior Adjusted	94.9	93.5	94.9	89.5	85.5	95.6
Interior Background	34.7	30.9	28.0	23.8	19.5	30.4
Interior Measurement	72.8	65.6	62.8	54.3	51.9	63.5
Interior Adjusted	72.8	65.6	62.8	54.3	51.9	63.5
Noise Reduction	22.1	27.9	32.1	35.2	33.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.2	29.2	33.0	31.4	28.2	37.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.6 dB

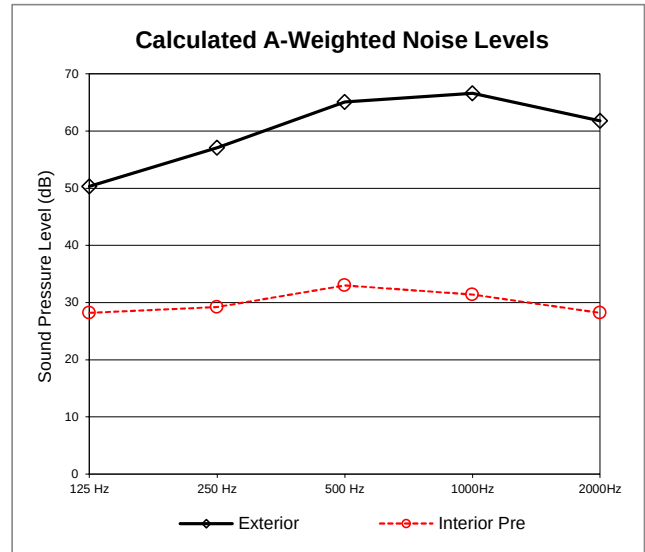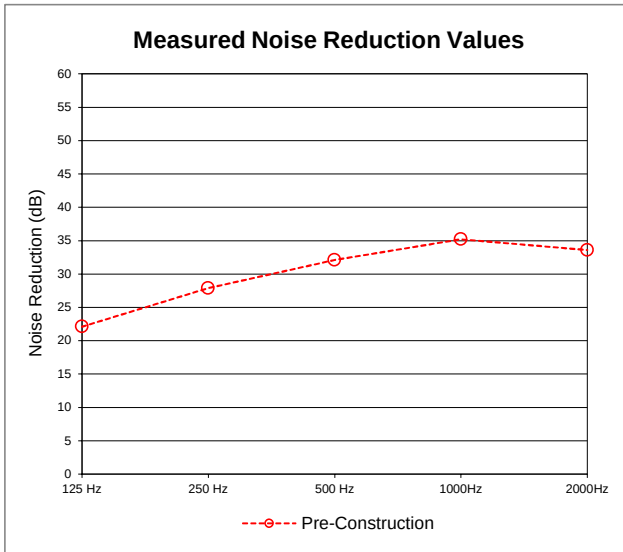



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Nguyen
 Address: 11248 20th Ave S
 Local City: Burien

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.1	55.3	55.0	52.1	45.9	56.3
Exterior Measurement (flush)	85.0	86.2	86.9	84.9	81.6	90.2
Exterior Adjusted	79.0	80.2	80.9	78.9	75.6	84.2
Interior Background	32.8	23.6	12.2	13.9	14.0	23.2
Interior Measurement	57.0	44.5	40.4	37.5	36.3	46.0
Interior Adjusted	57.0	44.5	40.4	37.5	36.3	46.0
Noise Reduction	22.0	35.7	40.5	41.4	39.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.3	21.4	24.6	25.2	22.5	32.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						37.9 dB

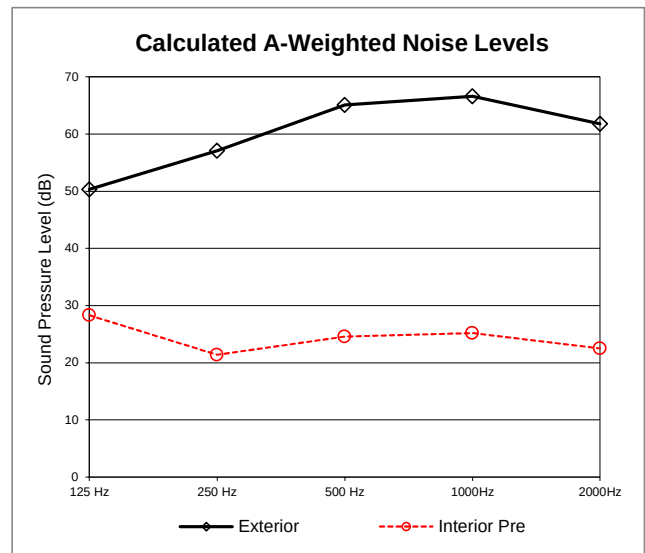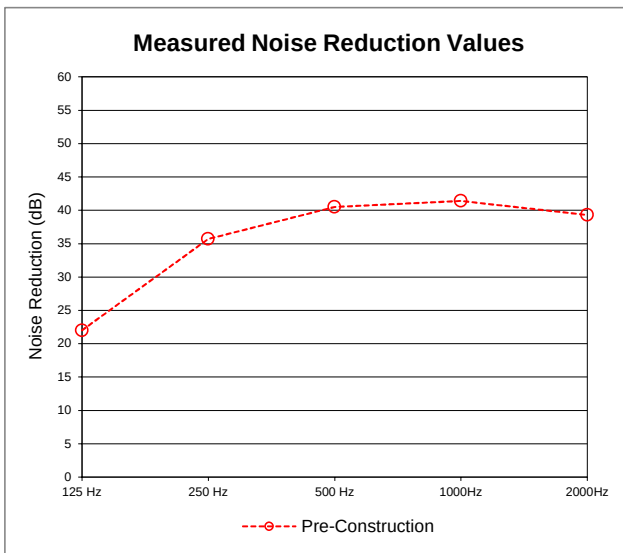



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Nguyen
 Address: 11248 20th Ave S
 Local City: Burien

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.1	55.3	55.0	52.1	45.9	56.3
Exterior Measurement (flush)	84.1	81.1	85.9	82.6	79.9	87.9
Exterior Adjusted	78.1	75.1	79.9	76.6	73.9	81.9
Interior Background	31.3	24.8	19.2	18.4	16.7	25.4
Interior Measurement	54.9	43.9	38.0	31.9	30.4	42.7
Interior Adjusted	54.9	43.8	37.9	31.7	30.2	42.6
Noise Reduction	23.2	31.3	42.0	44.9	43.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.1	25.8	23.1	21.7	18.1	31.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						38.8 dB

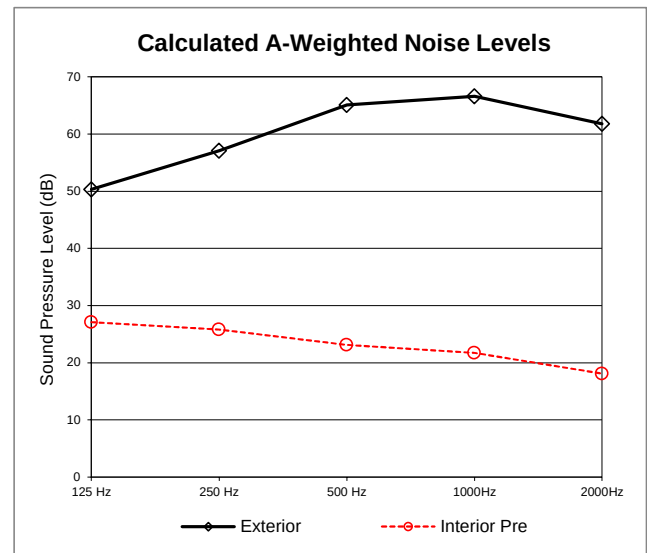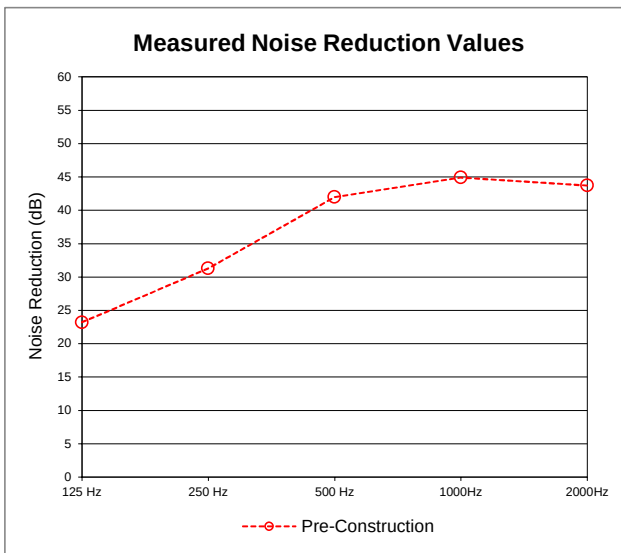



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.1	58.6	54.2	52.5	49.8	57.9
Exterior Measurement (flush)	90.6	92.5	92.0	90.1	85.0	94.4
Exterior Adjusted	84.6	86.5	86.0	84.1	79.0	88.4
Interior Background	48.5	42.8	38.6	36.4	28.9	41.3
Interior Measurement	64.5	60.7	58.0	51.6	50.4	59.5
Interior Adjusted	64.4	60.6	57.9	51.5	50.4	59.4
Noise Reduction	20.2	25.9	28.1	32.6	28.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.1	31.2	37.0	34.0	33.2	40.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.2 dB

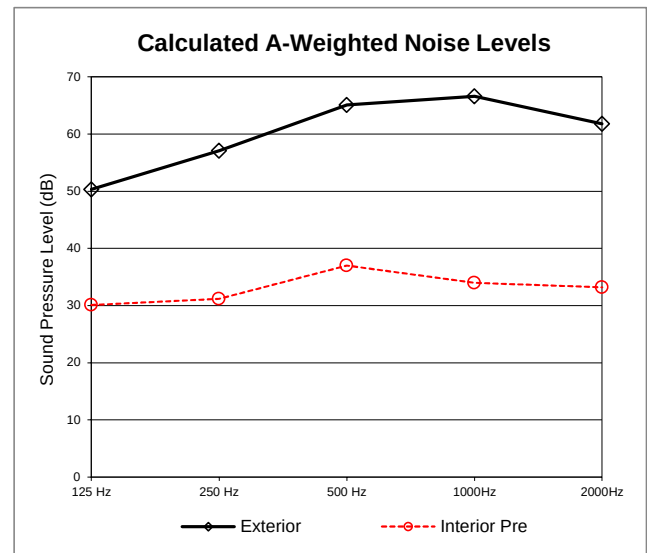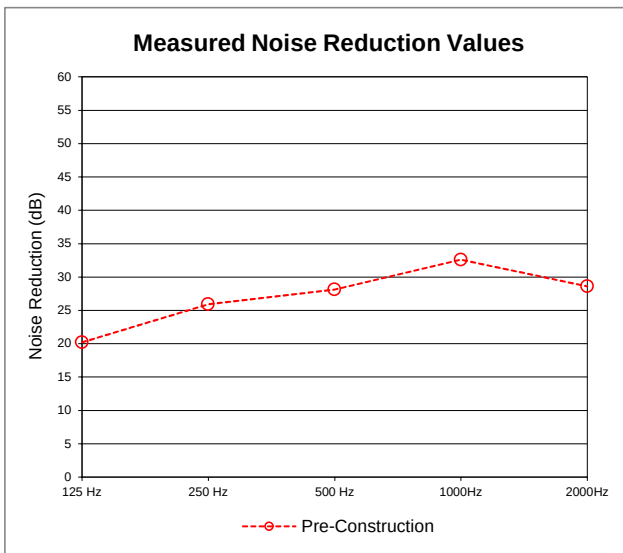



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Sitting Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.4	50.9	51.3	52.0	49.1	56.0
Exterior Measurement (flush)	92.8	91.9	93.5	88.9	86.9	95.4
Exterior Adjusted	86.8	85.9	87.5	82.9	80.9	89.4
Interior Background	38.2	30.3	24.1	20.4	18.5	28.8
Interior Measurement	68.0	66.4	61.6	58.0	56.1	64.4
Interior Adjusted	68.0	66.4	61.6	58.0	56.1	64.4
Noise Reduction	18.8	19.5	25.9	24.9	24.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.5	37.6	39.2	41.7	37.0	45.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						24.5 dB

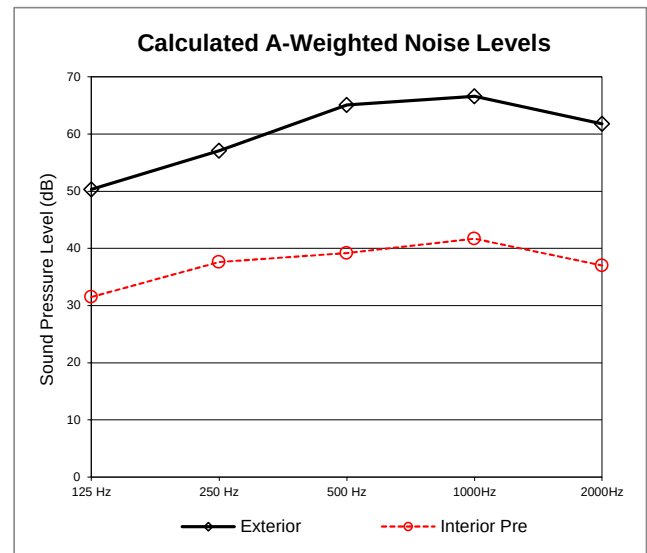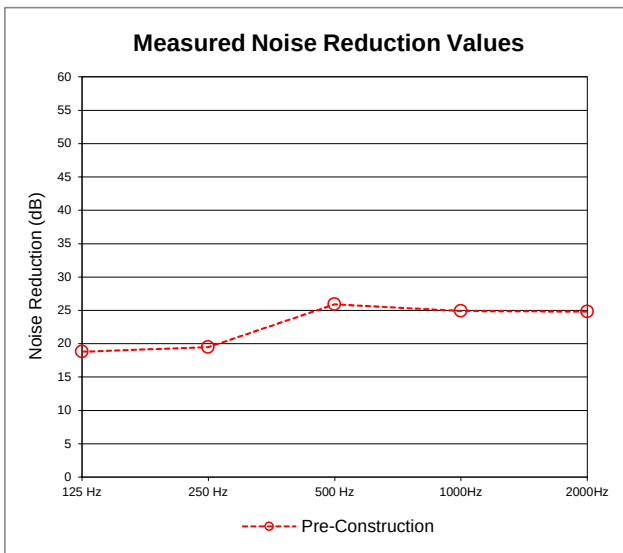



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Sitting Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.5	53.8	53.4	51.9	44.6	55.7
Exterior Measurement (flush)	110.0	107.3	108.6	102.1	97.6	108.9
Exterior Adjusted	104.0	101.3	102.6	96.1	91.6	102.9
Interior Background	38.2	30.3	24.1	20.4	18.5	28.8
Interior Measurement	79.5	65.5	60.1	48.8	40.9	65.3
Interior Adjusted	79.5	65.5	60.1	48.8	40.9	65.3
Noise Reduction	24.5	35.8	42.5	47.3	50.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	25.8	21.3	22.6	19.3	11.1	29.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.0 dB

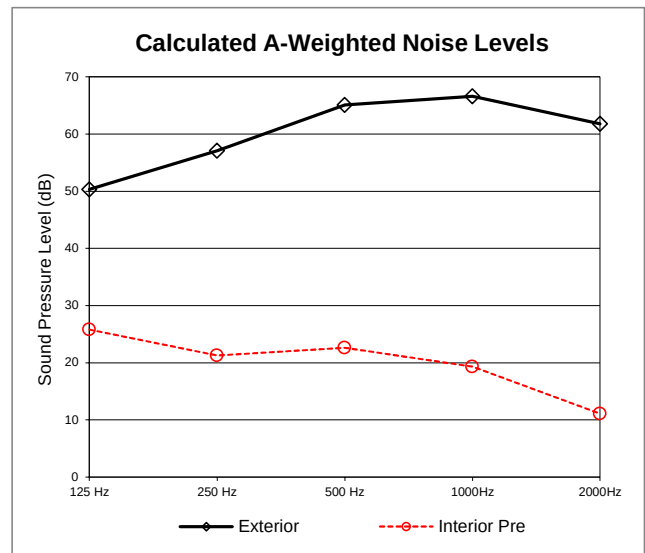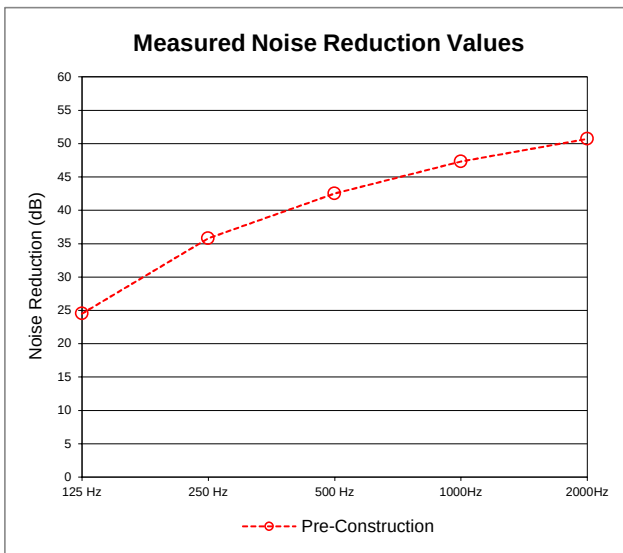

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Dining Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.4	50.9	51.3	52.0	49.1	56.0
Exterior Measurement (flush)	96.5	96.7	99.3	94.7	90.8	100.3
Exterior Adjusted	90.5	90.7	93.3	88.7	84.8	94.3
Interior Background	46.7	43.6	40.4	37.3	32.3	42.9
Interior Measurement	69.9	69.3	69.5	66.2	64.3	71.7
Interior Adjusted	69.9	69.3	69.5	66.2	64.3	71.7
Noise Reduction	20.6	21.4	23.8	22.5	20.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.7	35.7	41.3	44.1	41.3	47.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						22.4 dB

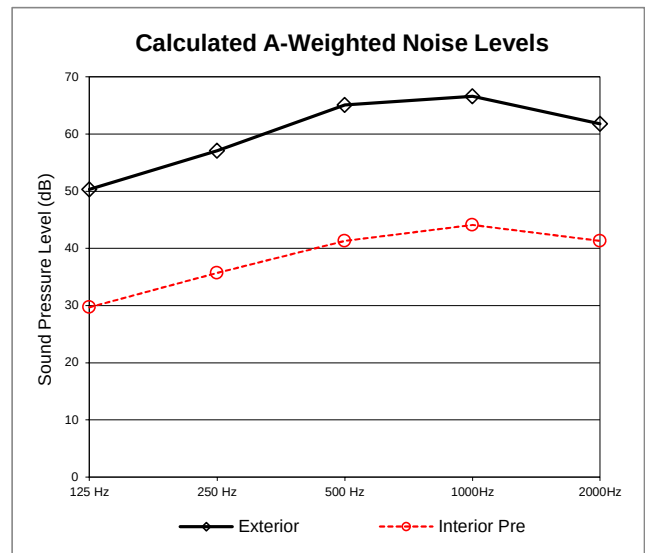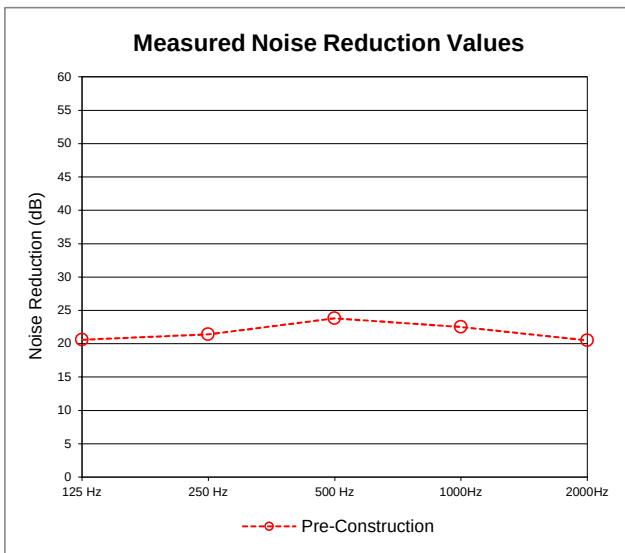



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.4	50.9	51.3	52.0	49.1	56.0
Exterior Measurement (flush)	98.5	98.8	100.3	95.4	91.4	101.4
Exterior Adjusted	92.5	92.8	94.3	89.4	85.4	95.4
Interior Background	41.9	39.6	38.0	33.7	29.0	39.4
Interior Measurement	68.6	65.6	62.6	51.7	47.2	62.5
Interior Adjusted	68.6	65.6	62.6	51.6	47.1	62.5
Noise Reduction	23.9	27.2	31.7	37.8	38.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.4	29.9	33.4	28.8	23.5	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

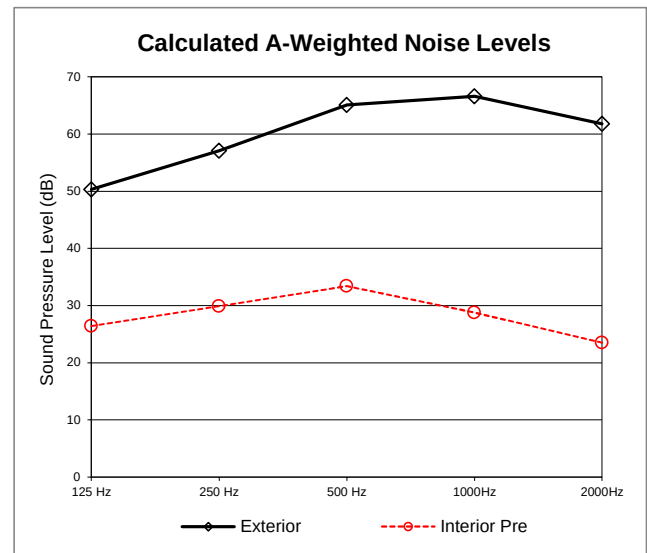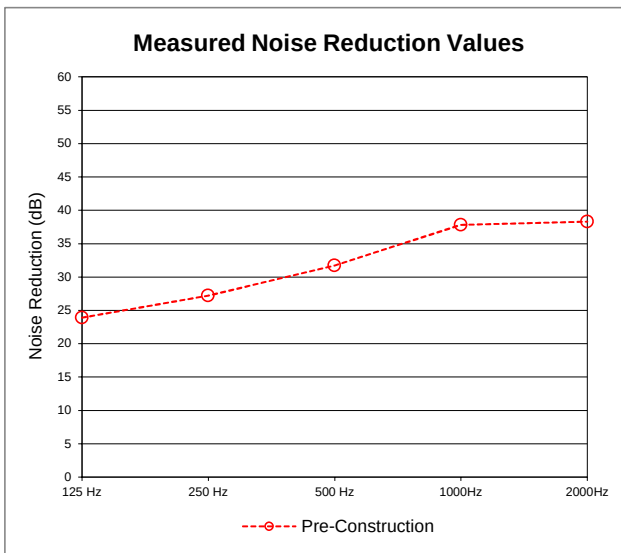



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.0	54.6	49.4	50.9	46.5	54.5
Exterior Measurement (flush)	90.0	94.9	95.0	90.1	87.7	96.4
Exterior Adjusted	84.0	88.9	89.0	84.1	81.7	90.4
Interior Background	37.8	34.0	27.5	21.8	18.5	30.7
Interior Measurement	66.5	62.1	59.2	51.6	46.0	59.7
Interior Adjusted	66.5	62.1	59.2	51.6	46.0	59.7
Noise Reduction	17.5	26.8	29.8	32.5	35.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.8	30.3	35.3	34.1	26.1	39.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.3 dB

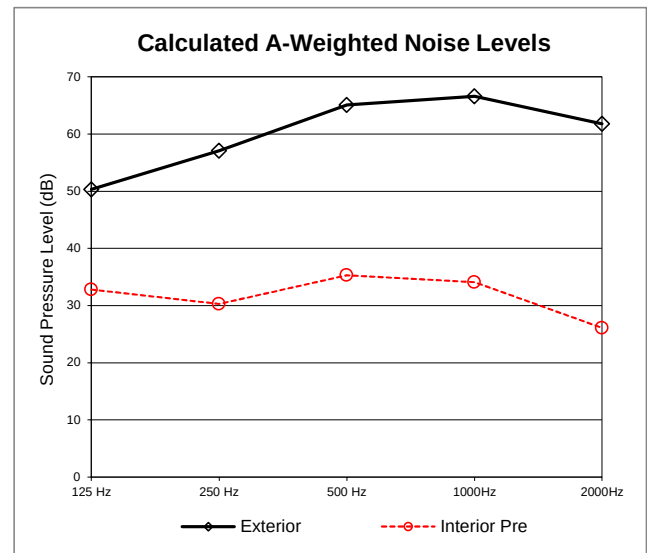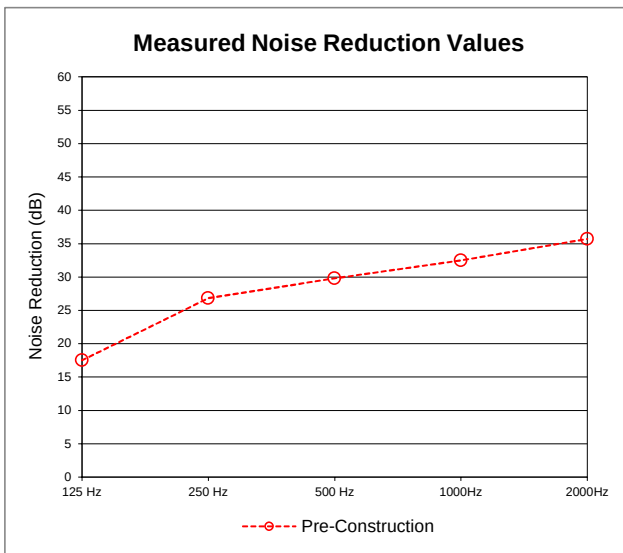

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA



Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.5	53.8	53.4	51.9	44.6	55.7
Exterior Measurement (flush)	87.2	84.3	87.6	84.8	81.9	89.8
Exterior Adjusted	81.2	78.3	81.6	78.8	75.9	83.8
Interior Background	32.0	29.5	34.0	24.7	19.5	32.4
Interior Measurement	63.4	48.8	45.8	36.8	28.3	49.1
Interior Adjusted	63.4	48.7	45.5	36.5	27.7	49.0
Noise Reduction	17.8	29.6	36.1	42.3	48.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.5	27.5	29.0	24.3	13.6	35.3

Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum): 34.7 dB

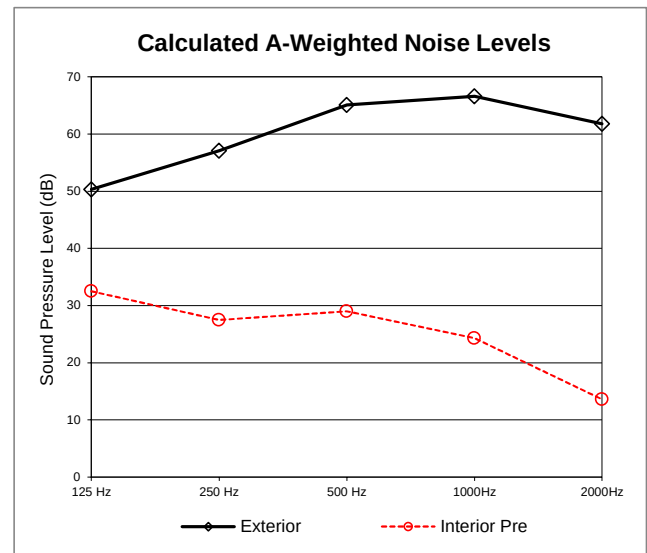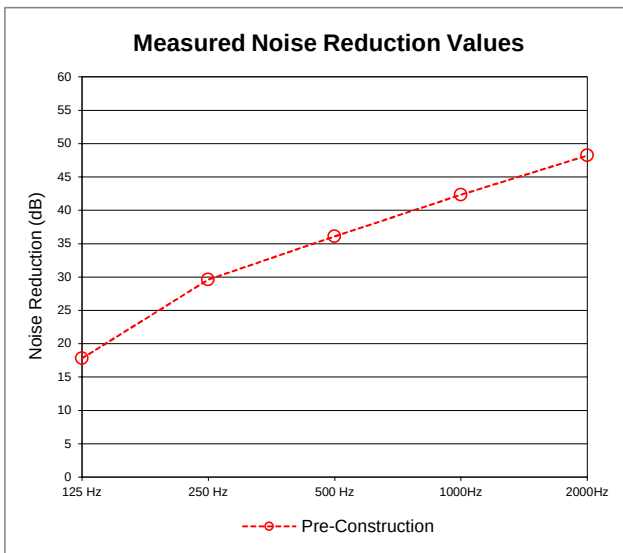



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Pond
 Address: 11254 20th Ave S
 Local City: Burien

Tested Room: Office Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 20, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.0	54.6	49.4	50.9	46.5	54.5
Exterior Measurement (flush)	94.3	93.8	98.2	92.8	88.4	98.5
Exterior Adjusted	88.3	87.8	92.2	86.8	82.4	92.5
Interior Background	34.7	30.8	24.3	17.7	20.7	28.1
Interior Measurement	68.5	61.1	60.1	49.9	37.6	59.6
Interior Adjusted	68.5	61.1	60.1	49.9	37.5	59.6
Noise Reduction	19.8	26.7	32.1	36.9	44.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.5	30.4	33.0	29.7	16.9	37.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.8 dB

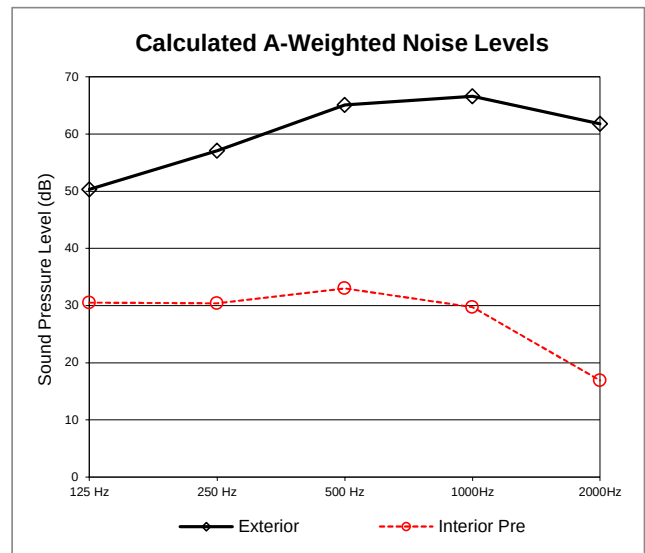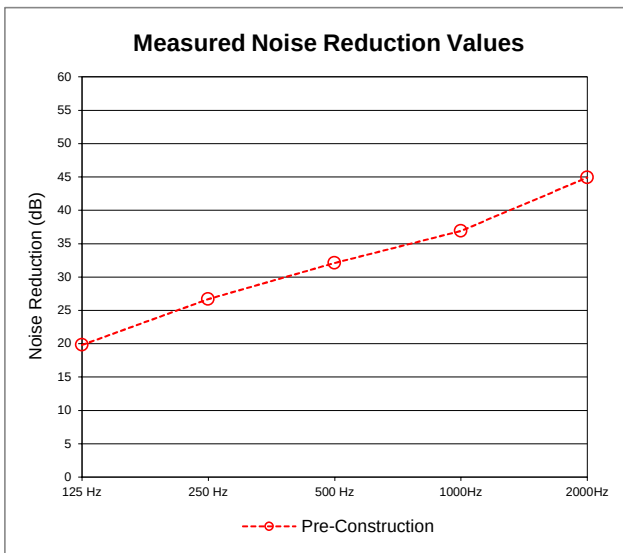

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	51.2	43.5	42.7	45.7	39.8	48.3
Exterior Measurement (flush)	89.8	88.7	92.5	87.4	85.7	94.2
Exterior Adjusted	83.8	82.7	86.5	81.4	79.7	88.2
Interior Background	41.0	40.5	33.1	22.6	18.1	35.1
Interior Measurement	68.5	57.1	53.0	49.0	41.4	56.3
Interior Adjusted	68.5	57.0	53.0	49.0	41.4	56.3
Noise Reduction	15.3	25.7	33.5	32.4	38.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.0	31.4	31.6	34.2	23.5	39.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.5 dB

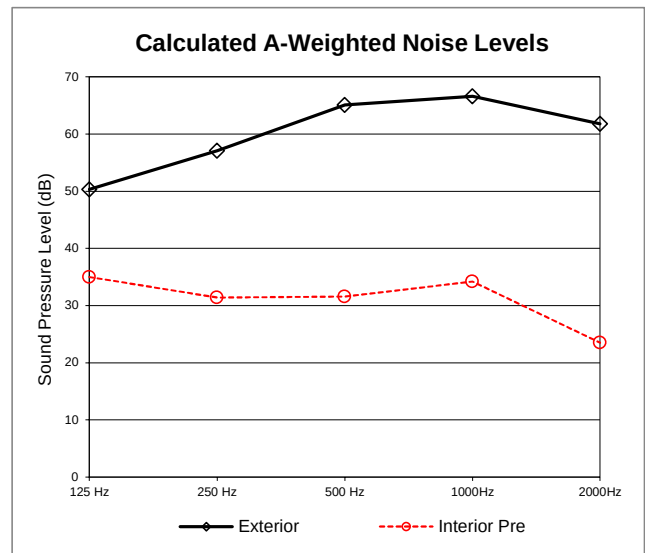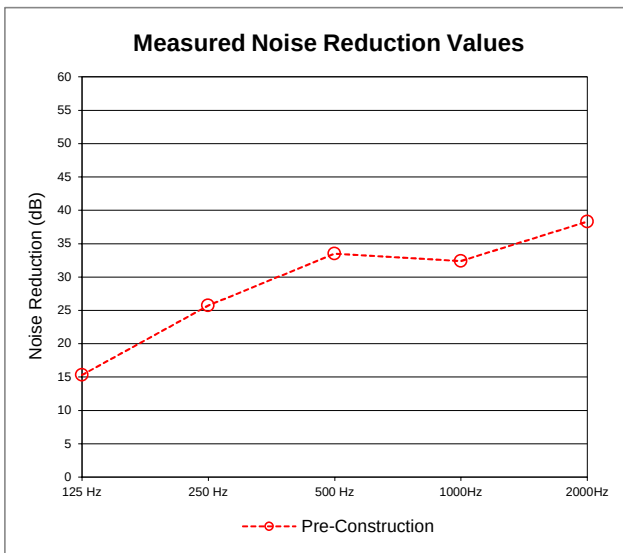

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade 1
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.3	47.4	46.3	45.8	40.3	49.6
Exterior Measurement (flush)	109.2	107.5	107.8	103.4	101.8	109.5
Exterior Adjusted	103.2	101.5	101.8	97.4	95.8	103.5
Interior Background	37.1	32.5	25.2	20.9	16.9	28.6
Interior Measurement	76.7	66.0	59.6	50.2	42.5	63.2
Interior Adjusted	76.7	66.0	59.6	50.2	42.5	63.2
Noise Reduction	26.5	35.5	42.2	47.2	53.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	23.8	21.6	22.9	19.4	8.5	28.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.7 dB

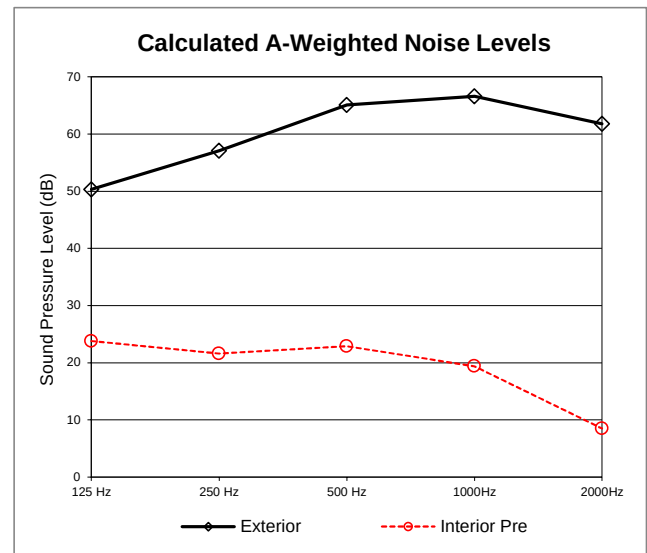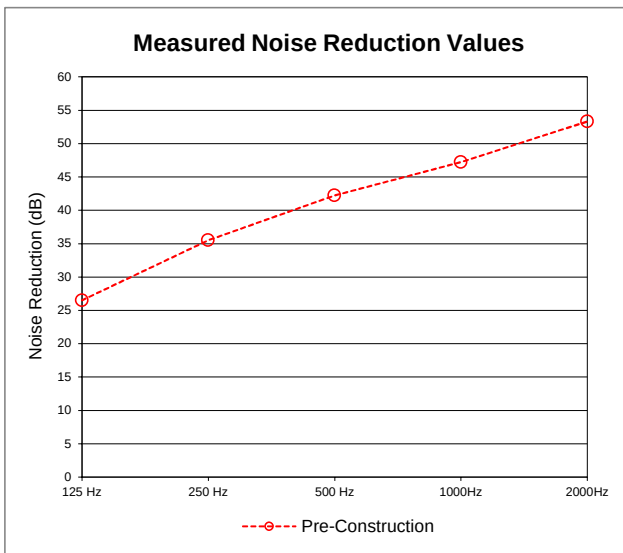

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	44.7	41.3	41.3	40.3	31.6	44.0
Exterior Measurement (flush)	91.9	88.7	91.3	86.4	81.2	92.0
Exterior Adjusted	85.9	82.7	85.3	80.4	75.2	86.0
Interior Background	37.1	32.5	25.2	20.9	16.9	28.6
Interior Measurement	68.3	60.8	56.9	49.9	42.7	58.4
Interior Adjusted	68.3	60.8	56.9	49.9	42.7	58.4
Noise Reduction	17.6	21.9	28.4	30.5	32.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.7	35.2	36.7	36.1	29.3	41.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.3 dB

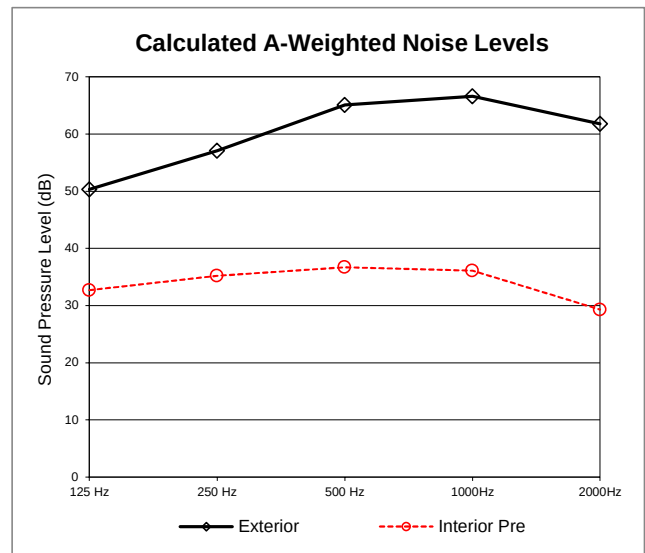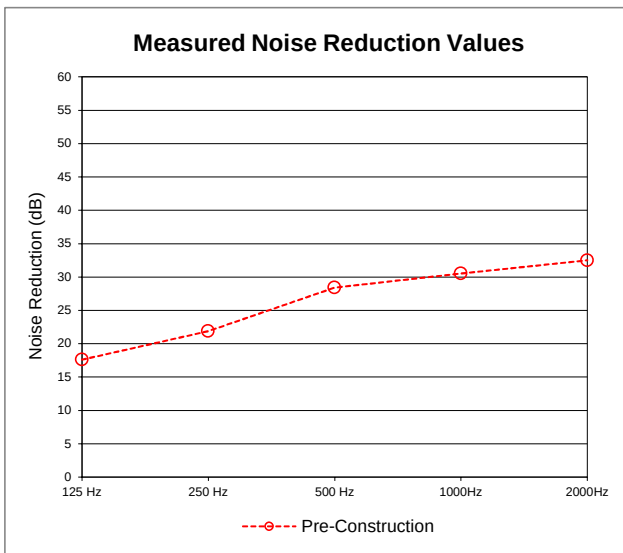

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Dining Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	44.7	41.3	41.3	40.3	31.6	44.0
Exterior Measurement (flush)	89.4	91.8	92.2	87.0	84.5	93.4
Exterior Adjusted	83.4	85.8	86.2	81.0	78.5	87.4
Interior Background	36.2	39.9	31.8	29.0	21.8	34.7
Interior Measurement	66.4	59.0	54.7	47.1	39.3	56.2
Interior Adjusted	66.4	58.9	54.7	47.0	39.2	56.2
Noise Reduction	17.0	26.9	31.5	34.0	39.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.3	30.2	33.6	32.6	22.5	38.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.3 dB

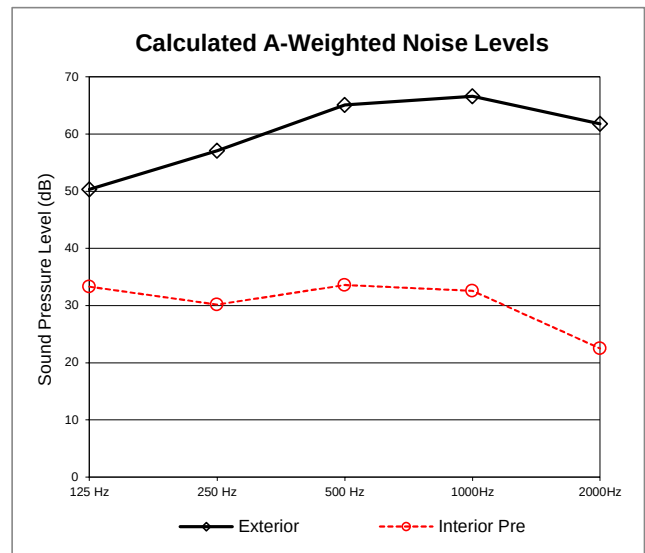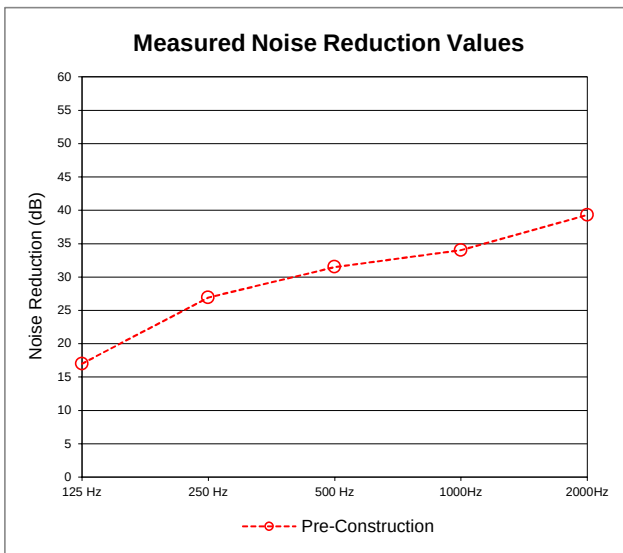



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	44.7	41.3	41.3	40.3	31.6	44.0
Exterior Measurement (flush)	90.6	91.5	90.9	84.9	81.6	91.7
Exterior Adjusted	84.6	85.5	84.9	78.9	75.6	85.7
Interior Background	40.7	43.0	35.4	31.6	24.6	37.8
Interior Measurement	65.1	56.6	53.4	46.7	37.9	54.7
Interior Adjusted	65.1	56.4	53.3	46.6	37.7	54.6
Noise Reduction	19.5	29.1	31.6	32.3	37.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.8	28.0	33.5	34.3	23.9	38.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.5 dB

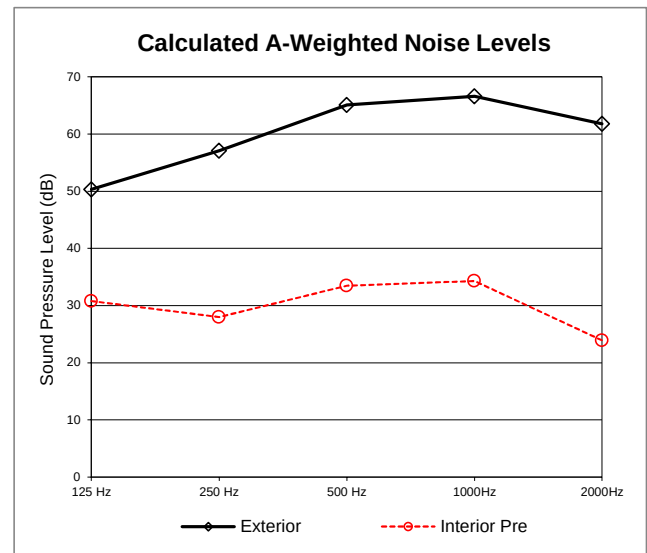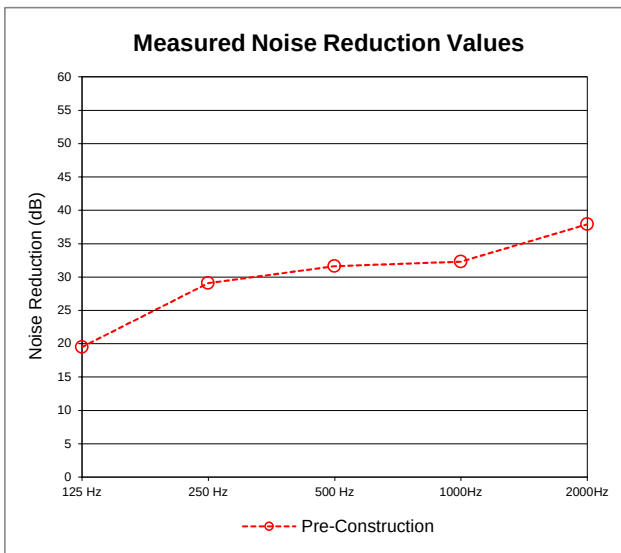



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.8	57.8	56.3	51.0	44.2	56.5
Exterior Measurement (flush)	92.7	95.4	95.7	92.0	88.7	98.3
Exterior Adjusted	86.7	89.4	89.7	86.0	82.7	92.3
Interior Background	30.9	23.6	17.0	11.0	11.0	22.5
Interior Measurement	63.3	54.5	48.3	41.4	34.7	51.4
Interior Adjusted	63.3	54.5	48.3	41.4	34.7	51.4
Noise Reduction	23.4	34.9	41.4	44.6	48.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.9	22.2	23.7	22.0	13.8	30.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						39.7 dB

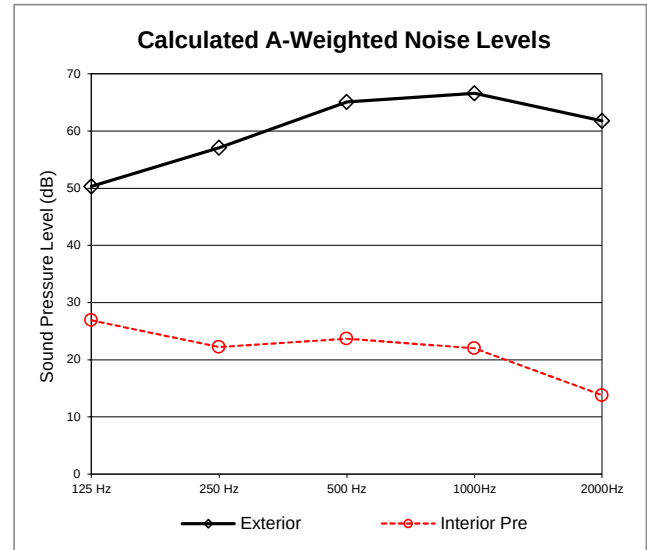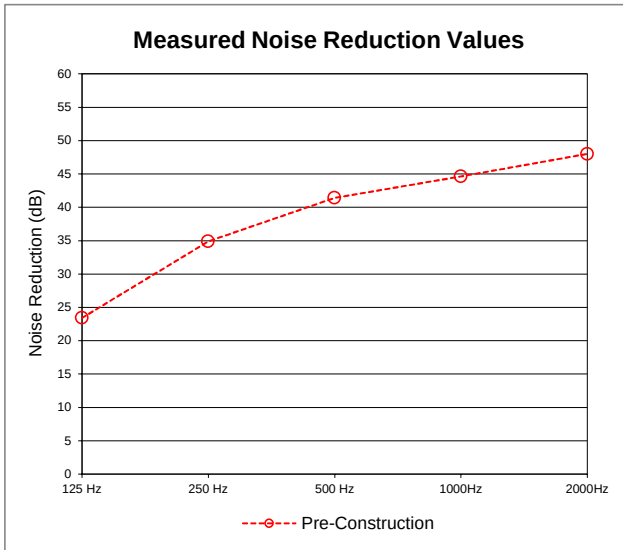

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	51.2	43.5	42.7	45.7	39.8	48.3
Exterior Measurement (flush)	90.2	87.8	91.1	89.0	83.6	93.6
Exterior Adjusted	84.2	81.8	85.1	83.0	77.6	87.6
Interior Background	48.3	38.6	38.6	31.3	26.7	39.4
Interior Measurement	66.8	59.2	55.3	52.1	54.0	59.5
Interior Adjusted	66.7	59.2	55.2	52.1	54.0	59.5
Noise Reduction	17.5	22.6	29.9	30.9	23.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.8	34.5	35.2	35.7	38.2	42.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						27.4 dB

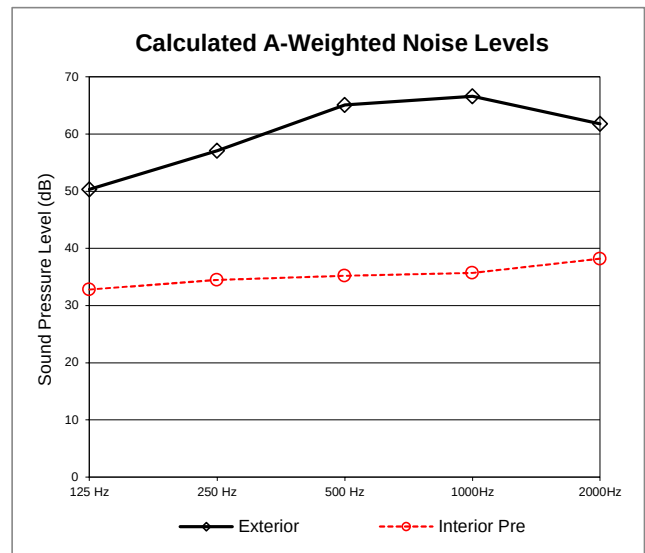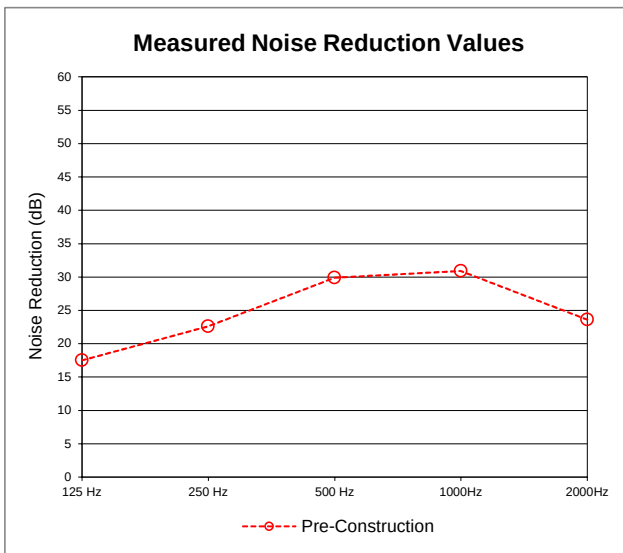

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gilderoy
 Address: 23019 20th Ave S
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	51.2	43.5	42.7	45.7	39.8	48.3
Exterior Measurement (flush)	91.0	89.8	91.6	90.6	87.7	95.2
Exterior Adjusted	85.0	83.8	85.6	84.6	81.7	89.2
Interior Background	44.2	40.3	33.0	23.0	18.8	35.3
Interior Measurement	65.8	52.0	48.2	39.7	34.9	51.5
Interior Adjusted	65.8	51.7	48.1	39.6	34.8	51.4
Noise Reduction	19.2	32.1	37.5	45.0	46.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.1	25.0	27.6	21.6	14.9	33.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.3 dB

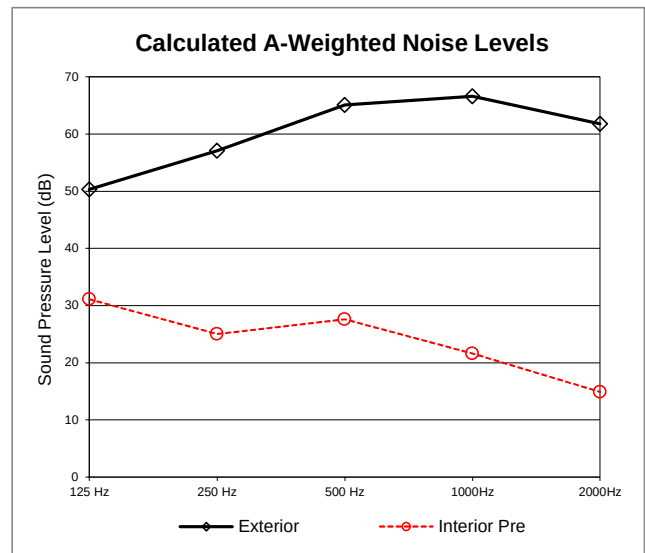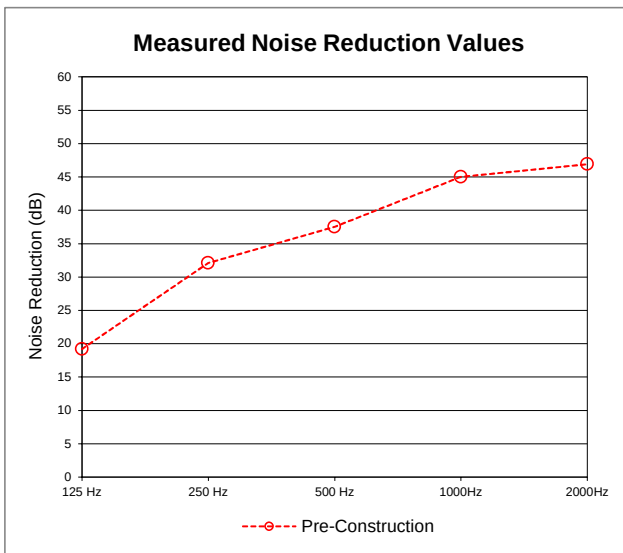



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	51.5	49.1	45.8	37.8	50.8
Exterior Measurement (flush)	87.0	89.8	89.3	86.8	85.1	93.0
Exterior Adjusted	81.0	83.8	83.3	80.8	79.1	87.0
Interior Background	37.5	27.9	25.0	24.4	19.6	29.8
Interior Measurement	63.7	57.7	55.7	48.6	47.9	56.9
Interior Adjusted	63.7	57.7	55.7	48.6	47.9	56.9
Noise Reduction	17.3	26.1	27.6	32.2	31.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.0	31.0	37.5	34.4	30.6	41.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.9 dB

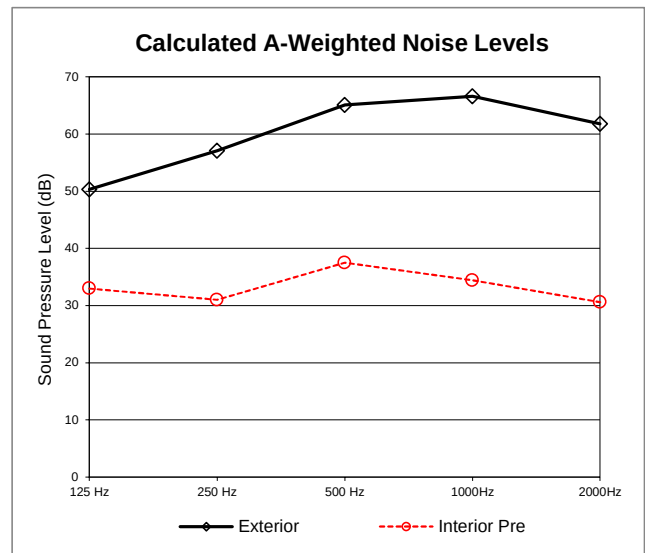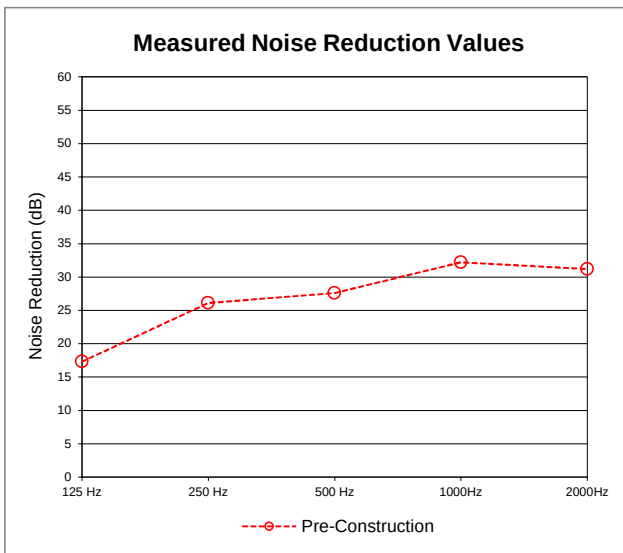



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Family Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	51.5	49.1	45.8	37.8	50.8
Exterior Measurement (flush)	92.9	88.1	87.9	86.9	83.4	93.0
Exterior Adjusted	86.9	82.1	81.9	80.9	77.4	87.0
Interior Background	43.8	40.0	31.3	23.8	14.3	35.5
Interior Measurement	64.5	53.5	50.5	43.0	38.2	52.5
Interior Adjusted	64.5	53.3	50.4	42.9	38.2	52.4
Noise Reduction	22.4	28.8	31.5	38.0	39.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.9	28.3	33.6	28.6	22.6	36.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.5 dB

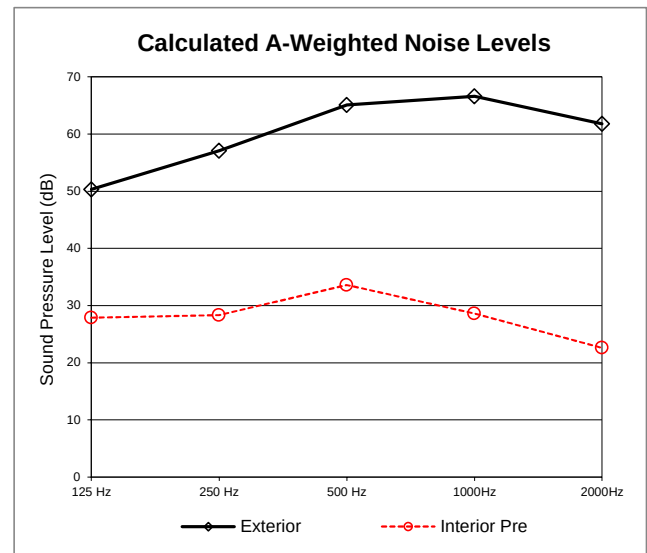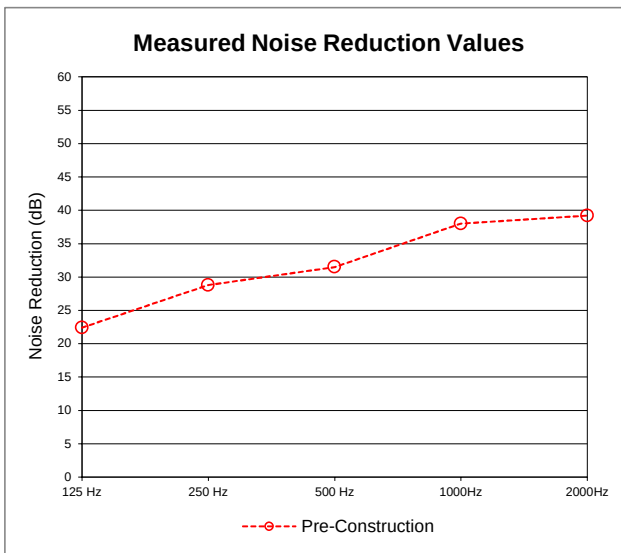

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.6	58.6	51.5	45.4	41.3	54.8
Exterior Measurement (flush)	98.6	99.3	99.4	95.7	92.5	102.3
Exterior Adjusted	92.6	93.3	93.4	89.7	86.5	96.3
Interior Background	39.0	32.9	27.6	24.2	22.9	32.1
Interior Measurement	67.9	69.0	61.8	52.9	44.8	63.5
Interior Adjusted	67.9	69.0	61.8	52.9	44.8	63.5
Noise Reduction	24.7	24.3	31.6	36.8	41.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	25.6	32.8	33.5	29.8	20.1	37.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.5 dB

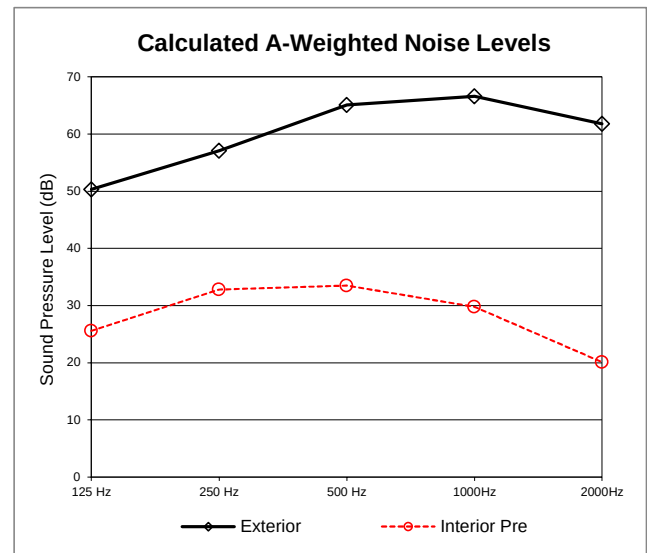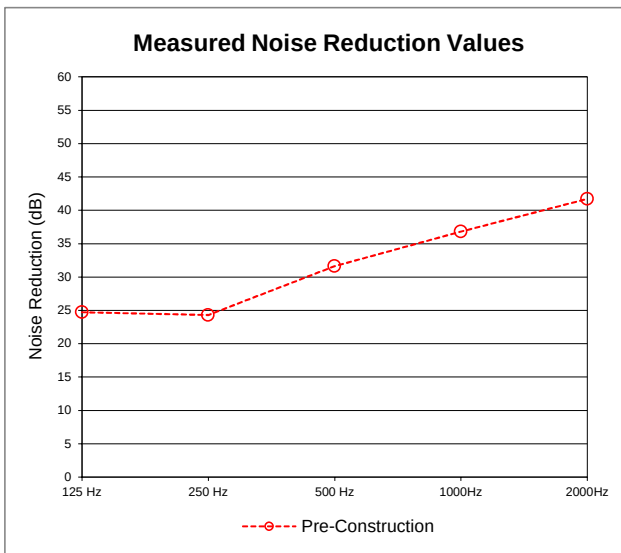



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Dining Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.6	58.6	51.5	45.4	41.3	54.8
Exterior Measurement (flush)	96.1	94.5	95.6	94.6	91.5	99.3
Exterior Adjusted	90.1	88.5	89.6	88.6	85.5	93.3
Interior Background	38.5	27.5	24.6	19.2	15.7	28.9
Interior Measurement	68.4	59.4	54.4	47.2	43.3	56.9
Interior Adjusted	68.4	59.4	54.4	47.2	43.3	56.9
Noise Reduction	21.7	29.1	35.2	41.4	42.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.6	28.0	29.9	25.2	19.6	34.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.6 dB

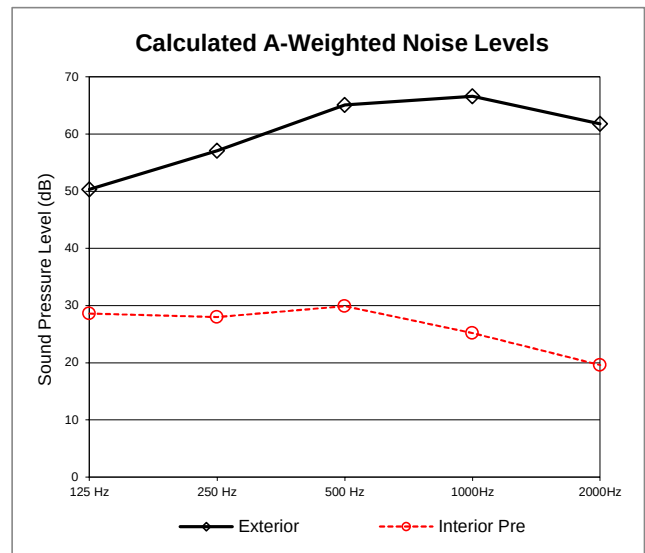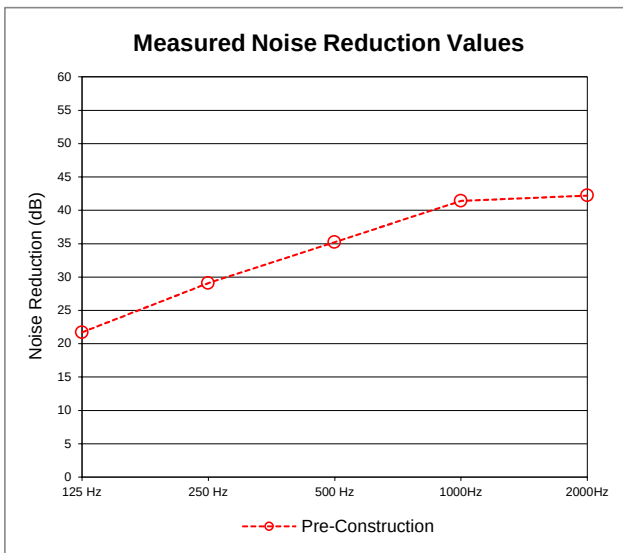



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Kitchen 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.6	58.6	51.5	45.4	41.3	54.8
Exterior Measurement (flush)	95.2	95.4	95.3	94.0	90.9	99.2
Exterior Adjusted	89.2	89.4	89.3	88.0	84.9	93.2
Interior Background	44.7	39.8	34.6	29.3	25.2	37.0
Interior Measurement	68.0	60.5	56.6	52.9	52.6	59.7
Interior Adjusted	68.0	60.5	56.6	52.9	52.6	59.7
Noise Reduction	21.2	28.9	32.7	35.1	32.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.1	28.2	32.4	31.5	29.5	37.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.6 dB

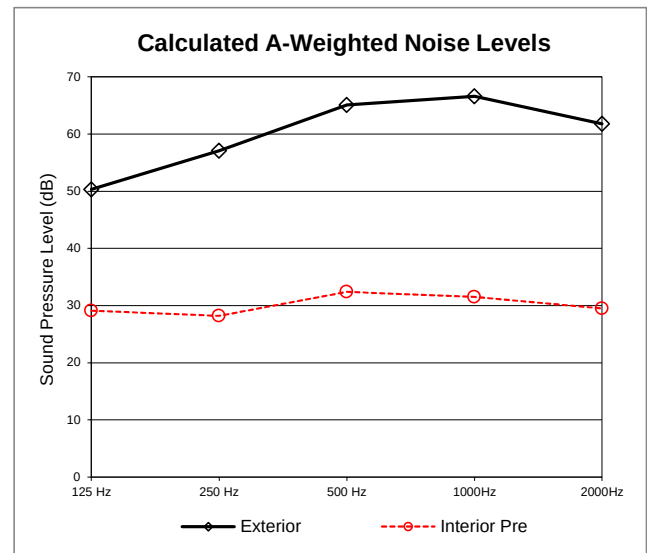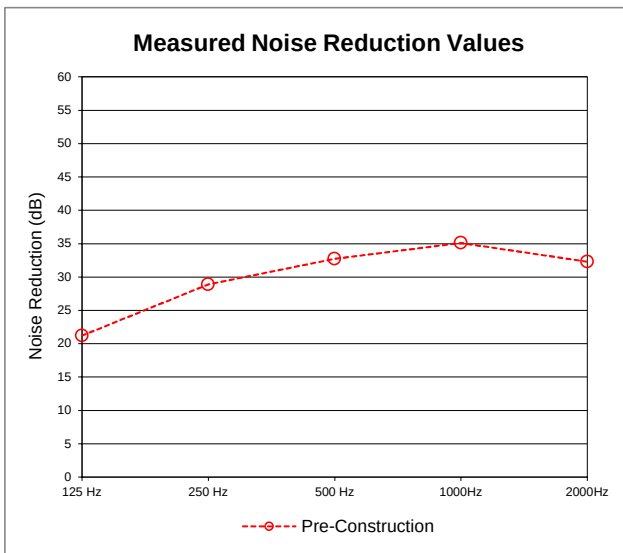



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Kitchen 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.6	58.6	51.5	45.4	41.3	54.8
Exterior Measurement (flush)	98.6	99.3	99.4	95.7	92.5	102.3
Exterior Adjusted	92.6	93.3	93.4	89.7	86.5	96.3
Interior Background	39.0	32.9	27.6	24.2	22.9	32.1
Interior Measurement	67.9	69.0	61.8	52.9	44.8	63.5
Interior Adjusted	67.9	69.0	61.8	52.9	44.8	63.5
Noise Reduction	24.7	24.3	31.6	36.8	41.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	25.6	32.8	33.5	29.8	20.1	37.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.5 dB

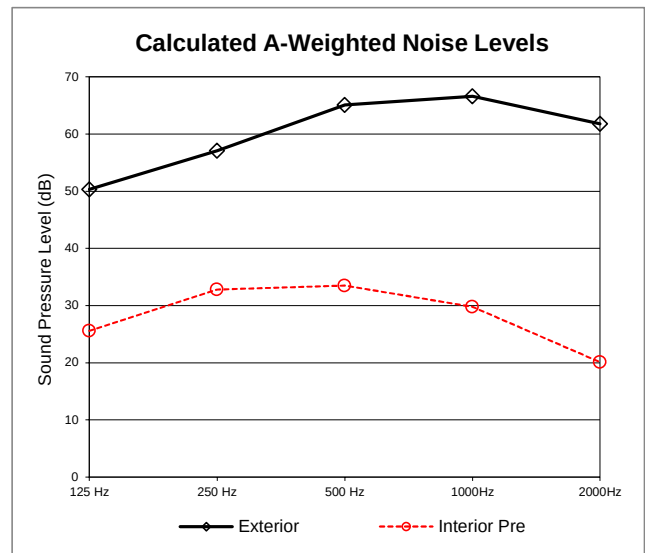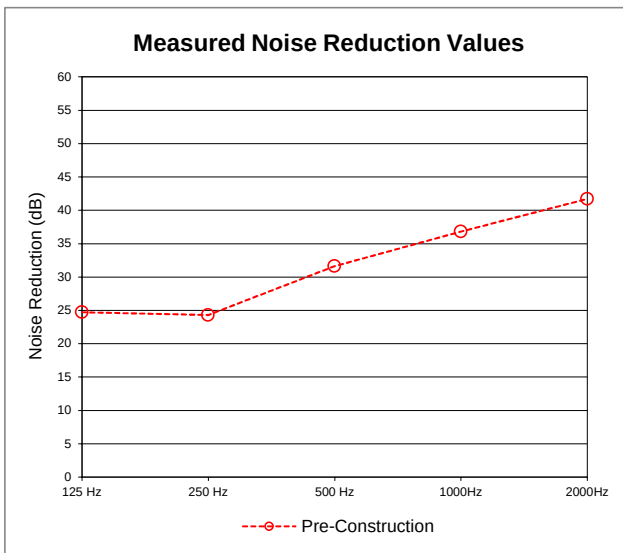



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.6	58.6	51.5	45.4	41.3	54.8
Exterior Measurement (flush)	95.6	94.1	94.6	90.4	87.4	96.6
Exterior Adjusted	89.6	88.1	88.6	84.4	81.4	90.6
Interior Background	36.4	26.7	23.4	20.1	16.6	27.4
Interior Measurement	66.5	58.0	52.9	45.4	44.5	55.5
Interior Adjusted	66.5	58.0	52.9	45.4	44.5	55.5
Noise Reduction	23.1	30.1	35.7	39.0	36.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.2	27.0	29.4	27.6	24.9	34.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.6 dB

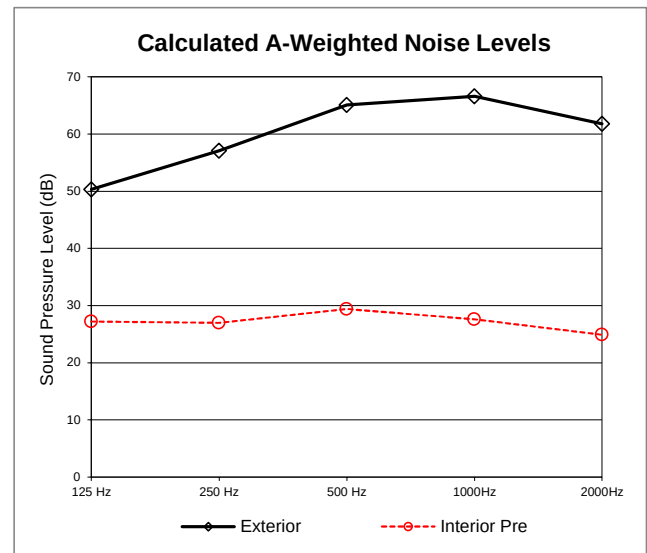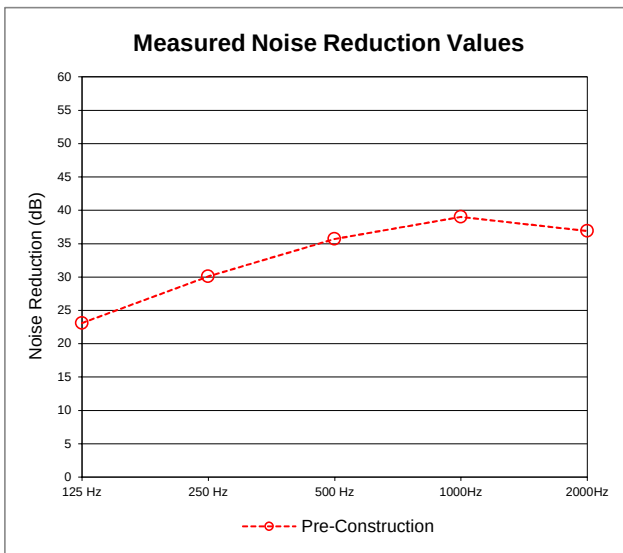



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	51.5	49.1	45.8	37.8	50.8
Exterior Measurement (flush)	91.7	89.3	91.1	88.3	87.2	94.4
Exterior Adjusted	85.7	83.3	85.1	82.3	81.2	88.4
Interior Background	30.7	24.8	17.6	14.9	15.6	24.4
Interior Measurement	59.3	52.2	48.3	42.4	37.2	50.0
Interior Adjusted	59.3	52.2	48.3	42.4	37.2	50.0
Noise Reduction	26.4	31.1	36.8	39.9	44.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	23.9	26.0	28.3	26.7	17.8	32.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						37.3 dB

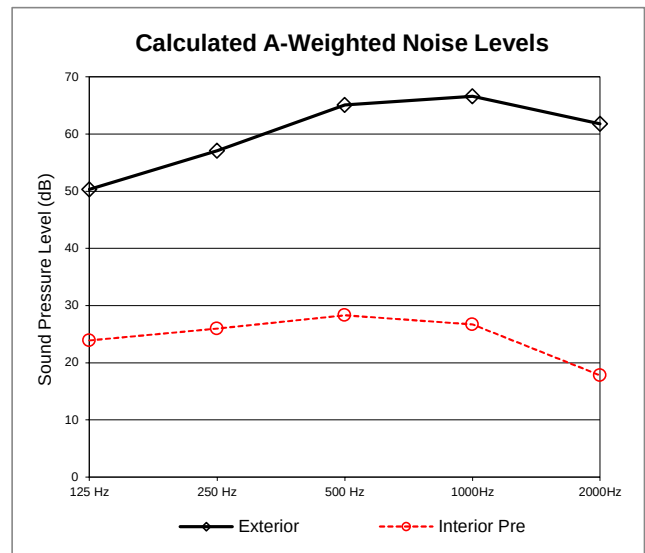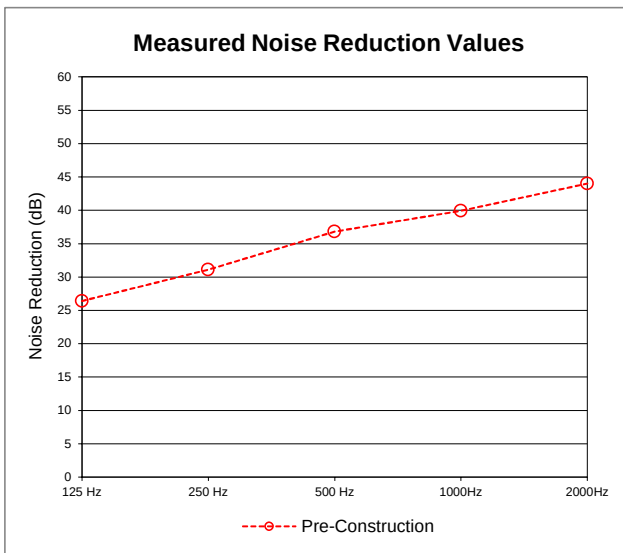



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Layer
 Address: 23147 20th Ave S
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	51.5	49.1	45.8	37.8	50.8
Exterior Measurement (flush)	91.7	92.0	92.8	90.5	89.5	96.2
Exterior Adjusted	85.7	86.0	86.8	84.5	83.5	90.2
Interior Background	33.0	29.3	20.9	18.1	18.1	27.5
Interior Measurement	64.7	56.3	51.3	44.8	43.0	54.1
Interior Adjusted	64.7	56.3	51.3	44.8	43.0	54.1
Noise Reduction	21.0	29.7	35.5	39.7	40.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.3	27.4	29.6	26.9	21.3	34.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.3 dB

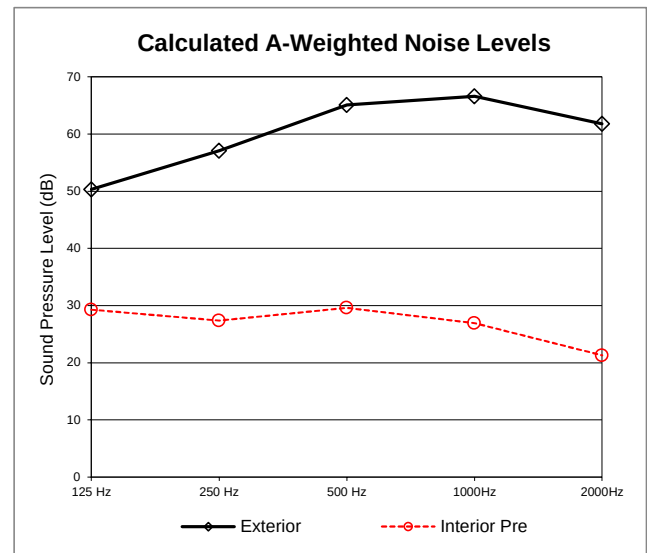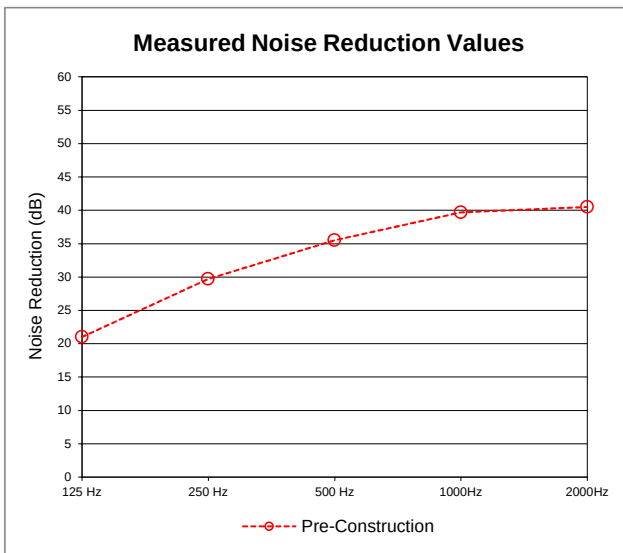



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Dustan
 Address: 12854 23rd Ave S
 Local City: SeaTac

Tested Room: Living / Kitchen Façade 1
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	61.6	60.1	59.2	56.6	46.1	60.4
Exterior Measurement (flush)	96.5	98.0	98.0	92.4	88.7	99.0
Exterior Adjusted	90.5	92.0	92.0	86.4	82.7	93.0
Interior Background	35.1	34.6	28.8	26.3	27.9	36.2
Interior Measurement	66.5	62.5	57.7	50.3	47.3	59.5
Interior Adjusted	66.5	62.5	57.7	50.3	47.2	59.5
Noise Reduction	24.0	29.5	34.3	36.1	35.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.3	27.6	30.8	30.5	26.3	35.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.3 dB

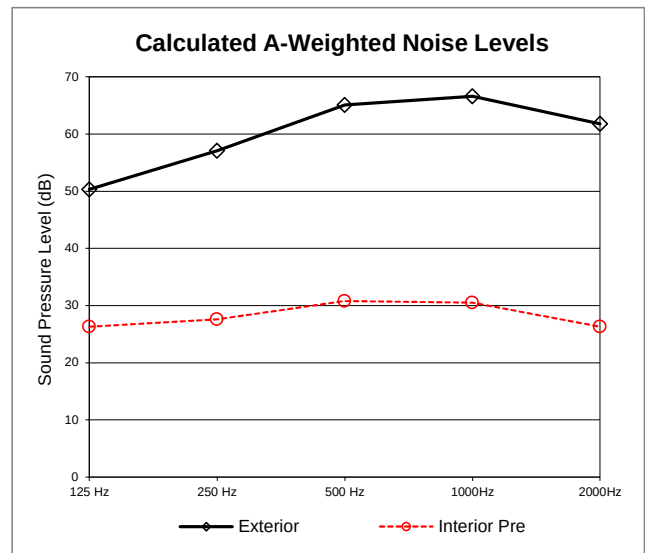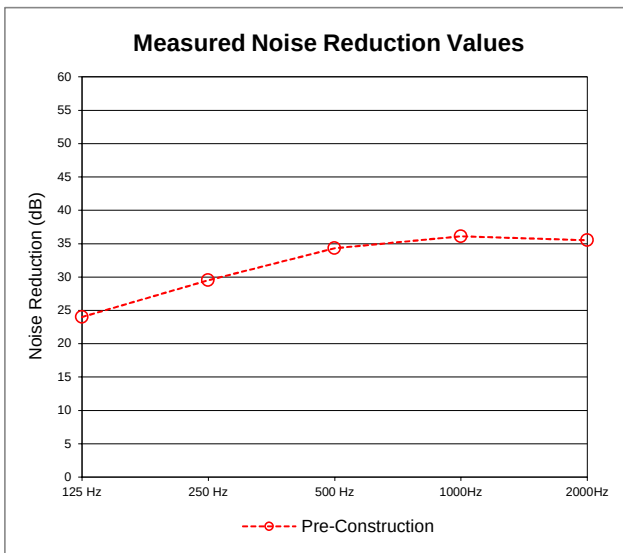

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Dustan
 Address: 12854 23rd Ave S
 Local City: SeaTac

Tested Room: Living / Kitchen Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	61.6	56.9	54.0	51.4	41.6	55.8
Exterior Measurement (flush)	97.6	95.3	96.1	91.3	88.5	97.8
Exterior Adjusted	91.6	89.3	90.1	85.3	82.5	91.8
Interior Background	35.1	34.6	28.8	26.3	27.9	36.2
Interior Measurement	68.3	62.3	58.5	47.7	38.9	59.0
Interior Adjusted	68.3	62.3	58.5	47.7	38.5	59.0
Noise Reduction	23.3	27.0	31.6	37.6	44.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.0	30.1	33.5	29.0	17.8	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

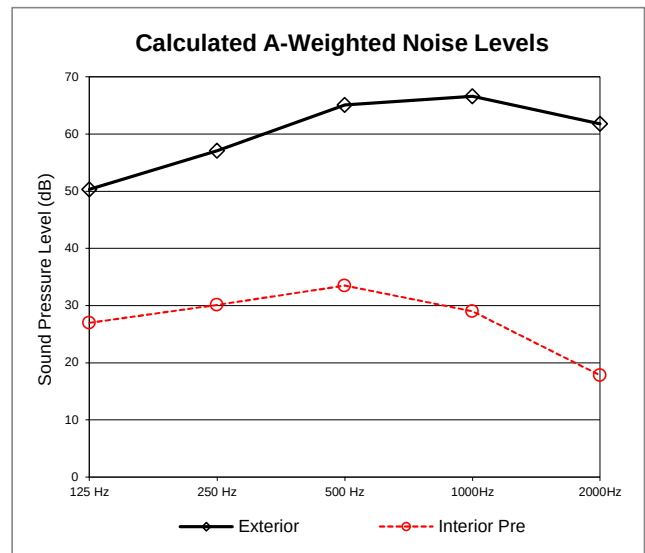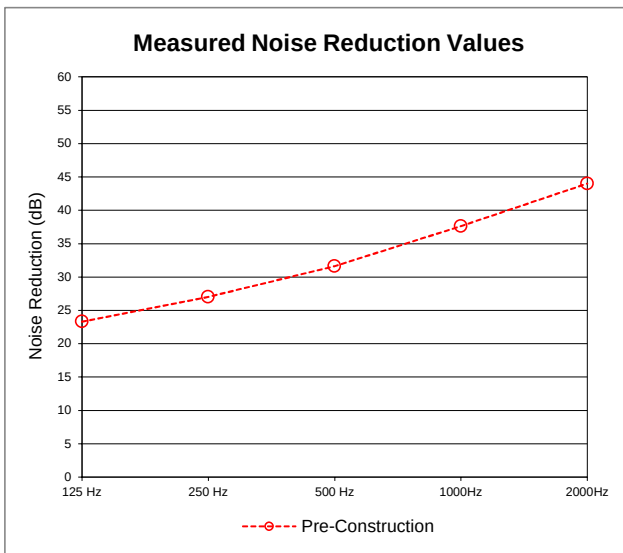

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Dustan
 Address: 12854 23rd Ave S
 Local City: SeaTac

Tested Room: Living / Kitchen Façade 3
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	67.8	60.0	59.1	56.3	47.0	60.7
Exterior Measurement (flush)	91.9	91.6	93.5	89.0	83.5	94.5
Exterior Adjusted	85.9	85.6	87.5	83.0	77.5	88.5
Interior Background	35.1	34.6	28.8	26.3	27.9	36.2
Interior Measurement	63.7	63.1	60.0	52.6	43.1	60.2
Interior Adjusted	63.7	63.1	60.0	52.6	43.0	60.2
Noise Reduction	22.2	22.5	27.5	30.4	34.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.1	34.6	37.6	36.2	27.3	41.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.5 dB

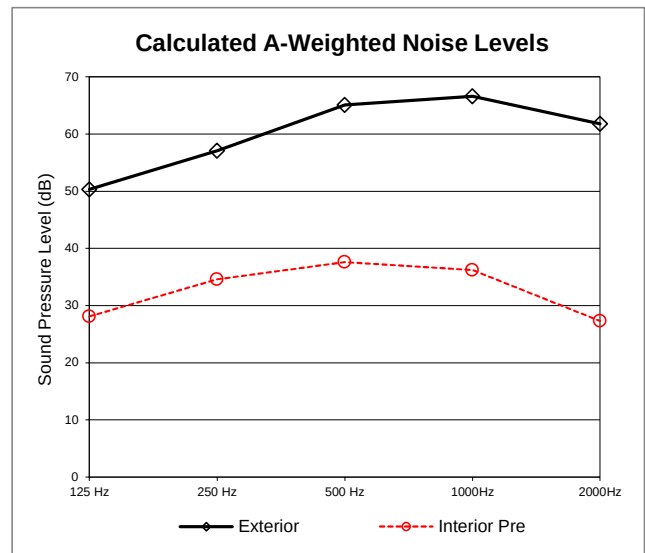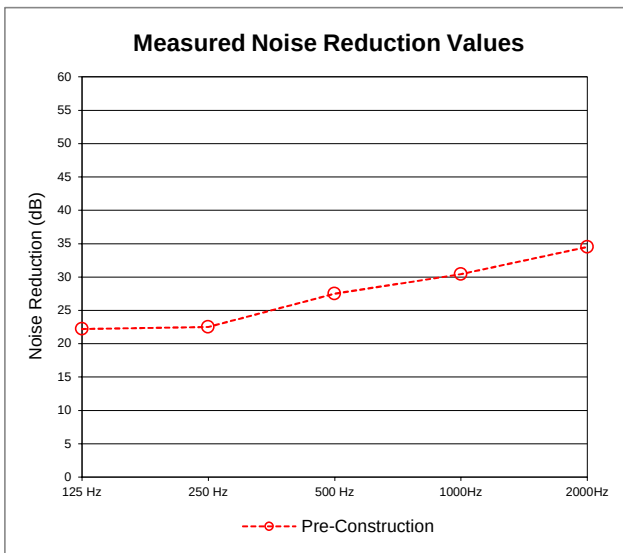

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Dustan
 Address: 12854 23rd Ave S
 Local City: SeaTac

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.5	51.9	50.3	49.0	39.6	52.5
Exterior Measurement (flush)	89.4	94.9	94.8	91.2	85.6	96.3
Exterior Adjusted	83.4	88.9	88.8	85.2	79.6	90.3
Interior Background	31.6	30.8	21.4	14.4	10.6	25.2
Interior Measurement	63.3	63.7	56.6	47.8	34.6	57.8
Interior Adjusted	63.3	63.7	56.6	47.8	34.6	57.8
Noise Reduction	20.1	25.2	32.2	37.4	45.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.2	31.9	32.9	29.2	16.8	37.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.7 dB

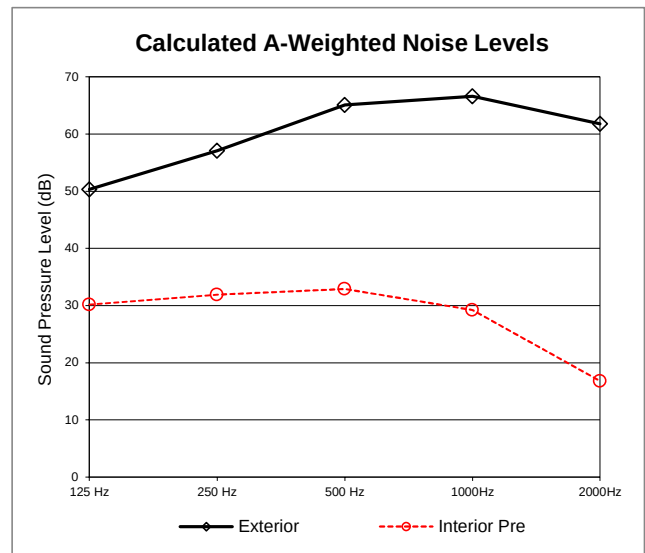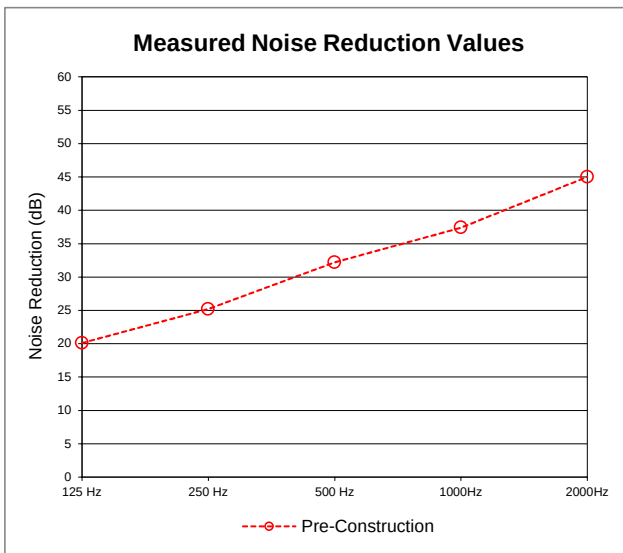

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Dustan
 Address: 12854 23rd Ave S
 Local City: SeaTac

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	65.3	58.2	55.0	54.1	42.0	57.8
Exterior Measurement (flush)	91.0	95.5	95.4	91.1	86.7	96.7
Exterior Adjusted	85.0	89.5	89.4	85.1	80.7	90.7
Interior Background	33.8	30.6	22.2	16.5	11.9	26.1
Interior Measurement	64.7	64.6	59.7	50.0	36.4	59.8
Interior Adjusted	64.7	64.6	59.7	50.0	36.4	59.8
Noise Reduction	20.3	24.9	29.7	35.1	44.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.0	32.2	35.4	31.5	17.5	38.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.2 dB

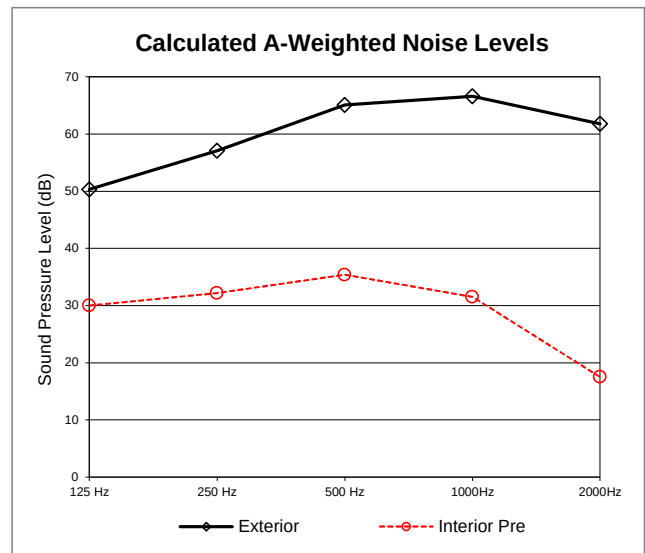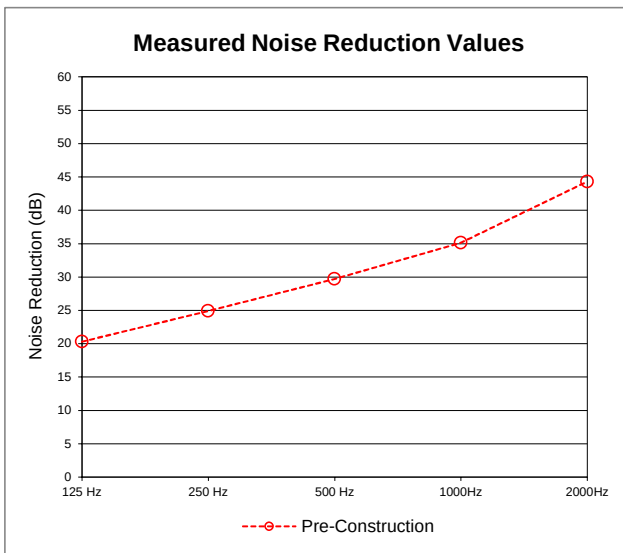



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tucker
 Address: 20822 25th Ave S
 Local City: Des Moines

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	56.5	53.4	49.7	41.4	54.9
Exterior Measurement (flush)	91.0	92.1	92.6	88.8	87.9	95.4
Exterior Adjusted	85.0	86.1	86.6	82.8	81.9	89.4
Interior Background	46.1	45.6	42.4	37.6	28.6	43.2
Interior Measurement	64.4	64.4	61.8	50.0	46.8	61.5
Interior Adjusted	64.3	64.3	61.7	49.7	46.7	61.4
Noise Reduction	20.7	21.8	24.9	33.1	35.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.6	35.3	40.2	33.5	26.6	42.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						27.6 dB

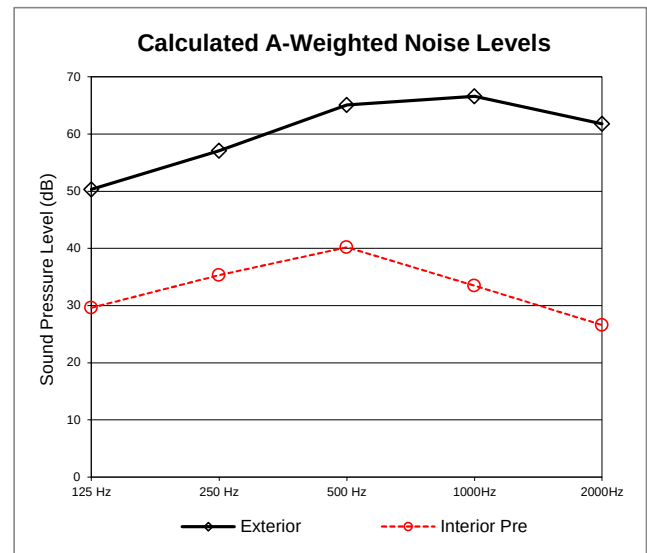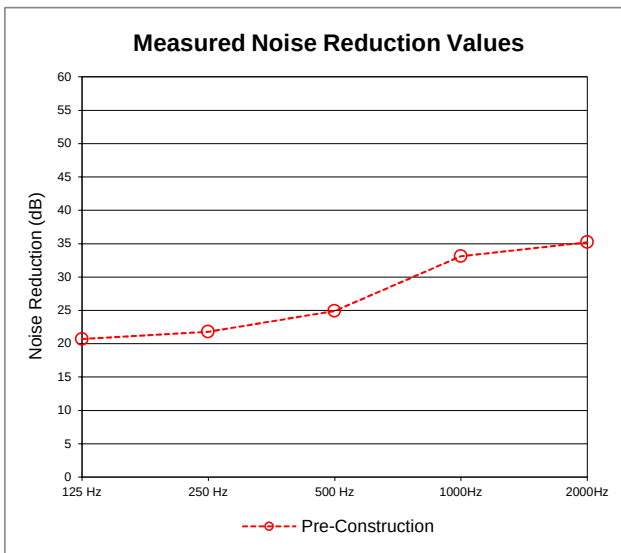

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tucker
 Address: 20822 25th Ave S
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.9	48.9	50.0	51.0	43.4	53.5
Exterior Measurement (flush)	92.4	91.4	91.1	90.2	88.2	95.6
Exterior Adjusted	86.4	85.4	85.1	84.2	82.2	89.6
Interior Background	37.8	35.2	39.0	37.0	31.3	40.6
Interior Measurement	65.2	63.6	57.0	47.4	40.5	58.4
Interior Adjusted	65.2	63.6	56.9	47.0	39.9	58.3
Noise Reduction	21.2	21.8	28.2	37.2	42.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.1	35.3	36.9	29.4	19.5	40.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.0 dB

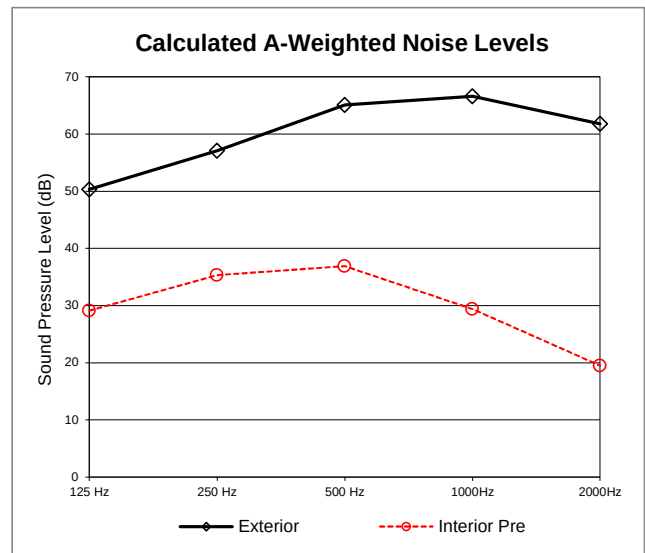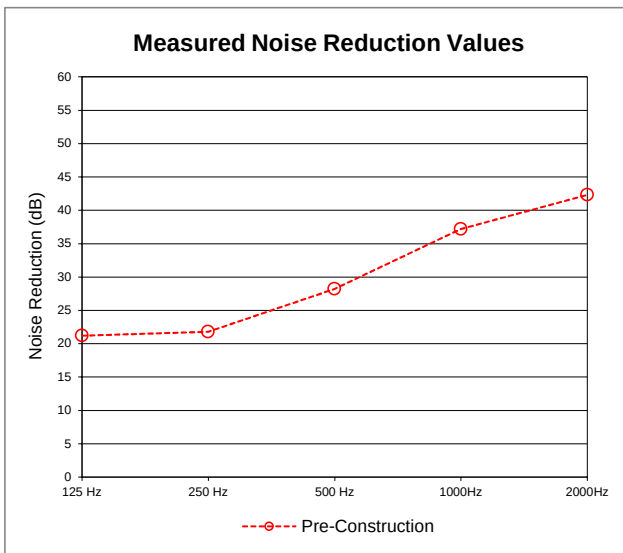



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tucker
 Address: 20822 25th Ave S
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.9	48.9	50.0	51.0	43.4	53.5
Exterior Measurement (flush)	94.0	95.2	96.9	93.8	89.6	98.9
Exterior Adjusted	88.0	89.2	90.9	87.8	83.6	92.9
Interior Background	30.8	24.3	14.9	10.1	10.7	22.0
Interior Measurement	68.9	67.8	61.9	47.3	38.6	62.6
Interior Adjusted	68.9	67.8	61.9	47.3	38.6	62.6
Noise Reduction	19.1	21.4	29.0	40.5	45.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.2	35.7	36.1	26.1	16.8	39.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.2 dB

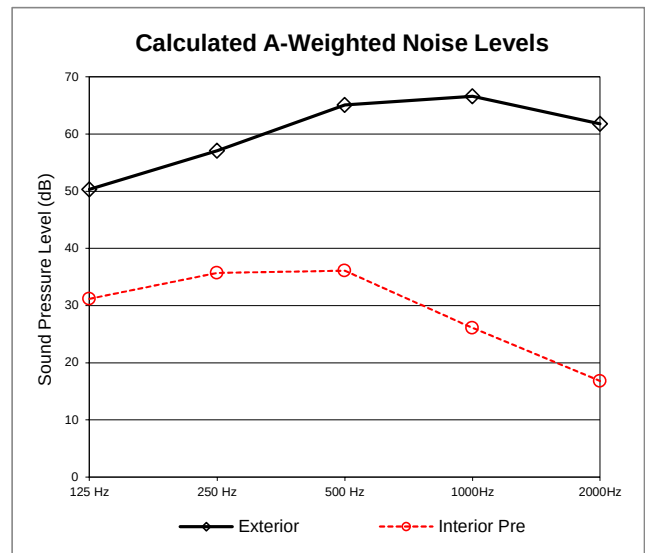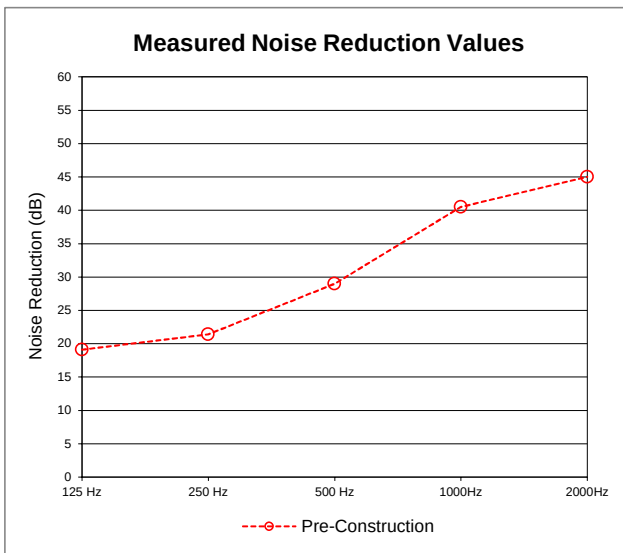



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tucker
 Address: 20822 25th Ave S
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	56.5	53.4	49.7	41.4	54.9
Exterior Measurement (flush)	91.1	87.0	91.1	88.2	84.7	93.2
Exterior Adjusted	85.1	81.0	85.1	82.2	78.7	87.2
Interior Background	44.0	44.1	36.4	24.6	16.0	37.7
Interior Measurement	61.7	56.0	54.6	44.1	39.3	54.6
Interior Adjusted	61.6	55.7	54.5	44.1	39.3	54.5
Noise Reduction	23.5	25.3	30.6	38.1	39.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.8	31.8	34.5	28.5	22.4	37.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.4 dB

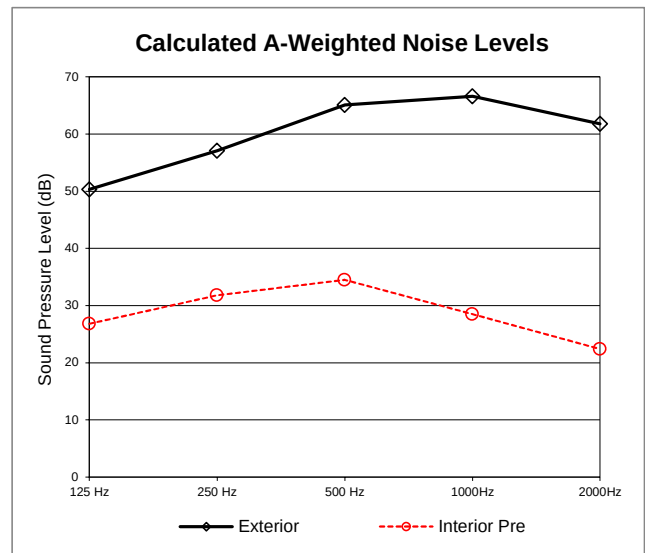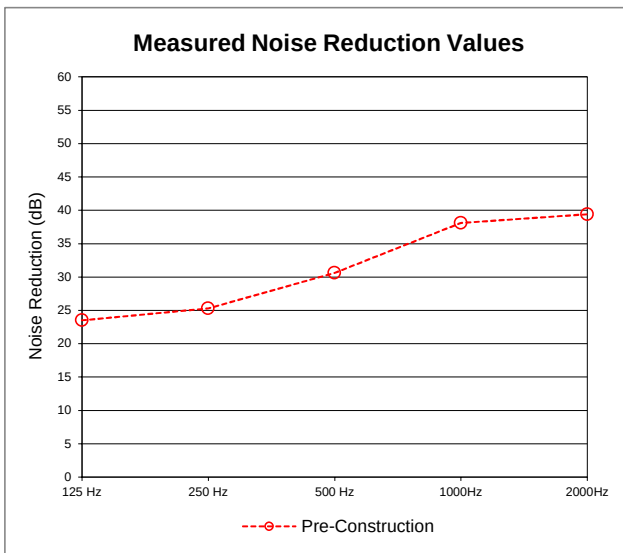



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Tucker
 Address: 20822 25th Ave S
 Local City: Des Moines

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 18, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	56.5	53.4	49.7	41.4	54.9
Exterior Measurement (flush)	89.5	91.6	91.6	88.5	85.1	93.8
Exterior Adjusted	83.5	85.6	85.6	82.5	79.1	87.8
Interior Background	37.3	30.4	24.8	14.8	11.8	26.9
Interior Measurement	66.0	60.1	57.9	43.6	38.0	57.4
Interior Adjusted	66.0	60.1	57.9	43.6	38.0	57.4
Noise Reduction	17.5	25.5	27.7	38.9	41.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.8	31.6	37.4	27.7	20.7	39.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.2 dB

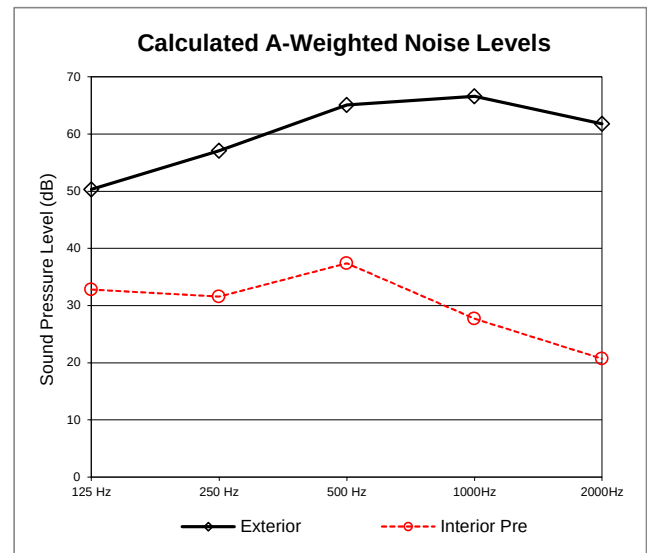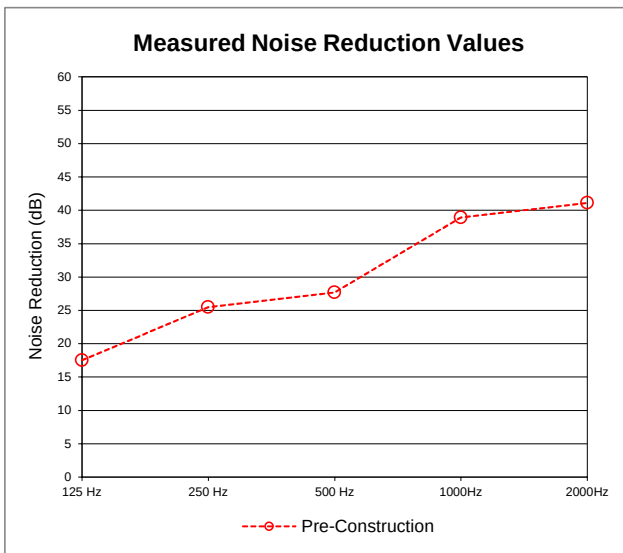

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Living Room Façade 1
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.1	52.7	50.1	52.8	40.9	54.7
Exterior Measurement (flush)	94.1	92.2	93.9	90.0	86.6	96.2
Exterior Adjusted	88.1	86.2	87.9	84.0	80.6	90.2
Interior Background	37.9	28.0	19.1	16.8	15.7	26.8
Interior Measurement	65.1	59.5	51.9	41.9	40.1	54.8
Interior Adjusted (roof)	65.6	60.0	52.4	42.4	40.6	55.3
Noise Reduction	22.5	26.2	35.5	41.6	40.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.8	30.9	29.6	25.0	21.8	35.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.9 dB

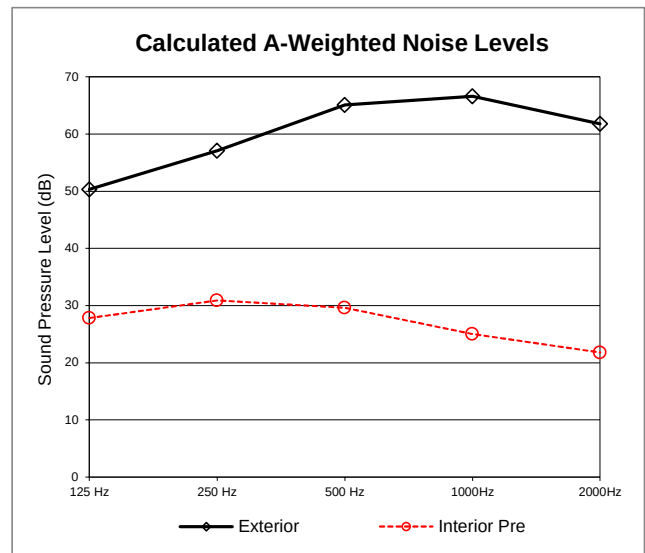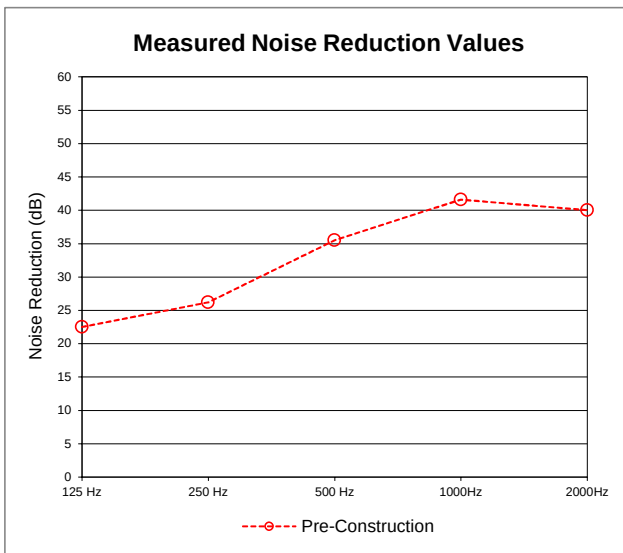



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Living Room Façade 2
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.9	51.5	50.3	50.1	39.1	53.0
Exterior Measurement (flush)	89.9	84.2	89.3	85.1	83.5	91.0
Exterior Adjusted	83.9	78.2	83.3	79.1	77.5	85.0
Interior Background	37.9	28.0	19.1	16.8	15.7	26.8
Interior Measurement	61.0	49.4	44.1	37.0	32.4	47.7
Interior Adjusted (roof)	61.5	49.9	44.6	37.5	32.8	48.2
Noise Reduction	22.4	28.3	38.7	41.6	44.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.9	28.8	26.4	25.0	17.1	33.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.6 dB

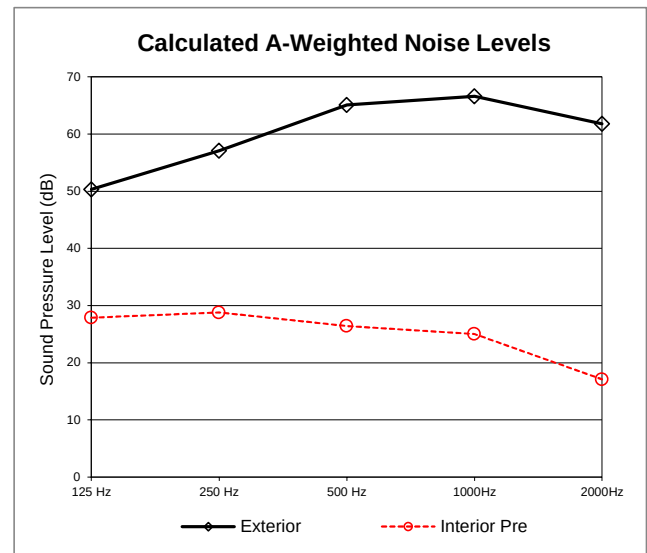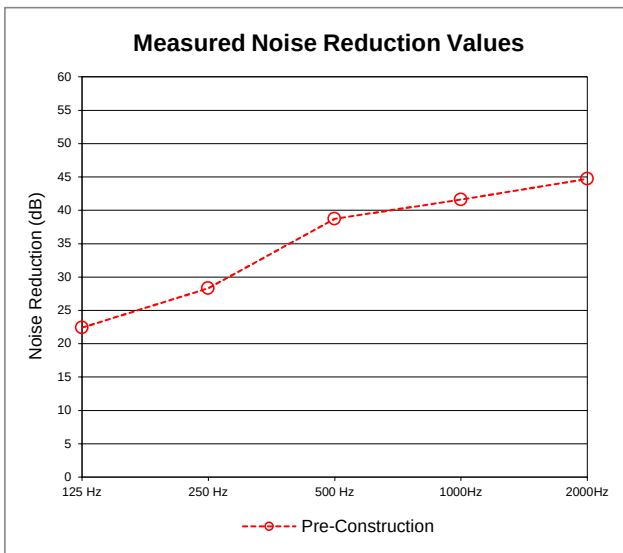



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.0	55.1	52.5	48.6	40.8	53.7
Exterior Measurement (flush)	91.0	91.5	94.0	90.1	88.6	96.5
Exterior Adjusted	85.0	85.5	88.0	84.1	82.6	90.5
Interior Background	37.2	38.8	31.9	22.2	18.5	33.3
Interior Measurement	63.5	63.7	60.7	51.8	46.2	60.8
Interior Adjusted	63.5	63.7	60.7	51.8	46.2	60.8
Noise Reduction	21.5	21.8	27.3	32.3	36.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.8	35.3	37.8	34.3	25.4	41.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.8 dB

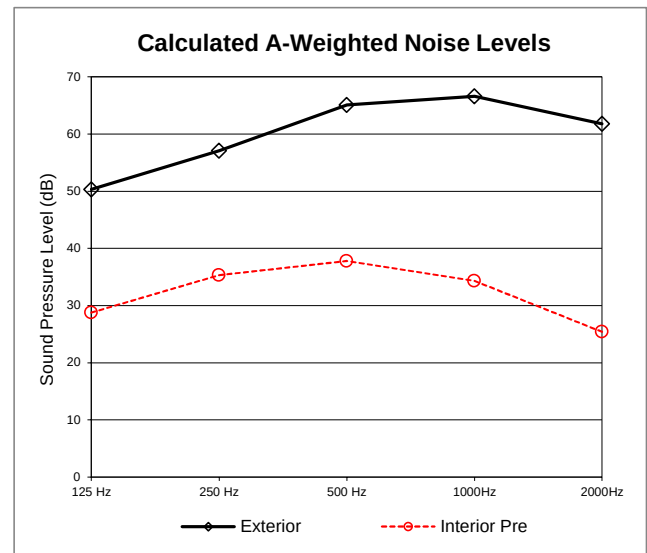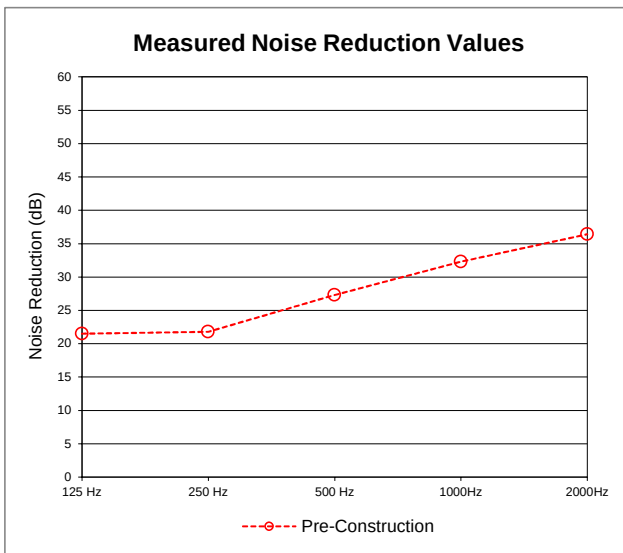

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Dining Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	56.8	54.8	54.3	44.1	57.4
Exterior Measurement (flush)	88.3	87.4	87.8	85.4	83.0	91.0
Exterior Adjusted	82.3	81.4	81.8	79.4	77.0	85.0
Interior Background	43.7	34.5	26.3	22.8	20.6	31.4
Interior Measurement	63.8	59.0	52.2	48.5	53.3	58.5
Interior Adjusted	63.8	59.0	52.2	48.5	53.3	58.5
Noise Reduction	18.5	22.4	29.6	30.9	23.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.8	34.7	35.5	35.7	38.1	42.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						27.4 dB

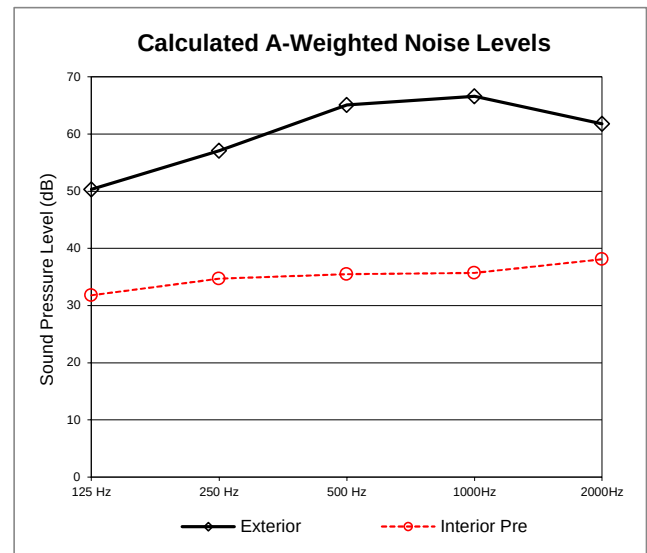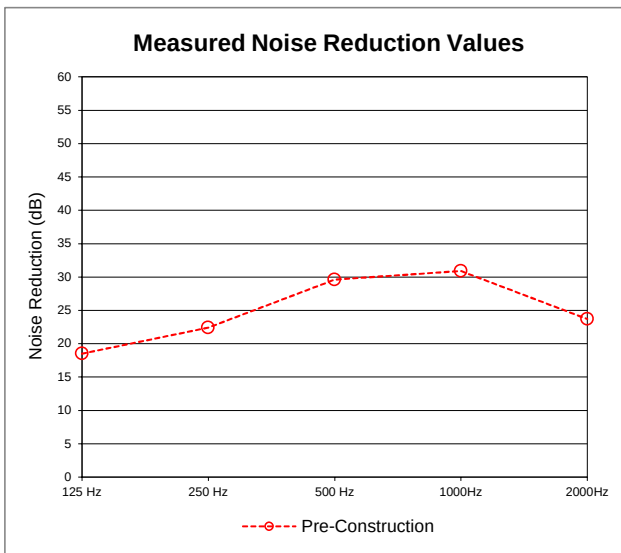



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Dinette Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.4	53.8	52.1	52.0	41.5	54.7
Exterior Measurement (flush)	96.7	98.5	99.6	96.3	92.0	101.6
Exterior Adjusted	90.7	92.5	93.6	90.3	86.0	95.6
Interior Background	38.8	43.4	37.3	32.8	28.4	39.7
Interior Measurement	68.6	63.4	58.8	49.9	43.7	60.0
Interior Adjusted	68.6	63.4	58.8	49.8	43.6	60.0
Noise Reduction	22.1	29.1	34.8	40.5	42.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.2	28.0	30.3	26.1	19.4	34.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.4 dB

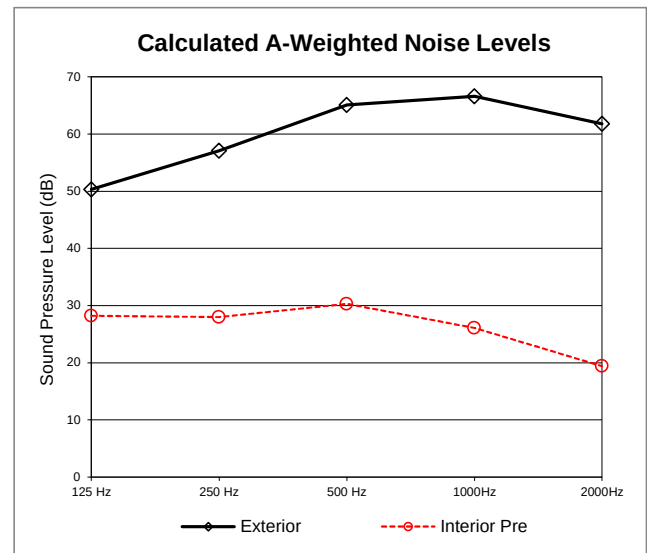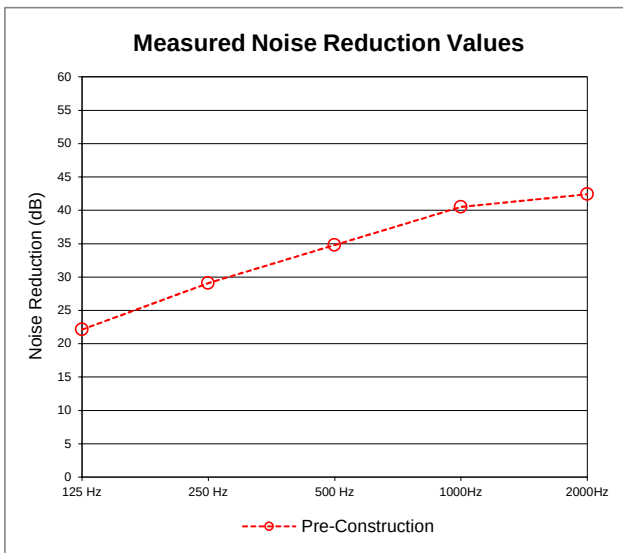

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.9	55.0	56.1	54.2	44.0	57.4
Exterior Measurement (flush)	93.6	95.8	95.1	92.0	89.5	97.6
Exterior Adjusted	87.6	89.8	89.1	86.0	83.5	91.6
Interior Background	34.1	27.1	21.6	24.8	26.8	32.4
Interior Measurement	67.8	62.4	60.0	50.6	46.8	60.5
Interior Adjusted	67.8	62.4	60.0	50.6	46.8	60.5
Noise Reduction	19.8	27.4	29.1	35.4	36.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.5	29.7	36.0	31.2	25.1	38.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.1 dB

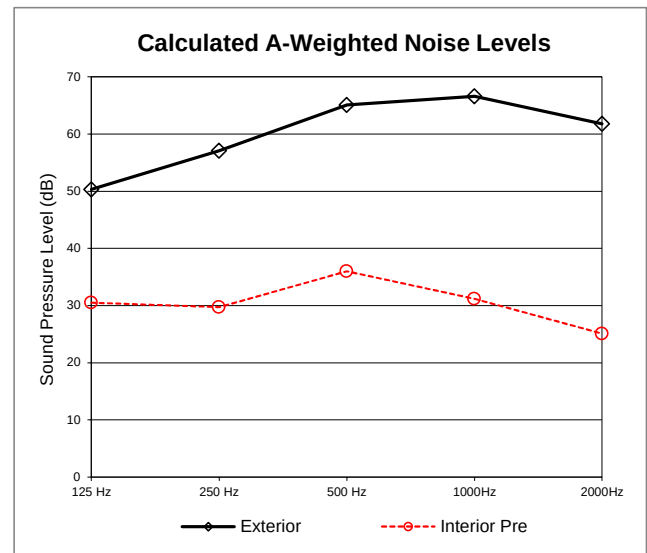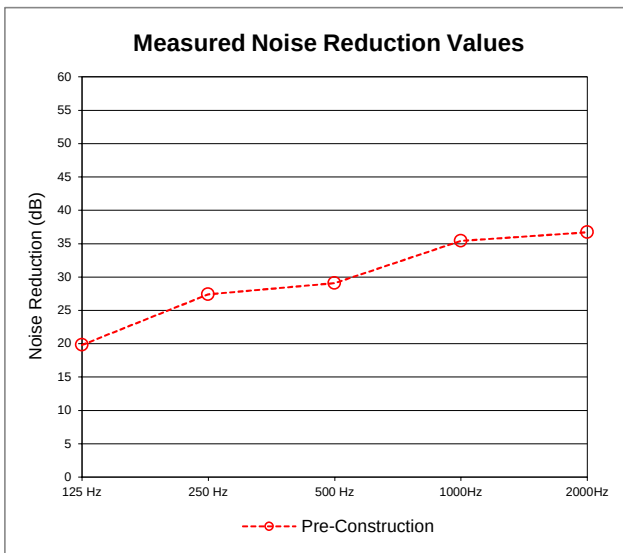



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.7	55.6	54.6	55.8	46.1	58.0
Exterior Measurement (flush)	94.1	93.9	95.2	90.2	86.5	96.3
Exterior Adjusted	88.1	87.9	89.2	84.2	80.5	90.3
Interior Background	39.2	28.1	17.6	14.6	15.6	26.8
Interior Measurement	61.0	52.5	45.8	37.4	33.8	48.9
Interior Adjusted (roof)	61.5	53.0	46.3	37.9	34.2	49.4
Noise Reduction	26.6	34.9	42.9	46.3	46.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	23.7	22.2	22.2	20.3	15.5	28.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.5 dB

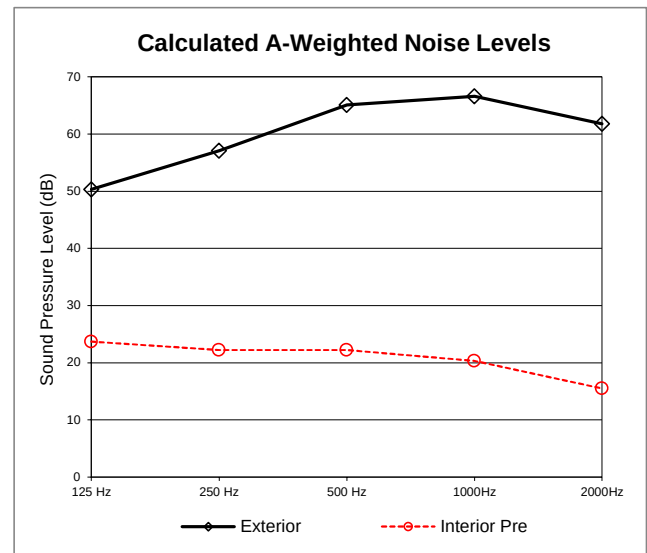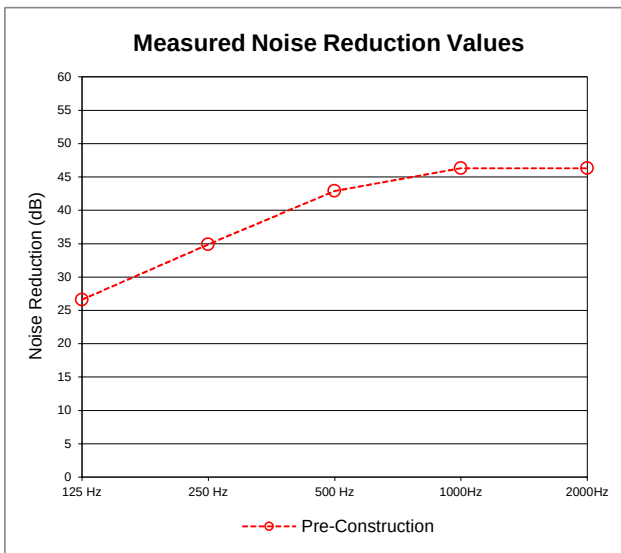

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.0	55.1	52.5	48.6	40.8	53.7
Exterior Measurement (flush)	89.7	93.8	93.5	90.6	86.7	95.7
Exterior Adjusted	83.7	87.8	87.5	84.6	80.7	89.7
Interior Background	44.9	34.9	21.6	12.5	10.9	30.9
Interior Measurement	62.0	59.0	51.8	42.9	37.5	54.0
Interior Adjusted (roof)	62.4	59.5	52.3	43.4	38.0	54.5
Noise Reduction	21.3	28.3	35.2	41.2	42.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.0	28.8	29.9	25.4	19.1	34.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.3 dB

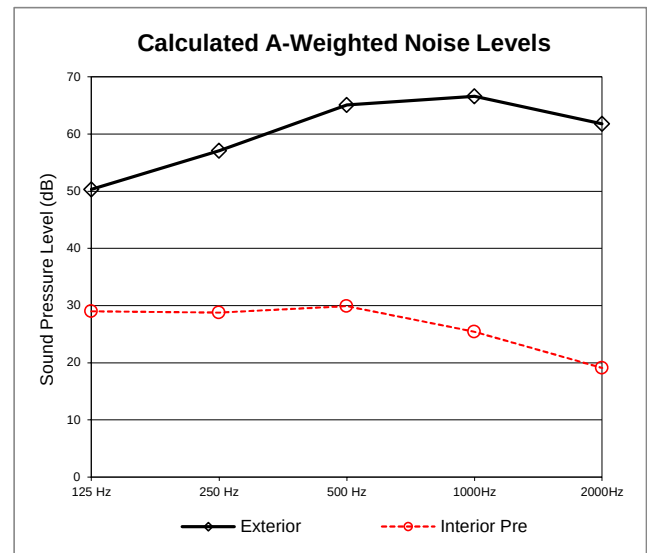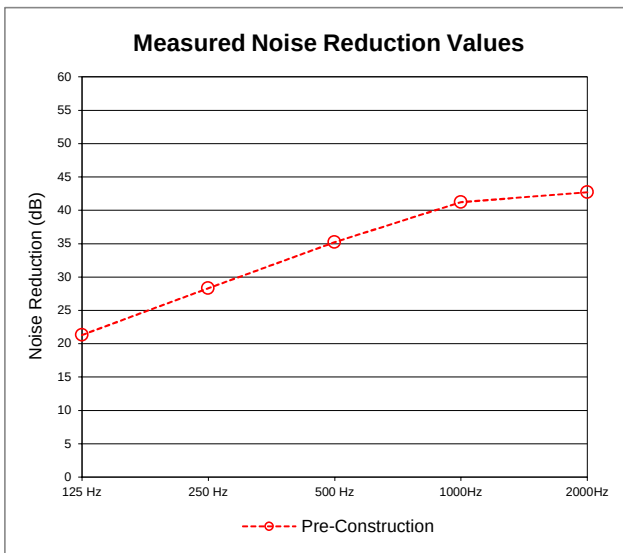

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Wynn
 Address: 2007 S 112th St
 Local City: Burien

Tested Room: Study Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.3	52.2	49.4	50.4	44.2	53.5
Exterior Measurement (flush)	98.0	97.0	97.0	95.2	90.7	100.0
Exterior Adjusted	92.0	91.0	91.0	89.2	84.7	94.0
Interior Background	38.8	34.6	28.0	22.5	17.8	30.9
Interior Measurement	68.3	66.6	66.1	57.8	52.6	66.3
Interior Adjusted	68.3	66.6	66.1	57.8	52.6	66.3
Noise Reduction	23.7	24.4	24.9	31.4	32.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.6	32.7	40.2	35.2	29.7	42.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						27.7 dB

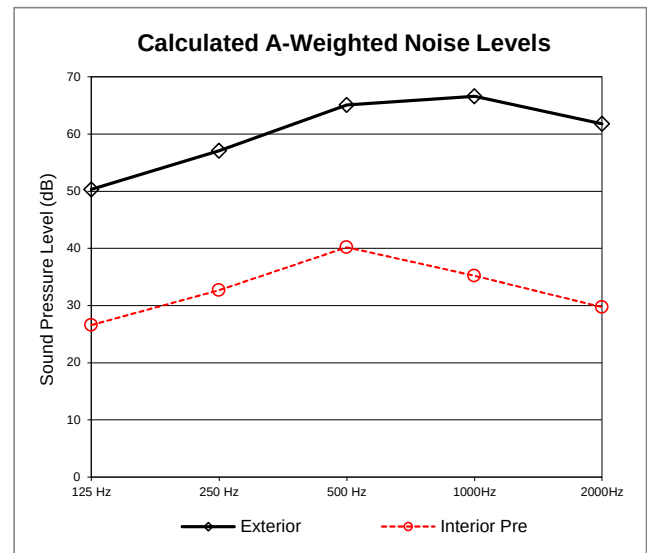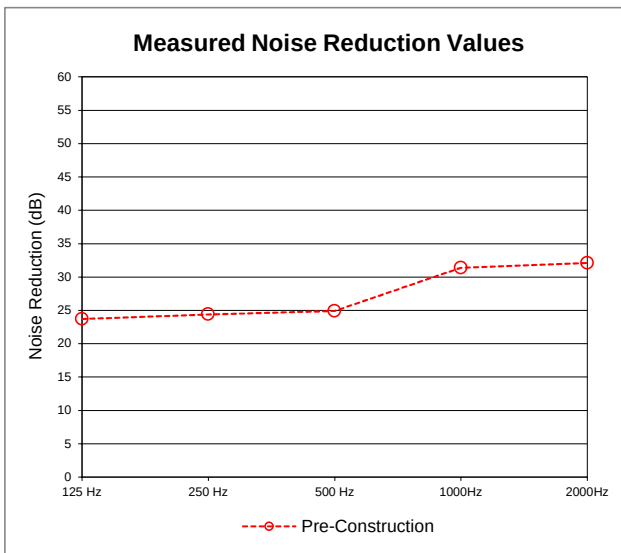



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carstensen
 Address: 1244 S 120th St
 Local City: Burien

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.3	54.0	52.3	52.5	43.0	55.3
Exterior Measurement (flush)	92.6	96.1	96.3	91.5	86.9	97.2
Exterior Adjusted	86.6	90.1	90.3	85.5	80.9	91.2
Interior Background	50.2	36.4	21.1	20.9	19.5	37.0
Interior Measurement	71.2	63.5	56.4	47.9	48.2	60.3
Interior Adjusted	71.2	63.5	56.4	47.9	48.2	60.3
Noise Reduction	15.4	26.6	33.9	37.6	32.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.9	30.5	31.2	29.0	29.1	38.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.5 dB

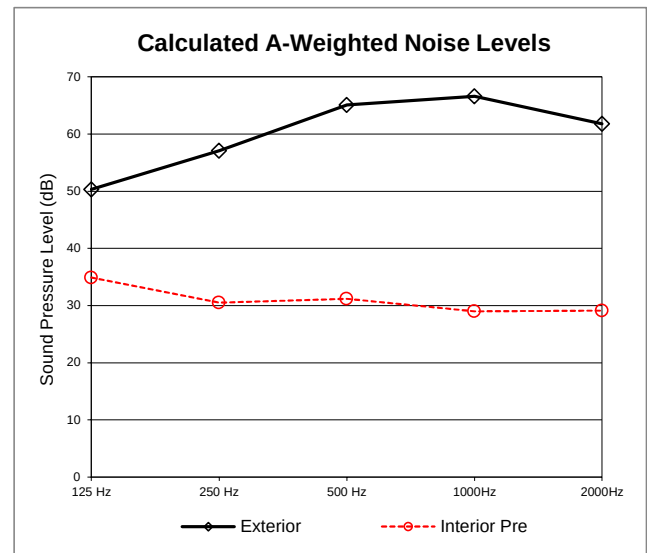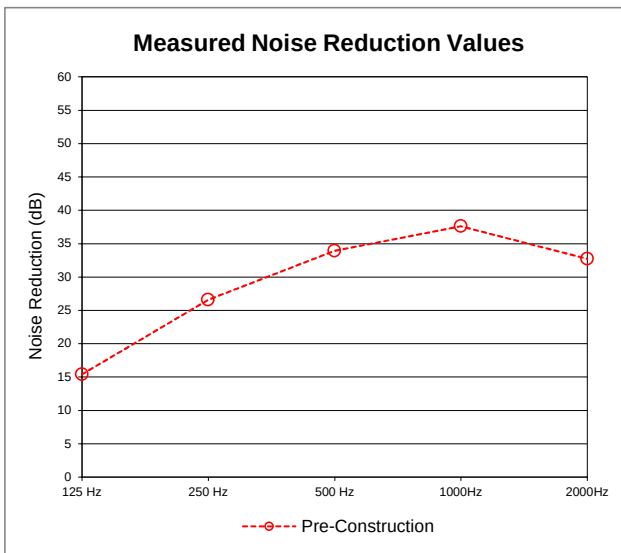



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carstensen
 Address: 1244 S 120th St
 Local City: Burien

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.1	51.5	48.9	48.3	39.9	51.7
Exterior Measurement (flush)	96.5	99.9	99.7	93.9	90.9	100.5
Exterior Adjusted	90.5	93.9	93.7	87.9	84.9	94.5
Interior Background	42.5	31.6	25.6	23.9	25.8	36.2
Interior Measurement	71.9	64.1	62.0	52.0	45.5	62.2
Interior Adjusted	71.9	64.1	62.0	52.0	45.5	62.2
Noise Reduction	18.6	29.8	31.7	35.9	39.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.7	27.3	33.4	30.7	22.4	37.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.6 dB

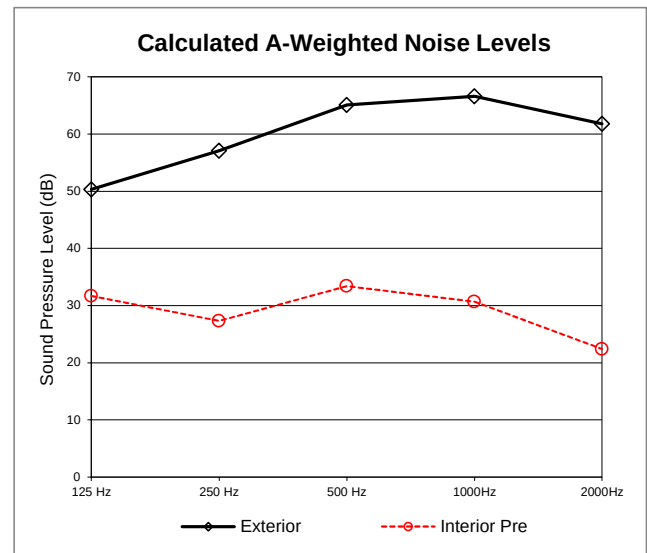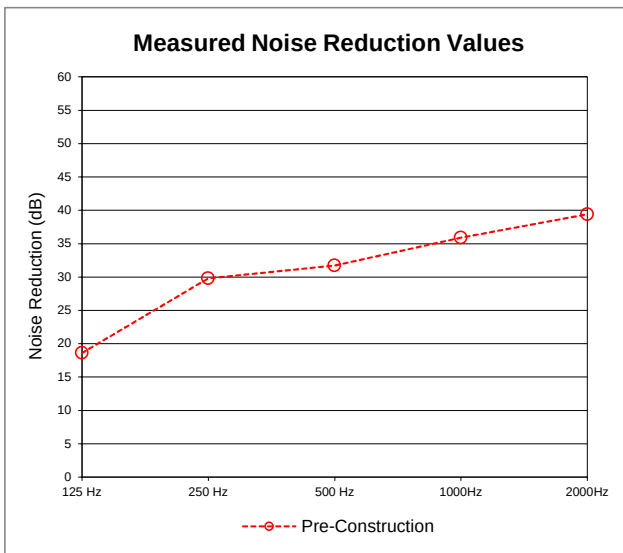

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carstensen
 Address: 1244 S 120th St
 Local City: Burien

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.6	53.1	53.6	52.4	44.7	55.6
Exterior Measurement (flush)	101.3	102.6	100.8	95.5	92.2	102.0
Exterior Adjusted	95.3	96.6	94.8	89.5	86.2	96.0
Interior Background	42.0	37.6	34.1	28.5	22.5	35.5
Interior Measurement	73.0	69.7	66.2	57.9	56.6	67.1
Interior Adjusted	73.0	69.7	66.2	57.9	56.6	67.1
Noise Reduction	22.3	26.9	28.6	31.6	29.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.0	30.2	36.5	35.0	32.2	40.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.6 dB

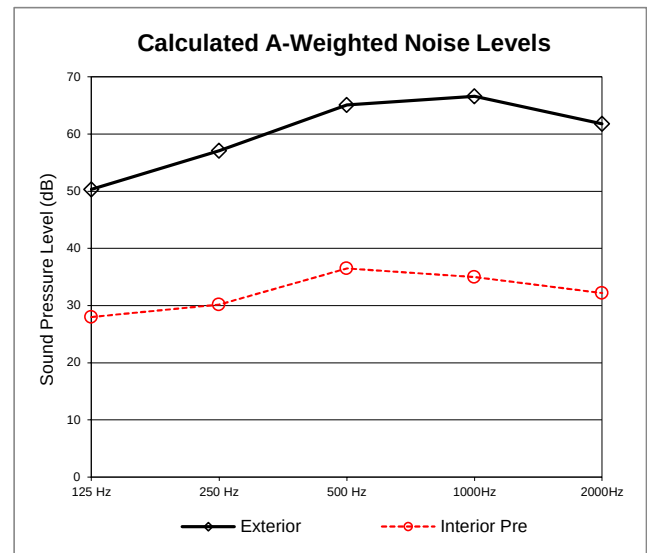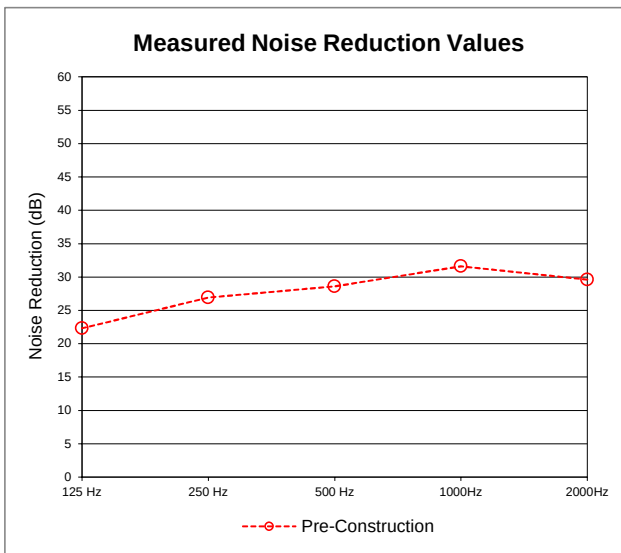

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carstensen
 Address: 1244 S 120th St
 Local City: Burien

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.9	53.1	50.2	46.2	38.7	51.4
Exterior Measurement (flush)	98.5	97.2	97.9	92.4	88.2	98.9
Exterior Adjusted	92.5	91.2	91.9	86.4	82.2	92.9
Interior Background	44.8	32.0	21.9	19.3	19.6	31.8
Interior Measurement	72.1	62.4	56.1	45.8	37.6	58.9
Interior Adjusted	72.1	62.4	56.1	45.8	37.5	58.9
Noise Reduction	20.4	28.8	35.8	40.6	44.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.9	28.3	29.3	26.0	17.1	34.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.3 dB

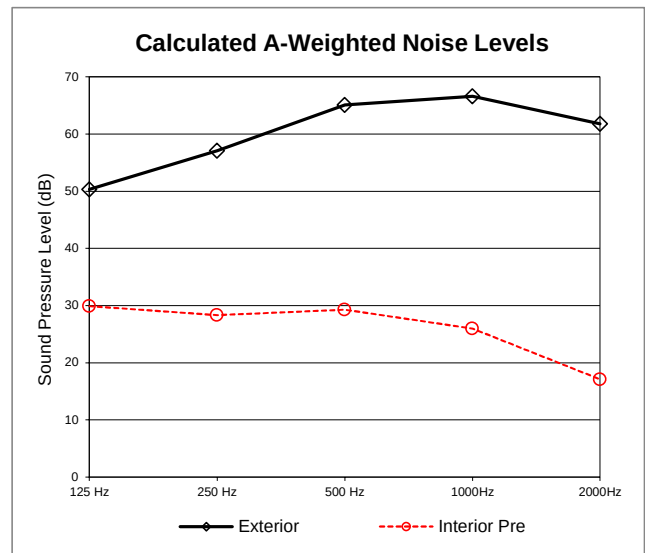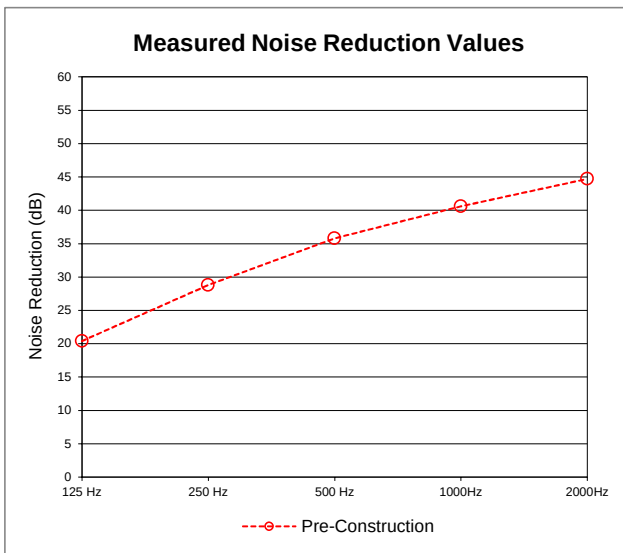



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carstensen
 Address: 1244 S 120th St
 Local City: Burien

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.1	58.1	55.7	51.8	40.0	56.9
Exterior Measurement (flush)	97.1	96.6	97.0	92.2	88.1	98.1
Exterior Adjusted	91.1	90.6	91.0	86.2	82.1	92.1
Interior Background	36.6	28.1	26.9	24.0	21.9	31.5
Interior Measurement	71.4	61.4	55.1	47.2	40.3	58.5
Interior Adjusted	71.4	61.4	55.1	47.2	40.2	58.5
Noise Reduction	19.7	29.2	35.9	39.0	41.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.6	27.9	29.2	27.6	19.9	35.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.9 dB

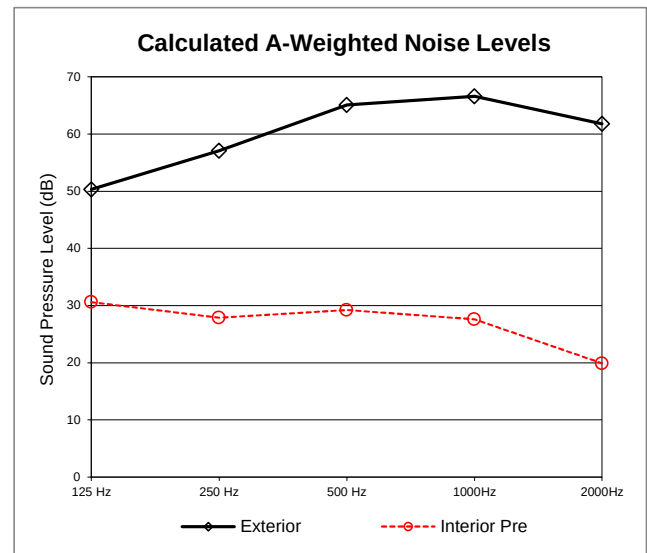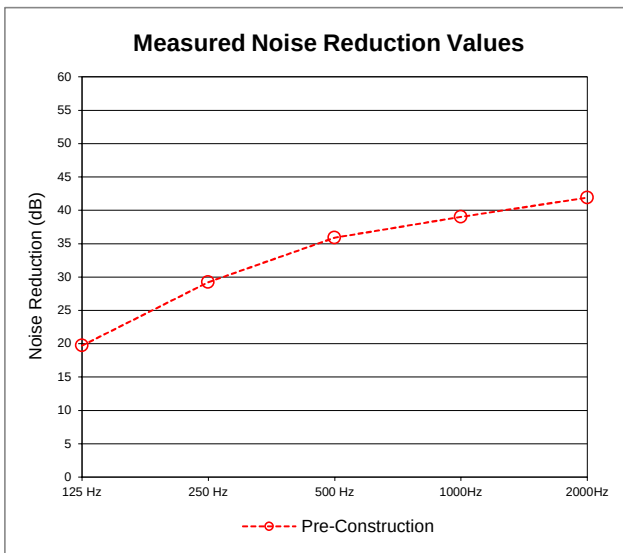



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Carstensen
 Address: 1244 S 120th St
 Local City: Burien

Tested Room: Den Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 16, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.1	58.1	55.7	51.8	40.0	56.9
Exterior Measurement (flush)	97.4	97.1	97.1	92.0	87.8	98.1
Exterior Adjusted	91.4	91.1	91.1	86.0	81.8	92.1
Interior Background	41.1	29.6	20.8	17.3	17.7	29.2
Interior Measurement	71.8	58.8	53.2	43.2	35.6	57.5
Interior Adjusted	71.8	58.8	53.2	43.2	35.5	57.5
Noise Reduction	19.6	32.3	37.9	42.8	46.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.7	24.8	27.2	23.8	15.5	33.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.4 dB

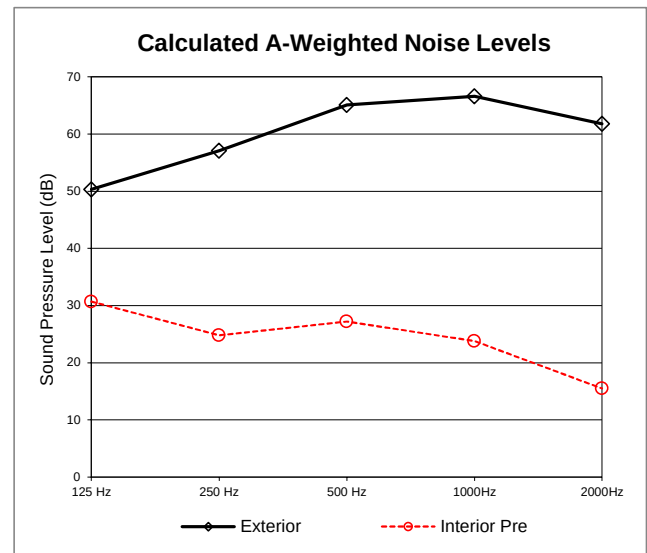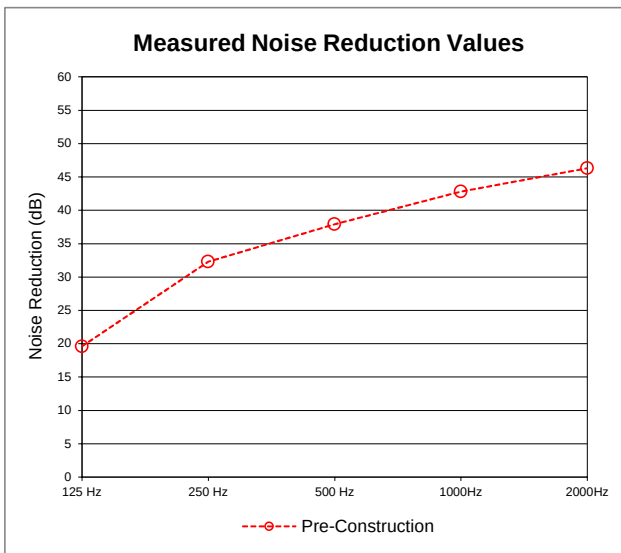

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.1	53.6	51.3	48.5	42.0	53.7
Exterior Measurement (flush)	89.7	93.0	92.5	87.9	85.7	94.3
Exterior Adjusted	83.7	87.0	86.5	81.9	79.7	88.3
Interior Background	37.6	28.1	21.8	16.1	13.6	26.5
Interior Measurement	67.6	55.2	51.0	43.2	34.3	54.3
Interior Adjusted	67.6	55.2	51.0	43.2	34.3	54.3
Noise Reduction	16.1	31.8	35.5	38.7	45.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.2	25.3	29.6	27.9	16.4	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

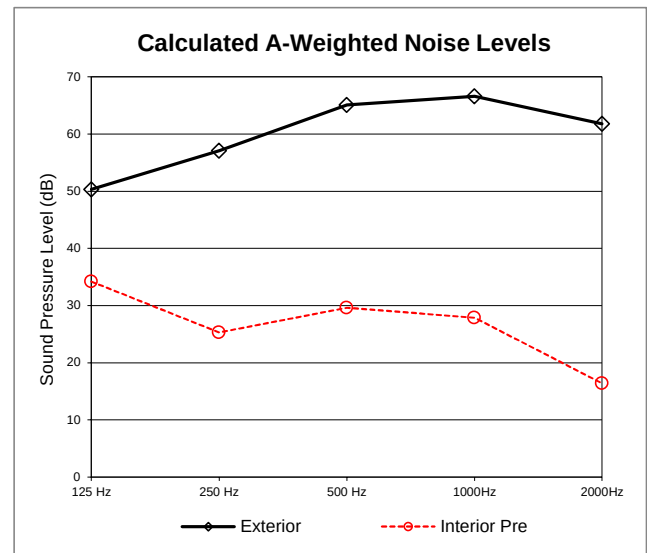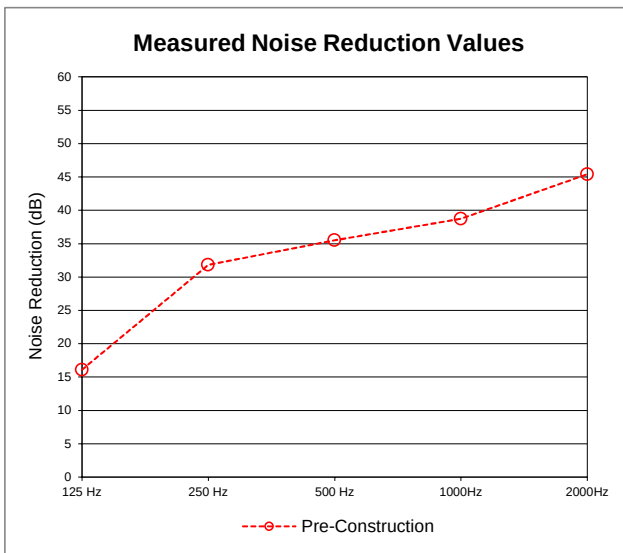



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Sitting Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.3	49.8	49.5	45.7	40.0	50.8
Exterior Measurement (flush)	99.0	97.2	98.5	94.1	89.3	99.6
Exterior Adjusted	93.0	91.2	92.5	88.1	83.3	93.6
Interior Background	35.6	22.5	17.8	18.8	15.1	25.4
Interior Measurement	74.4	62.3	59.6	59.4	45.9	63.3
Interior Adjusted	74.4	62.3	59.6	59.4	45.9	63.3
Noise Reduction	18.6	28.9	32.9	28.7	37.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.7	28.2	32.2	37.9	24.4	40.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.9 dB

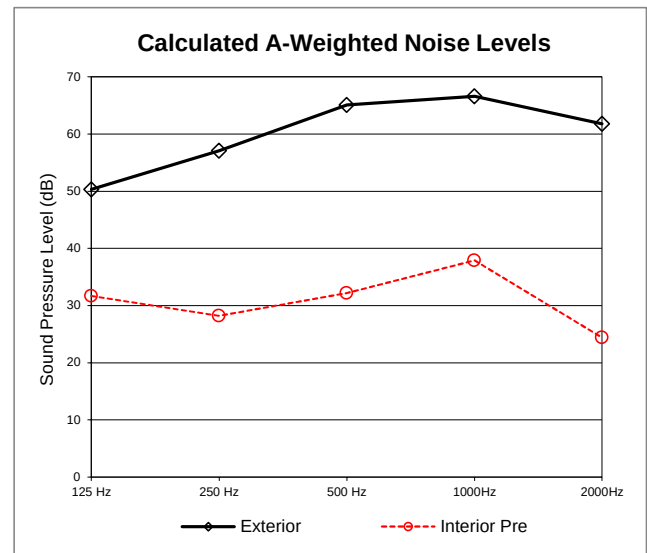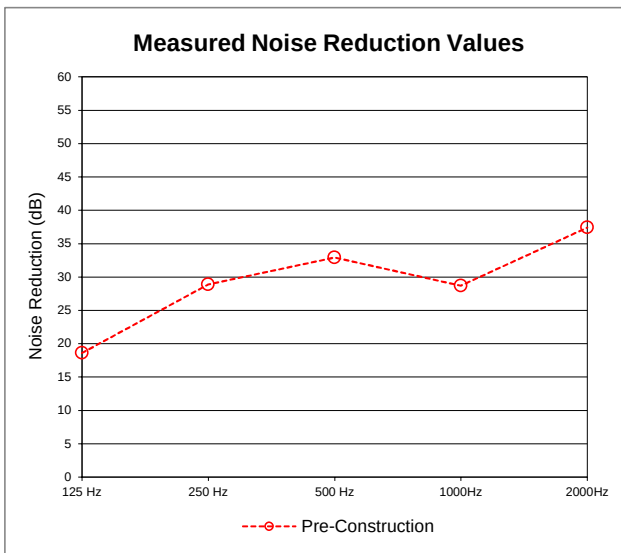



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Sitting Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	48.9	48.7	46.5	41.5	51.0
Exterior Measurement (flush)	90.8	94.0	96.7	88.5	83.8	95.8
Exterior Adjusted	84.8	88.0	90.7	82.5	77.8	89.8
Interior Background	35.6	22.5	17.8	18.8	15.1	25.4
Interior Measurement	66.8	59.1	53.2	47.0	42.5	56.1
Interior Adjusted	66.8	59.1	53.2	47.0	42.5	56.1
Noise Reduction	18.0	28.9	37.5	35.5	35.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.3	28.2	27.6	31.1	26.5	36.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.3 dB

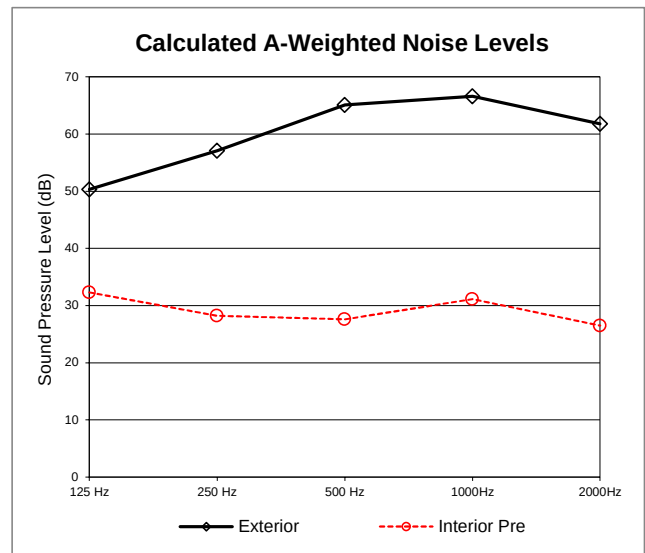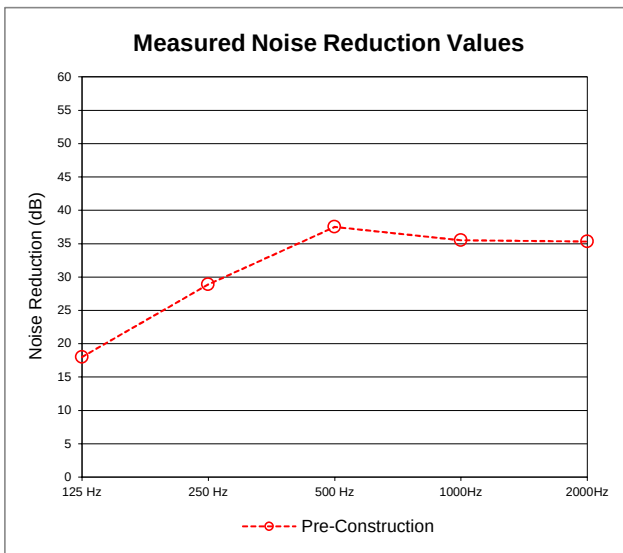



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.8	48.9	48.7	46.5	41.5	51.0
Exterior Measurement (flush)	89.4	91.2	93.3	88.8	86.3	94.6
Exterior Adjusted	83.4	85.2	87.3	82.8	80.3	88.6
Interior Background	47.0	48.0	38.9	37.5	34.0	43.7
Interior Measurement	65.9	60.5	58.6	52.2	44.4	59.0
Interior Adjusted	65.8	60.2	58.6	52.1	44.0	58.9
Noise Reduction	17.6	25.0	28.7	30.7	36.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.7	32.1	36.4	35.9	25.5	40.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.2 dB

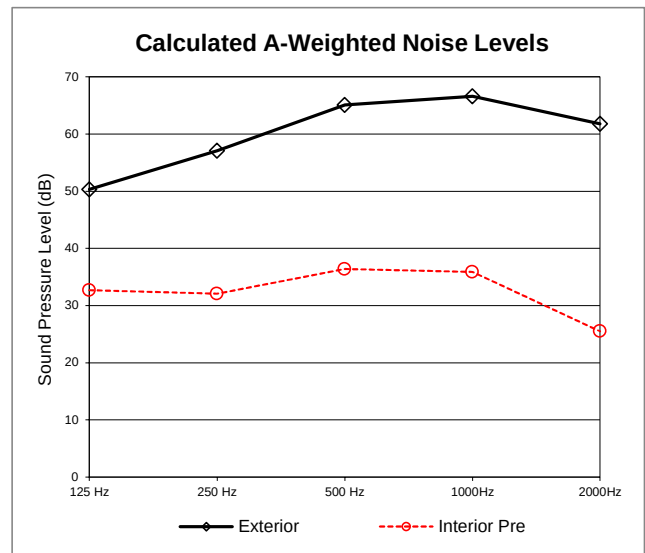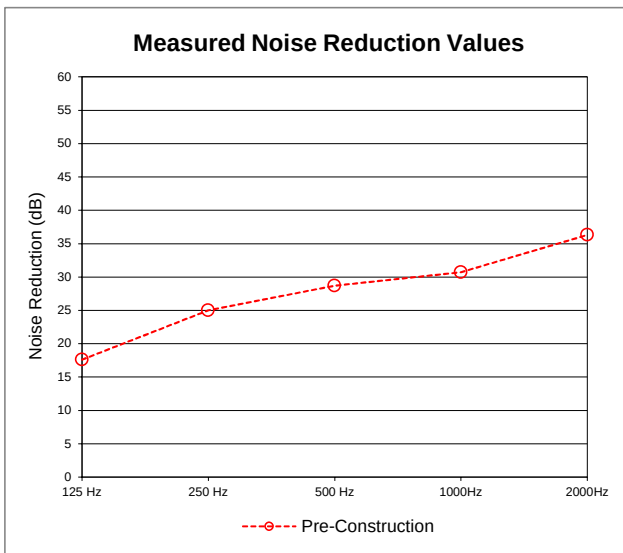

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.4	49.9	49.2	47.7	41.8	51.7
Exterior Measurement (flush)	104.7	103.8	104.7	98.1	94.8	104.7
Exterior Adjusted	98.7	97.8	98.7	92.1	88.8	98.7
Interior Background	39.8	29.4	26.4	17.6	15.5	28.4
Interior Measurement	79.2	67.0	59.4	46.7	39.3	64.4
Interior Adjusted	79.2	67.0	59.4	46.7	39.3	64.4
Noise Reduction	19.5	30.8	39.3	45.4	49.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.8	26.3	25.8	21.2	12.3	33.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.7 dB

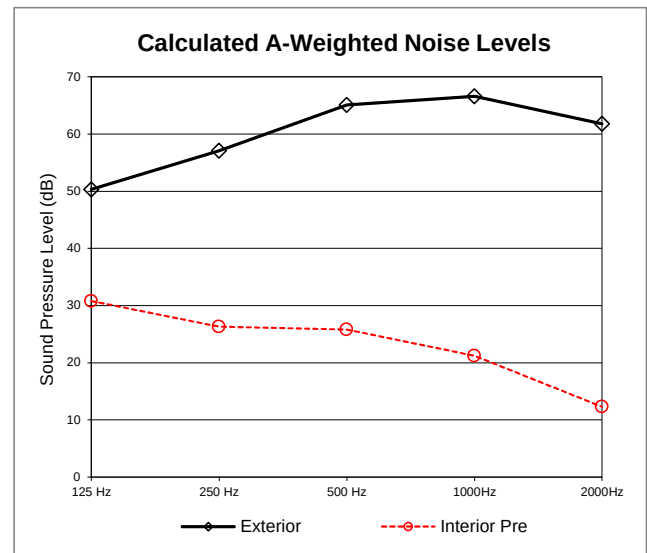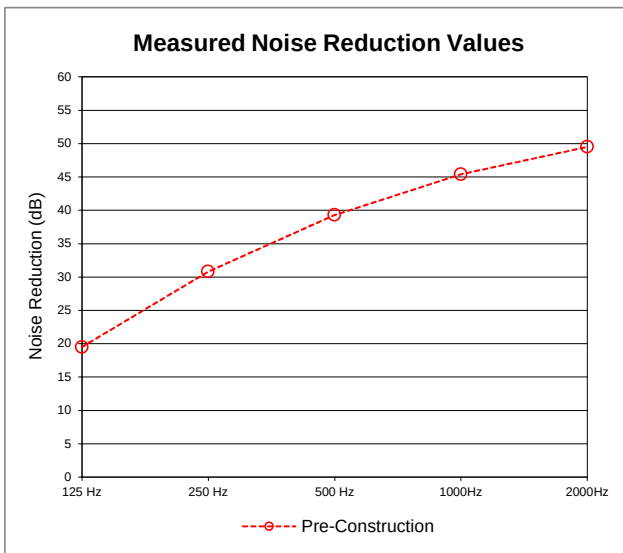



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.4	53.8	53.1	49.5	43.9	54.5
Exterior Measurement (flush)	90.2	88.3	92.2	86.9	83.8	92.9
Exterior Adjusted	84.2	82.3	86.2	80.9	77.8	86.9
Interior Background	41.9	45.5	29.8	23.0	17.4	37.1
Interior Measurement	62.5	52.7	44.3	34.0	29.6	49.7
Interior Adjusted	62.5	51.8	44.1	33.6	29.3	49.5
Noise Reduction	21.7	30.5	42.1	47.3	48.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.6	26.6	23.0	19.3	13.3	31.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						38.3 dB

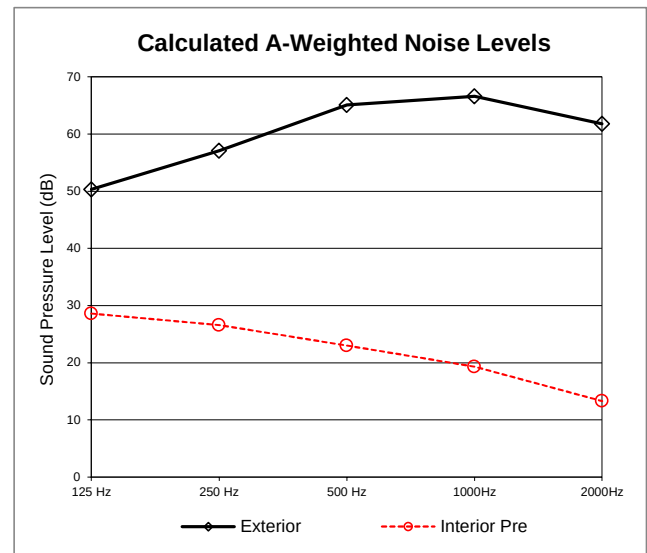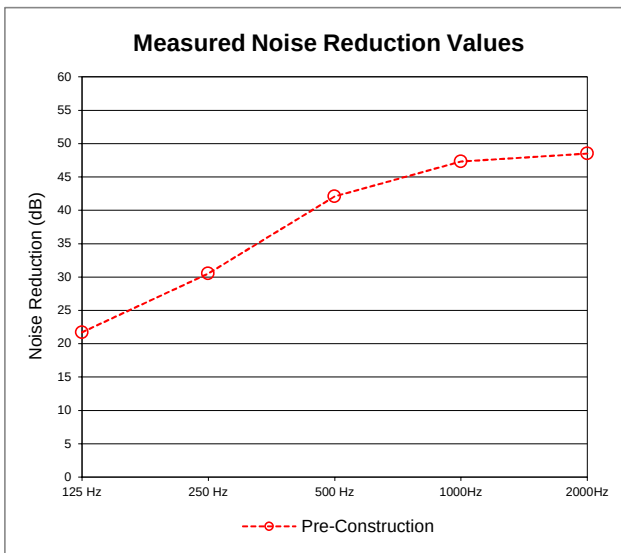

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Chey & Han
 Address: 2516 S 146th St
 Local City: SeaTac

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 17, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.4	53.8	53.1	49.5	43.9	54.5
Exterior Measurement (flush)	89.8	91.2	92.7	87.8	85.0	93.9
Exterior Adjusted	83.8	85.2	86.7	81.8	79.0	87.9
Interior Background	48.5	45.7	35.5	27.1	25.6	39.9
Interior Measurement	61.2	53.0	46.0	37.0	33.0	49.6
Interior Adjusted	61.0	52.1	45.6	36.5	32.1	49.1
Noise Reduction	22.8	33.1	41.1	45.3	46.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.5	24.0	24.0	21.3	14.9	30.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						39.1 dB

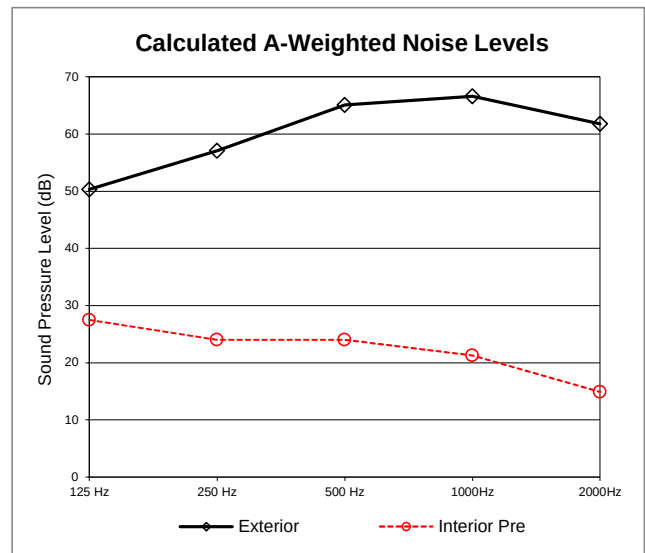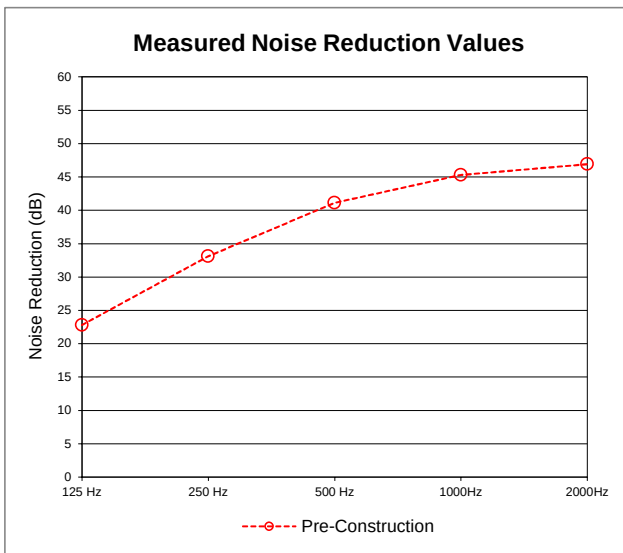

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Meza
 Address: 2637 S 150th St
 Local City: SeaTac

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	54.6	53.8	53.1	46.9	56.9
Exterior Measurement (flush)	91.8	93.5	92.8	87.4	85.0	94.1
Exterior Adjusted	85.8	87.5	86.8	81.4	79.0	88.1
Interior Background	38.5	34.4	35.3	30.0	25.7	35.9
Interior Measurement	64.5	56.5	55.1	49.5	51.3	58.4
Interior Adjusted	64.5	56.5	55.1	49.5	51.3	58.4
Noise Reduction	21.3	31.0	31.7	31.9	27.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.0	26.1	33.4	34.7	34.1	39.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.5 dB

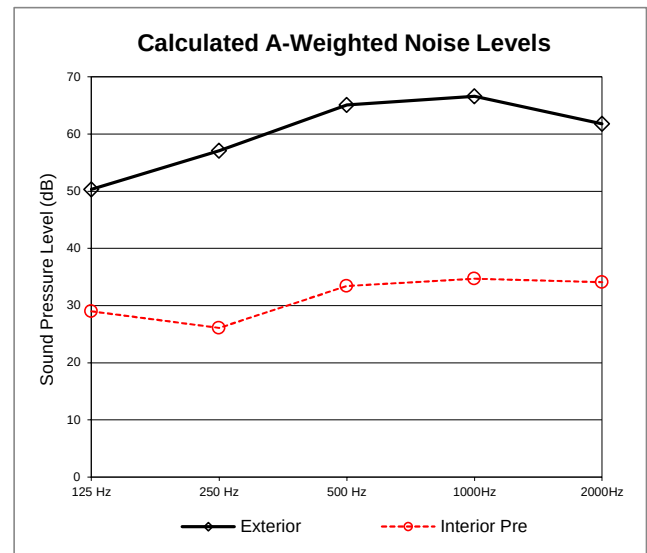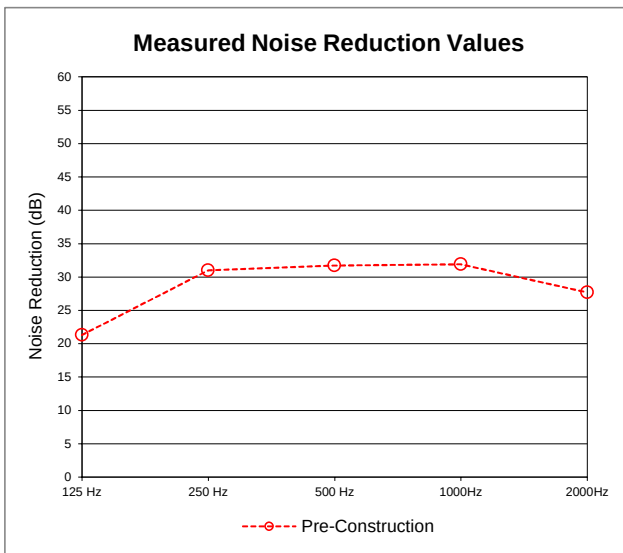



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Meza
 Address: 2637 S 150th St
 Local City: SeaTac

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	65.5	64.9	58.3	56.3	50.3	61.3
Exterior Measurement (flush)	88.2	89.3	93.2	87.6	84.9	93.7
Exterior Adjusted	82.2	83.3	87.2	81.6	78.9	87.7
Interior Background	39.4	34.1	33.1	29.8	27.9	35.5
Interior Measurement	63.8	54.1	50.5	46.0	38.3	52.9
Interior Adjusted	63.8	54.1	50.4	45.9	37.9	52.8
Noise Reduction	18.4	29.2	36.8	35.7	41.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.9	27.9	28.3	30.9	20.8	36.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.8 dB

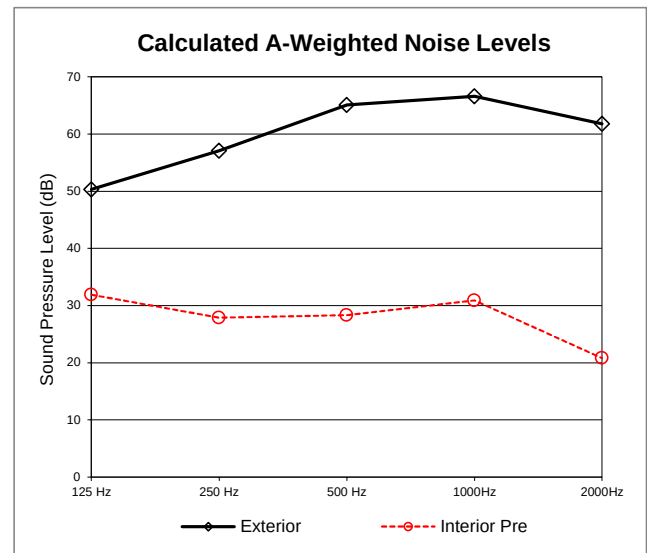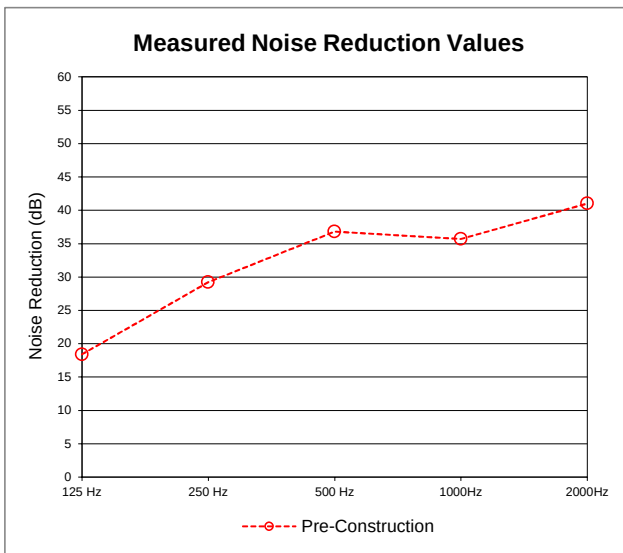



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Meza
 Address: 2637 S 150th St
 Local City: SeaTac

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.5	56.2	56.2	52.1	46.6	57.1
Exterior Measurement (flush)	108.6	108.3	109.4	102.5	98.8	109.8
Exterior Adjusted	102.6	102.3	103.4	96.5	92.8	103.8
Interior Background	42.3	29.7	23.5	18.0	17.4	29.1
Interior Measurement	75.6	70.2	64.6	52.0	41.5	65.7
Interior Adjusted	75.6	70.2	64.6	52.0	41.5	65.7
Noise Reduction	27.0	32.1	38.8	44.5	51.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	23.3	25.0	26.3	22.1	10.5	30.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						39.5 dB

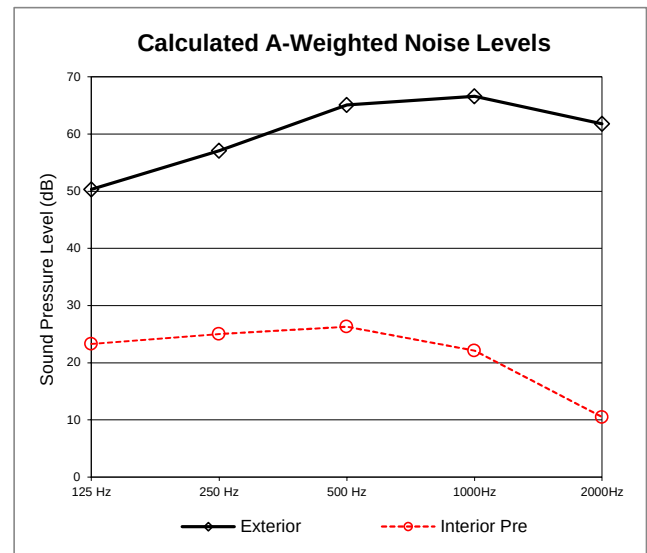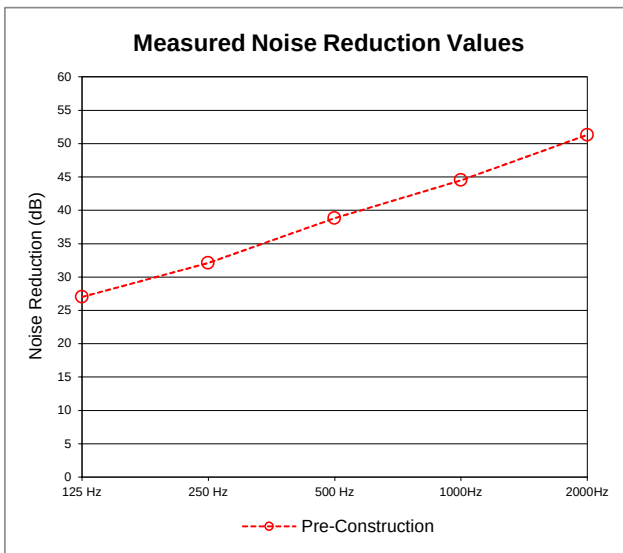

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Meza
 Address: 2637 S 150th St
 Local City: SeaTac

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	54.6	53.8	53.1	46.9	56.9
Exterior Measurement (flush)	90.8	88.9	92.0	87.7	83.8	93.0
Exterior Adjusted	84.8	82.9	86.0	81.7	77.8	87.0
Interior Background	44.7	30.4	17.5	15.5	15.6	30.0
Interior Measurement	62.5	54.8	47.6	36.8	28.6	50.6
Interior Adjusted	62.4	54.8	47.6	36.8	28.4	50.6
Noise Reduction	22.4	28.1	38.4	44.9	49.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.9	29.0	26.7	21.7	12.4	33.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.9 dB

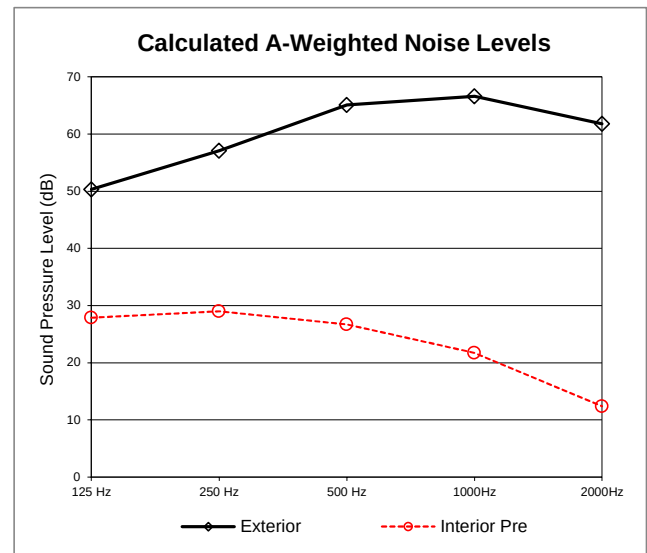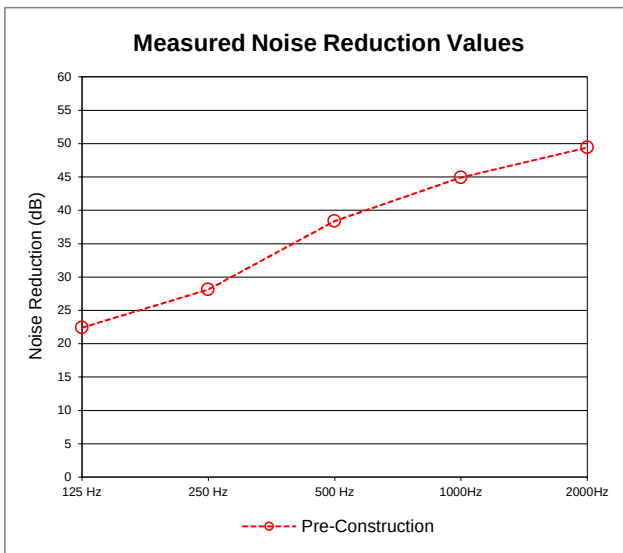

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Meza
 Address: 2637 S 150th St
 Local City: SeaTac

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 19, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	54.6	53.8	53.1	46.9	56.9
Exterior Measurement (flush)	92.5	91.2	92.0	88.4	84.3	93.8
Exterior Adjusted	86.5	85.2	86.0	82.4	78.3	87.8
Interior Background	44.7	30.4	17.5	15.5	15.6	30.0
Interior Measurement	63.4	51.0	46.2	34.7	28.2	49.1
Interior Adjusted	63.3	51.0	46.2	34.6	28.0	49.0
Noise Reduction	23.2	34.2	39.8	47.8	50.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.1	22.9	25.3	18.8	11.5	30.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						39.4 dB

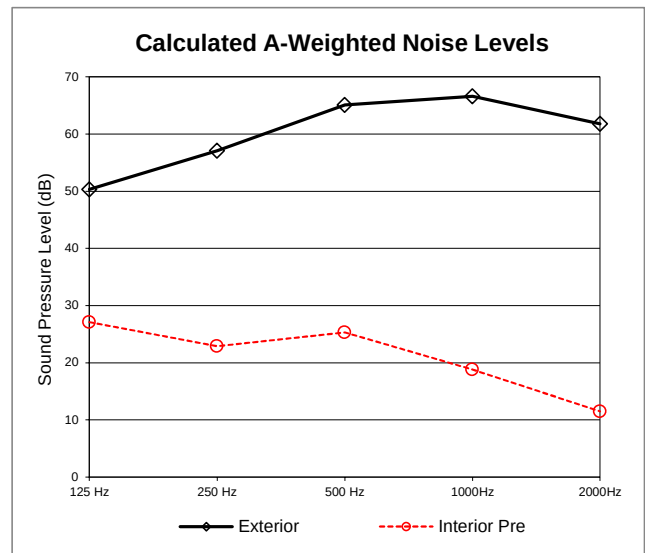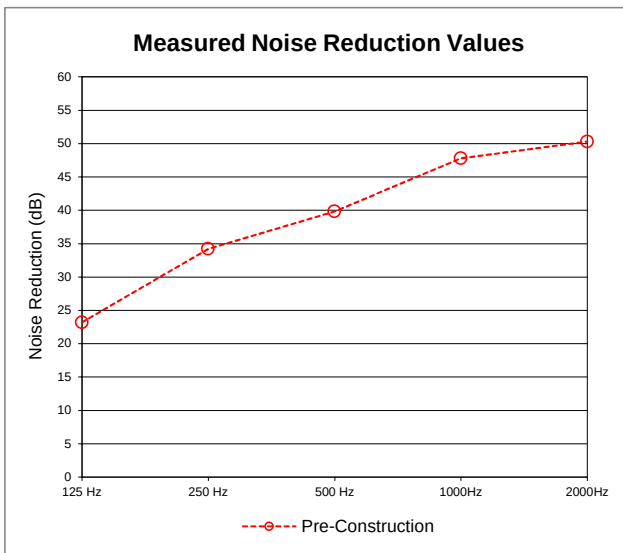



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th PI
 Local City: Burien

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.8	52.9	53.8	57.9	51.9	60.2
Exterior Measurement (flush)	87.2	90.8	91.0	88.3	84.5	94.2
Exterior Adjusted	81.2	84.8	85.0	82.3	78.5	88.2
Interior Background	41.2	32.3	29.4	24.3	19.7	31.5
Interior Measurement	60.4	54.2	52.1	45.7	37.2	52.7
Interior Adjusted	60.3	54.2	52.1	45.7	37.1	52.7
Noise Reduction	20.9	30.6	32.9	36.6	41.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.4	26.5	32.2	30.0	20.4	36.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.9 dB

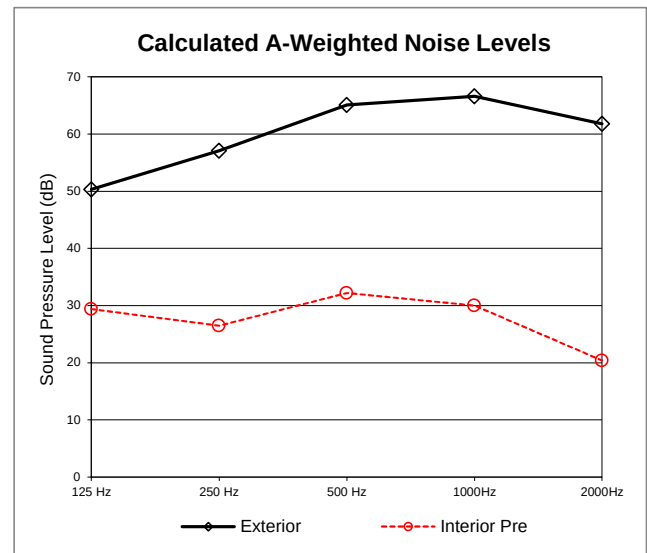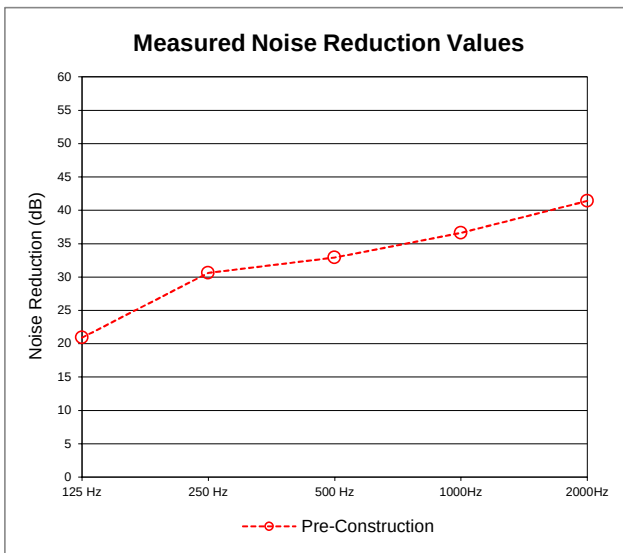

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th Pl
 Local City: Burien

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	51.2	52.2	53.2	46.6	56.3
Exterior Measurement (flush)	89.6	90.8	90.5	88.0	84.9	94.0
Exterior Adjusted	83.6	84.8	84.5	82.0	78.9	88.0
Interior Background	36.3	29.9	25.5	25.5	24.1	31.5
Interior Measurement	60.2	57.5	52.0	47.9	41.9	54.5
Interior Adjusted	60.2	57.5	52.0	47.9	41.8	54.5
Noise Reduction	23.4	27.3	32.5	34.1	37.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.9	29.8	32.6	32.5	24.7	37.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.7 dB

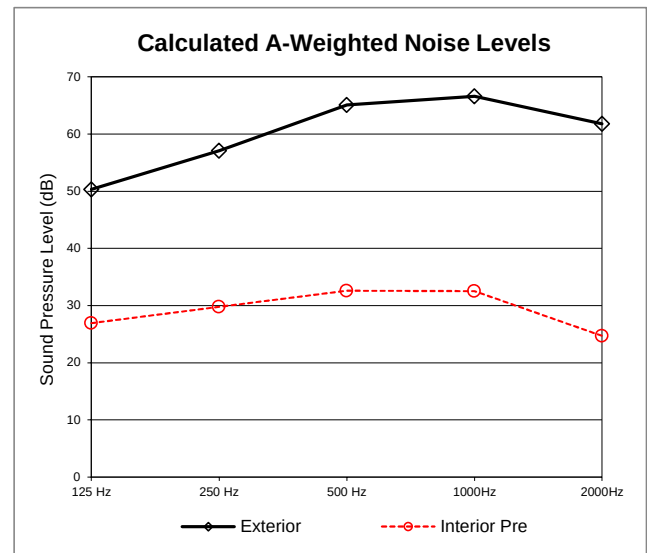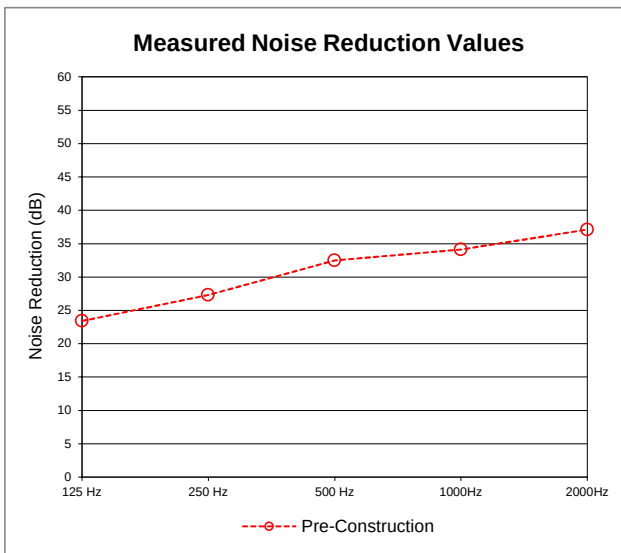



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th PI
 Local City: Burien

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.8	52.9	53.8	57.9	51.9	60.2
Exterior Measurement (flush)	92.9	95.1	96.1	93.5	90.3	98.6
Exterior Adjusted	86.9	89.1	90.1	87.5	84.3	92.6
Interior Background	33.4	22.9	16.2	17.4	16.9	26.5
Interior Measurement	64.6	60.7	55.0	48.7	40.5	56.6
Interior Adjusted	64.6	60.7	55.0	48.7	40.5	56.6
Noise Reduction	22.3	28.4	35.1	38.8	43.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.0	28.7	30.0	27.8	18.0	34.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.2 dB

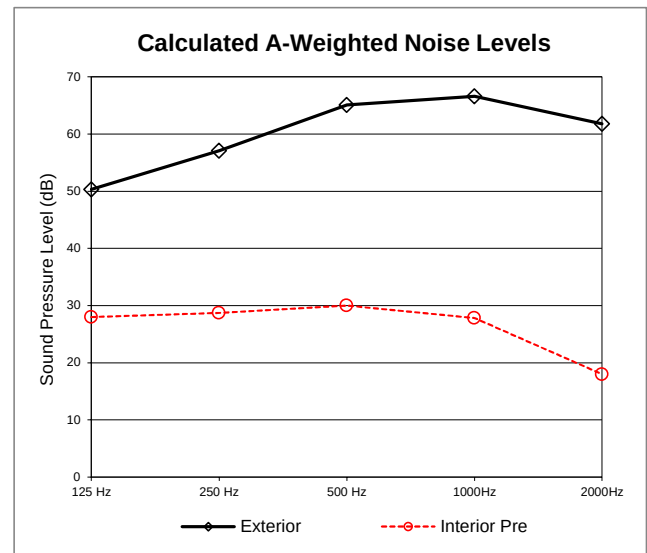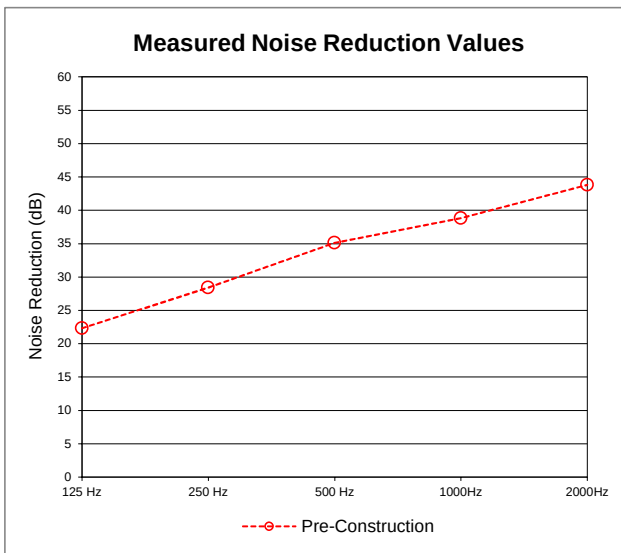



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th Pl
 Local City: Burien

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	64.8	52.9	53.8	57.9	51.9	60.2
Exterior Measurement (flush)	90.9	95.1	94.9	91.7	88.5	97.7
Exterior Adjusted	84.9	89.1	88.9	85.7	82.5	91.7
Interior Background	40.6	28.4	22.4	18.8	19.0	29.1
Interior Measurement	64.1	59.5	51.4	43.9	38.2	54.2
Interior Adjusted	64.1	59.5	51.4	43.9	38.1	54.2
Noise Reduction	20.8	29.6	37.5	41.8	44.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.5	27.5	27.6	24.8	17.4	33.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.2 dB

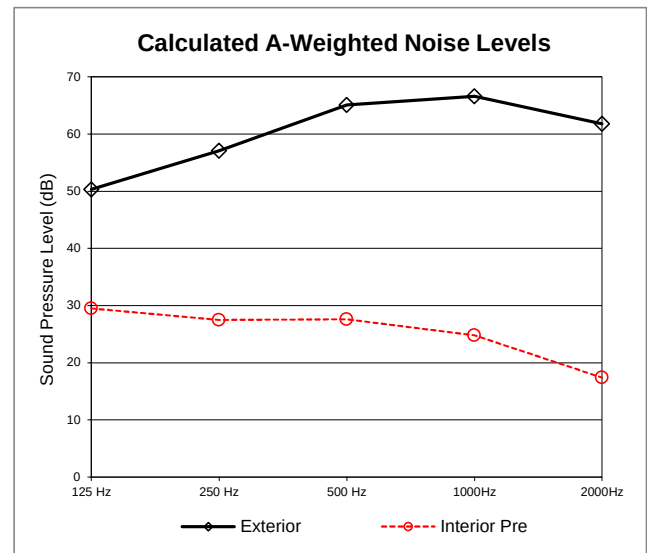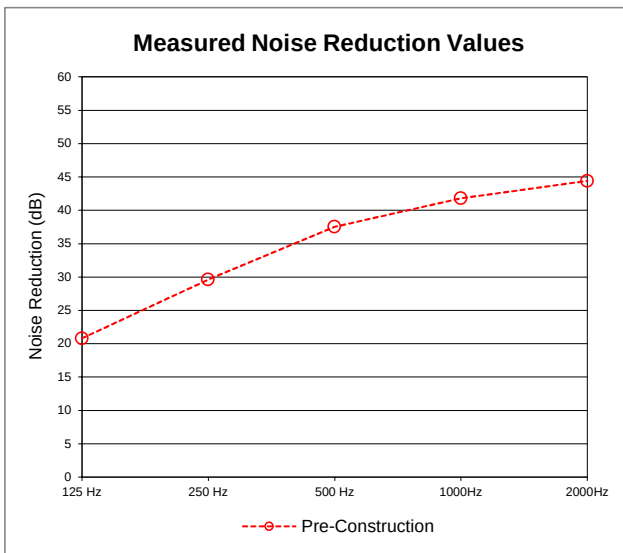

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th Pl
 Local City: Burien

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	51.2	52.2	53.2	46.6	56.3
Exterior Measurement (flush)	90.1	91.8	91.3	87.3	84.1	93.8
Exterior Adjusted	84.1	85.8	85.3	81.3	78.1	87.8
Interior Background	35.3	32.8	26.9	26.6	25.0	32.5
Interior Measurement	64.6	58.6	51.5	45.4	41.3	54.8
Interior Adjusted	64.6	58.6	51.5	45.3	41.2	54.8
Noise Reduction	19.5	27.2	33.8	36.0	36.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.8	29.9	31.3	30.6	24.9	37.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.0 dB

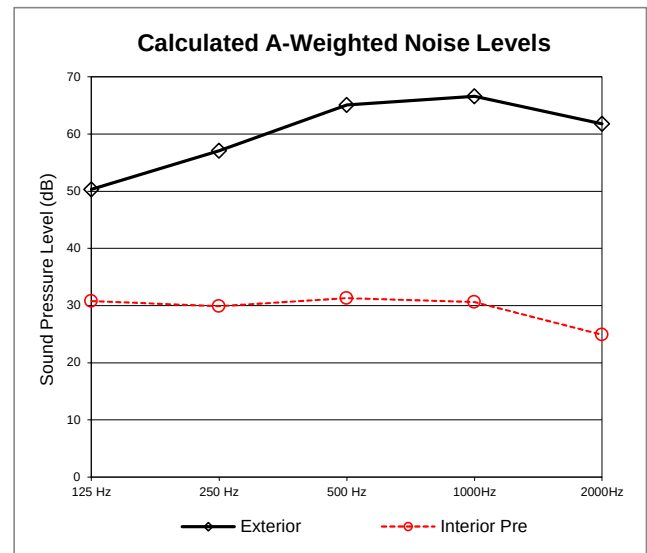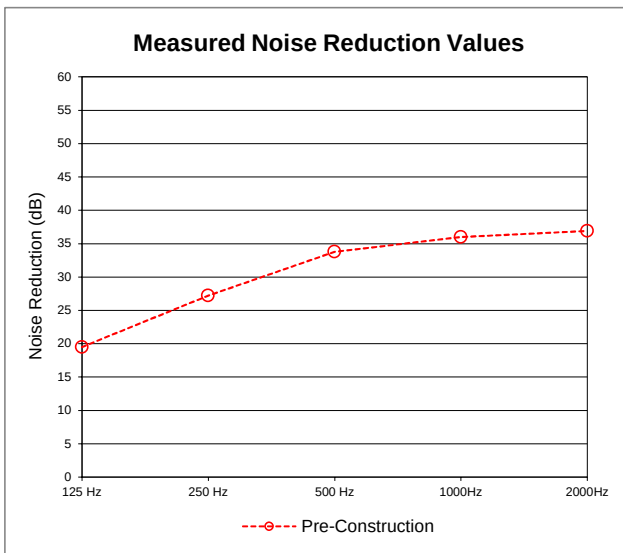



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th Pl
 Local City: Burien

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	51.2	52.2	53.2	46.6	56.3
Exterior Measurement (flush)	91.5	92.1	92.1	88.4	86.0	95.2
Exterior Adjusted	85.5	86.1	86.1	82.4	80.0	89.2
Interior Background	39.0	25.0	19.5	21.3	23.1	30.8
Interior Measurement	60.4	55.7	49.4	42.8	38.2	51.9
Interior Adjusted	60.4	55.7	49.4	42.8	38.1	51.9
Noise Reduction	25.1	30.4	36.7	39.6	41.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	25.2	26.7	28.4	27.0	19.9	33.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.8 dB

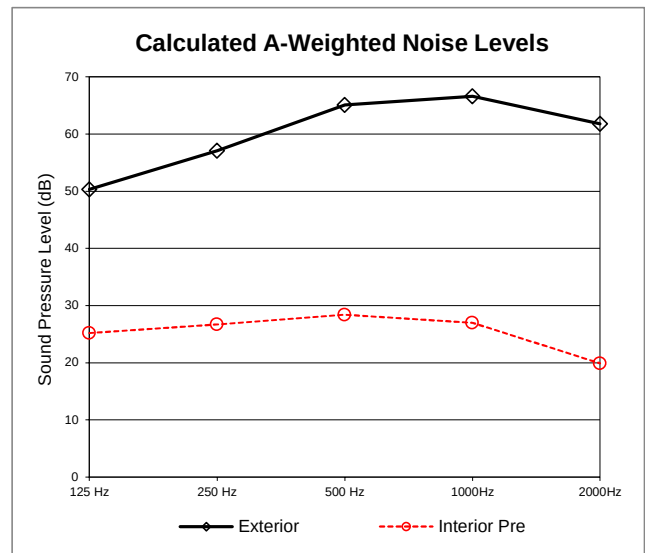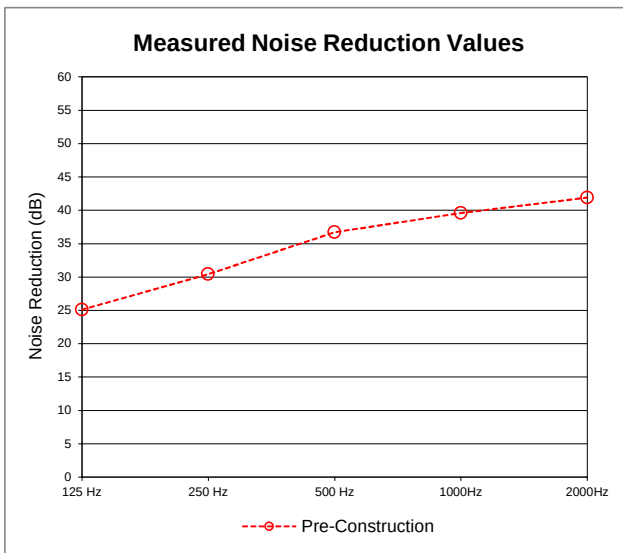



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Lindeke
 Address: 850 S 177th PI
 Local City: Burien

Tested Room: Office Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 26, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.8	56.4	55.5	57.5	50.6	60.0
Exterior Measurement (flush)	88.1	89.5	90.4	85.9	82.6	92.4
Exterior Adjusted	82.1	83.5	84.4	79.9	76.6	86.4
Interior Background	39.3	34.0	28.3	25.7	25.3	33.6
Interior Measurement	65.8	58.9	55.8	52.7	49.6	58.7
Interior Adjusted	65.8	58.9	55.8	52.7	49.6	58.7
Noise Reduction	16.3	24.6	28.6	27.2	27.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.0	32.5	36.5	39.4	34.8	43.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						26.9 dB

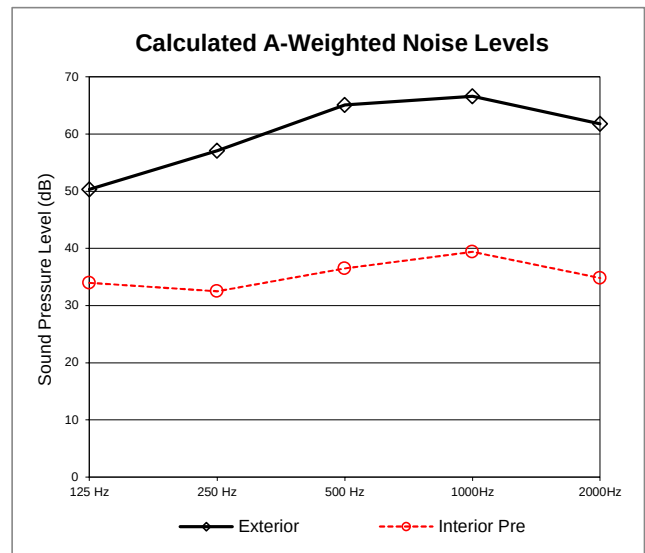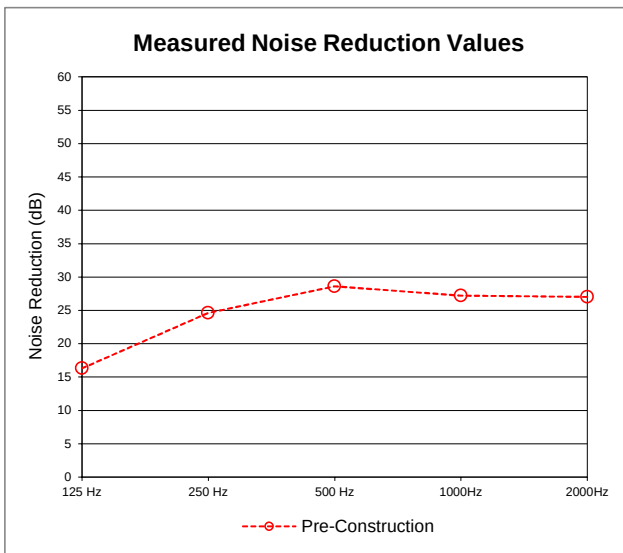

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zacher
 Address: 1020 S 202nd St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.0	52.4	53.7	57.1	49.1	58.9
Exterior Measurement (flush)	91.1	95.5	95.2	92.3	89.0	97.9
Exterior Adjusted	85.1	89.5	89.2	86.3	83.0	91.9
Interior Background	33.9	33.2	27.7	20.7	16.5	29.5
Interior Measurement	65.7	60.7	58.1	50.0	43.6	58.4
Interior Adjusted	65.7	60.7	58.1	50.0	43.6	58.4
Noise Reduction	19.4	28.8	31.1	36.3	39.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.9	28.3	34.0	30.3	22.4	37.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.5 dB

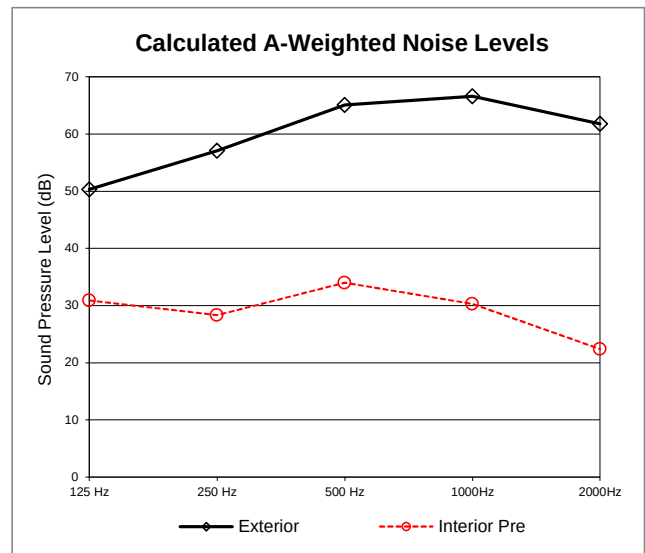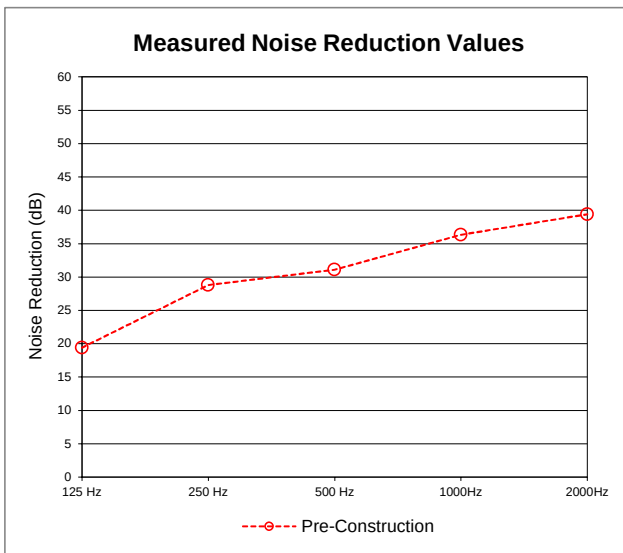

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zacher
 Address: 1020 S 202nd St
 Local City: Des Moines

Tested Room: Sitting Room Façade 1
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.4	54.3	55.7	55.8	47.8	58.4
Exterior Measurement (flush)	94.2	98.8	97.3	93.3	89.8	99.6
Exterior Adjusted	88.2	92.8	91.3	87.3	83.8	93.6
Interior Background	43.0	31.4	24.9	21.2	18.7	31.7
Interior Measurement	73.3	63.5	60.0	49.5	39.9	61.5
Interior Adjusted	73.3	63.5	60.0	49.5	39.9	61.5
Noise Reduction	14.9	29.3	31.3	37.8	43.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.4	27.8	33.8	28.8	17.9	38.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.4 dB

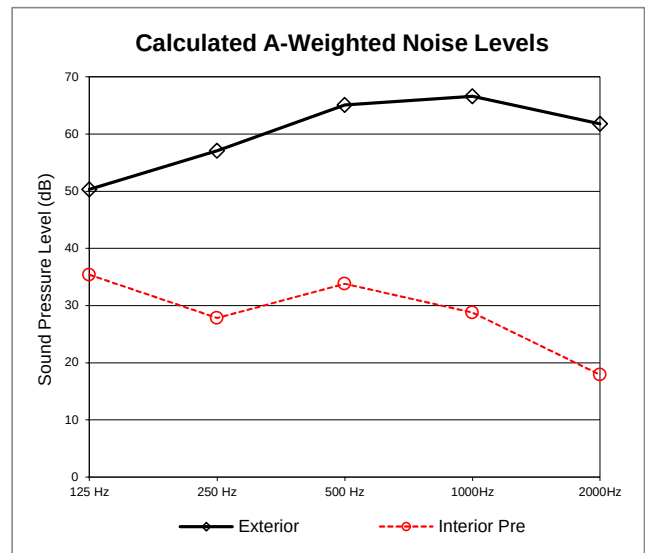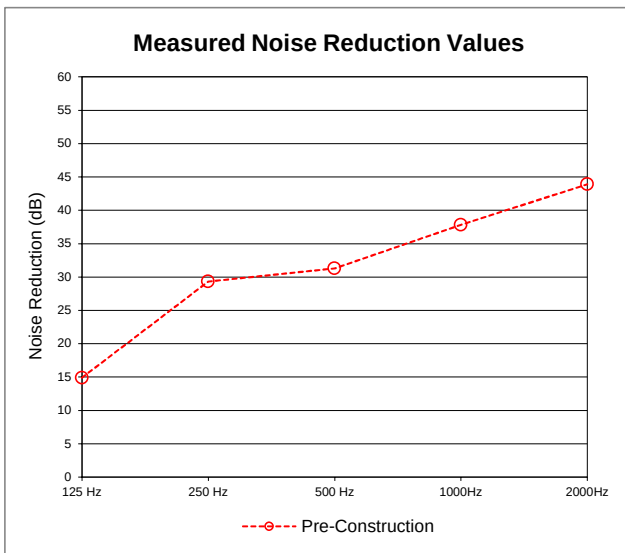



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zacher
 Address: 1020 S 202nd St
 Local City: Des Moines

Tested Room: Sitting Room Façade 2
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.4	54.3	55.7	55.8	47.8	58.4
Exterior Measurement (flush)	89.3	90.9	92.7	90.2	85.5	95.2
Exterior Adjusted	83.3	84.9	86.7	84.2	79.5	89.2
Interior Background	43.0	31.4	24.9	21.2	18.7	31.7
Interior Measurement	68.3	58.2	53.5	47.6	39.3	56.4
Interior Adjusted	68.3	58.2	53.5	47.6	39.3	56.4
Noise Reduction	15.0	26.7	33.2	36.6	40.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.3	30.4	31.9	30.0	21.6	38.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.4 dB

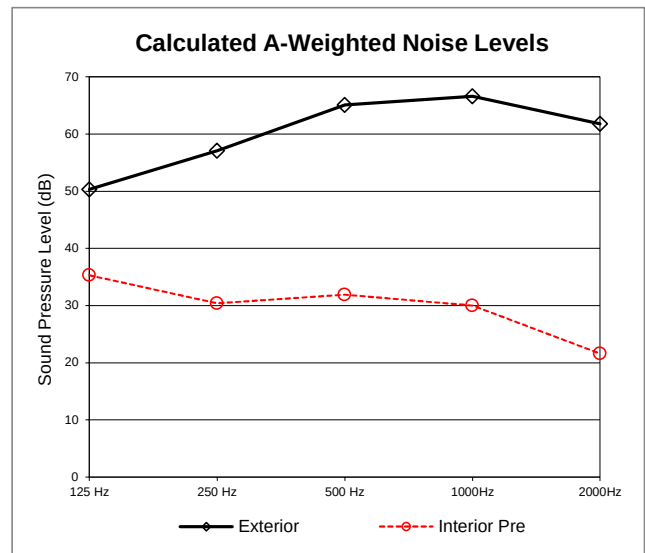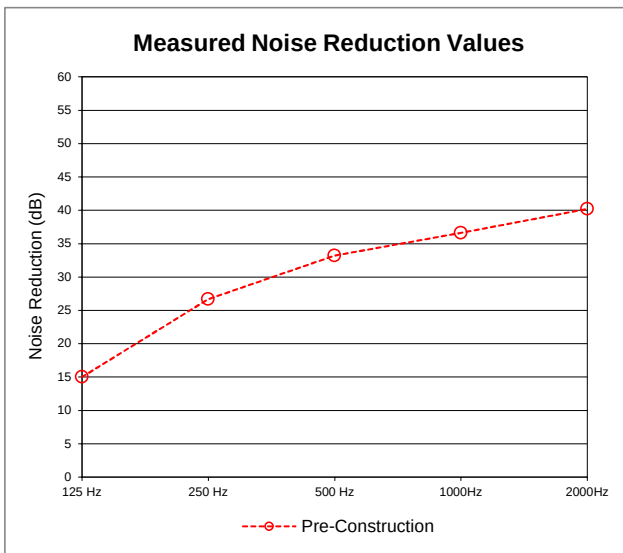

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zacher
 Address: 1020 S 202nd St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.0	52.4	53.7	57.1	49.1	58.9
Exterior Measurement (flush)	90.0	89.4	91.7	88.2	85.3	94.2
Exterior Adjusted	84.0	83.4	85.7	82.2	79.3	88.2
Interior Background	28.6	23.2	16.9	15.4	13.0	22.9
Interior Measurement	63.4	56.7	50.4	42.6	36.1	52.9
Interior Adjusted	63.4	56.7	50.4	42.6	36.1	52.9
Noise Reduction	20.6	26.7	35.3	39.6	43.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.7	30.4	29.8	27.0	18.6	35.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.5 dB

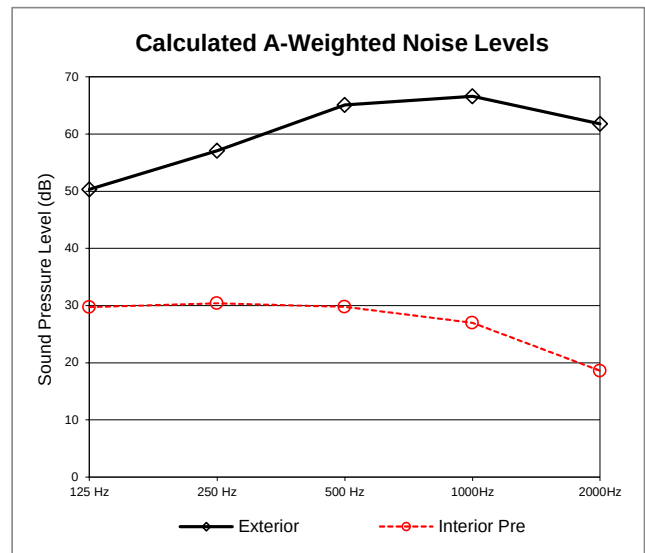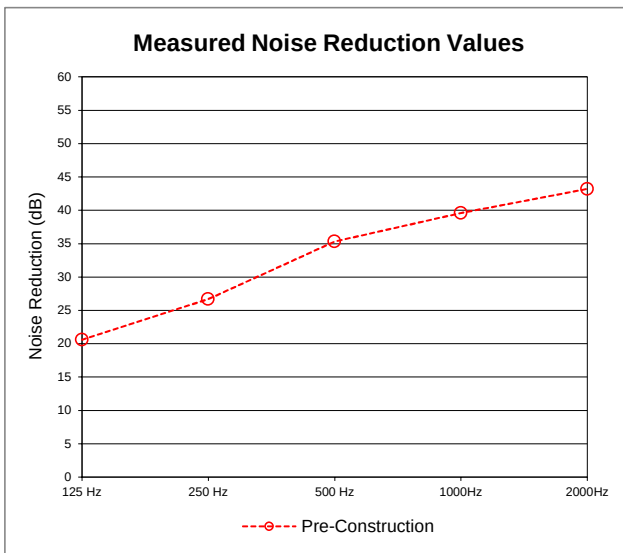



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zacher
 Address: 1020 S 202nd St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.0	63.3	57.8	52.0	43.3	59.3
Exterior Measurement (flush)	94.2	98.8	97.3	93.3	89.8	99.6
Exterior Adjusted	88.2	92.8	91.3	87.3	83.8	93.6
Interior Background	42.3	35.0	24.2	21.7	21.1	31.5
Interior Measurement	68.2	62.8	55.1	45.4	34.9	57.7
Interior Adjusted	68.2	62.8	55.1	45.4	34.7	57.7
Noise Reduction	20.0	30.0	36.2	41.9	49.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.3	27.1	28.9	24.7	12.7	34.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.7 dB

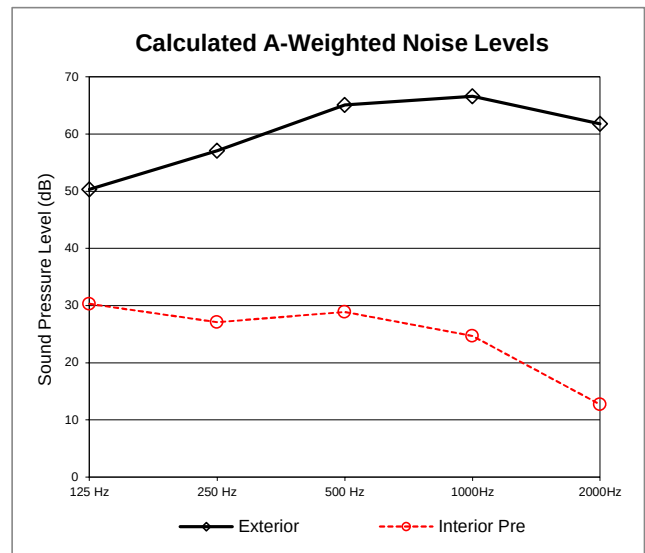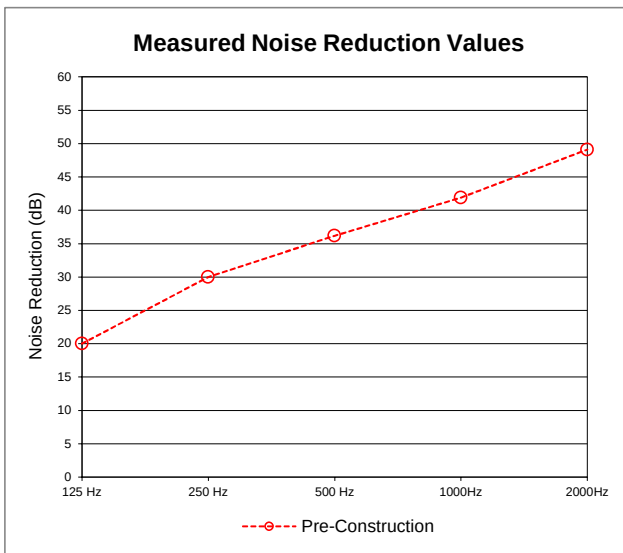



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Zacher
 Address: 1020 S 202nd St
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 25, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	57.0	52.4	53.7	57.1	49.1	58.9
Exterior Measurement (flush)	88.3	93.9	92.7	90.8	87.9	96.2
Exterior Adjusted	82.3	87.9	86.7	84.8	81.9	90.2
Interior Background	35.9	31.9	21.9	17.2	14.7	27.4
Interior Measurement	60.6	53.1	49.5	41.9	34.6	50.6
Interior Adjusted	60.6	53.1	49.5	41.9	34.6	50.6
Noise Reduction	21.7	34.8	37.2	42.9	47.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.6	22.3	27.9	23.7	14.5	32.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						37.5 dB

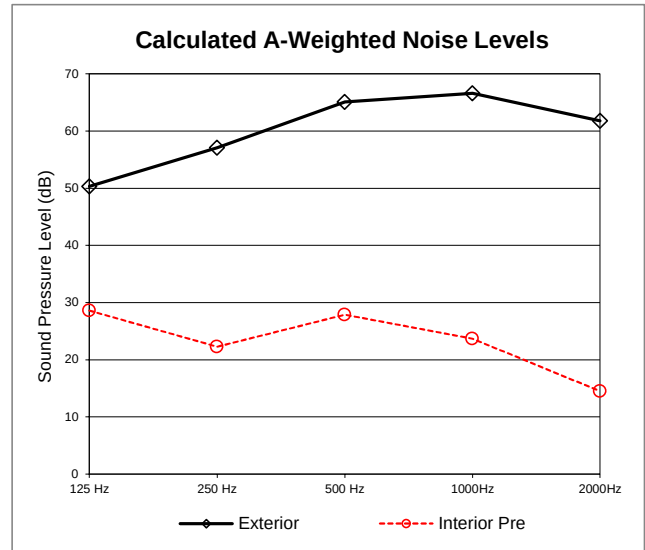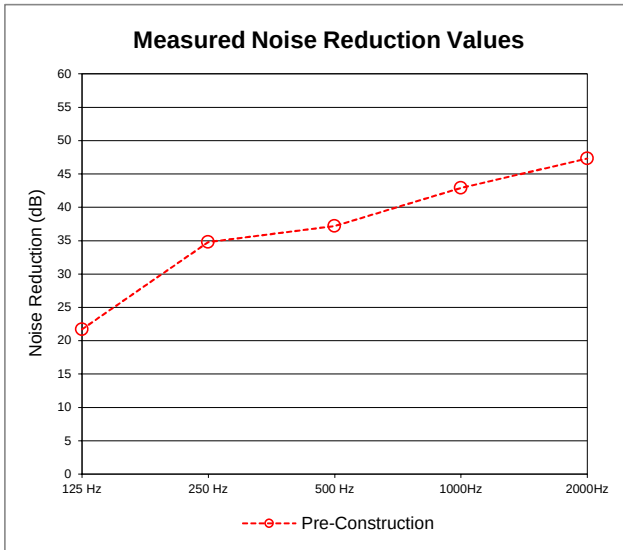



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Reeder
 Address: 925 S 206th St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	72.3	73.5	69.0	59.7	48.7	68.9
Exterior Measurement (flush)	91.0	91.6	92.3	89.8	86.6	94.7
Exterior Adjusted	84.9	85.5	86.3	83.8	80.6	88.7
Interior Background	40.7	35.4	31.1	27.5	26.9	35.6
Interior Measurement	62.4	58.9	54.4	46.0	40.0	55.1
Interior Adjusted	62.4	58.9	54.4	45.9	39.8	55.1
Noise Reduction	22.5	26.6	31.9	37.9	40.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.8	30.5	33.2	28.7	21.0	36.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.3 dB

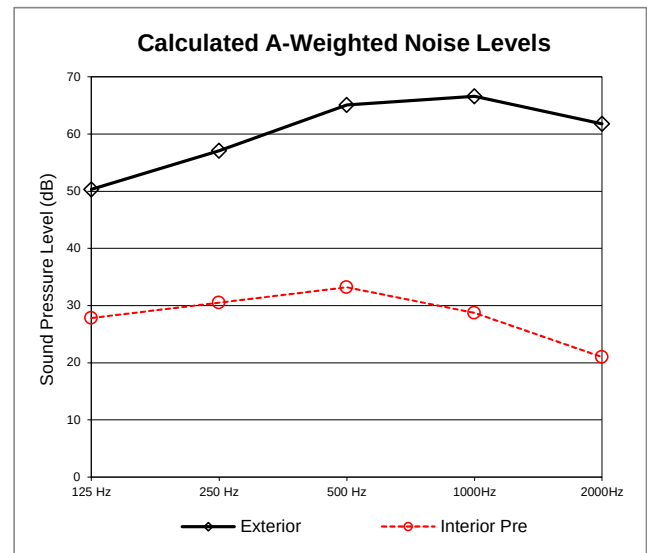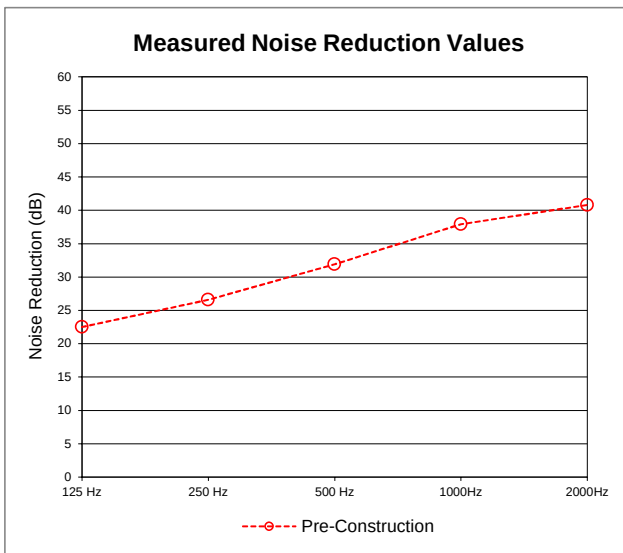

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Reeder
 Address: 925 S 206th St
 Local City: Des Moines

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	58.0	53.1	53.8	50.8	40.0	54.7
Exterior Measurement (flush)	90.4	87.7	92.4	89.6	86.2	95.2
Exterior Adjusted	84.4	81.7	86.4	83.6	80.2	89.2
Interior Background	35.7	27.8	23.6	18.0	16.9	28.4
Interior Measurement	62.5	53.9	51.7	45.0	34.6	52.9
Interior Adjusted	62.5	53.9	51.7	45.0	34.5	52.9
Noise Reduction	21.9	27.8	34.7	38.6	45.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.4	29.3	30.4	28.0	16.1	35.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.8 dB

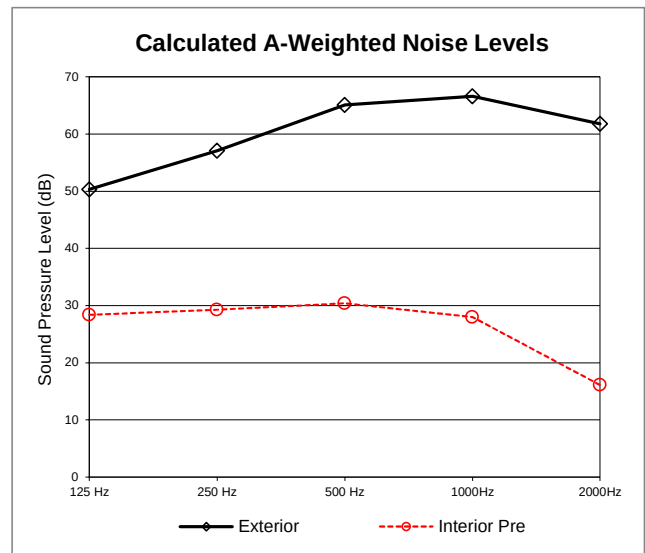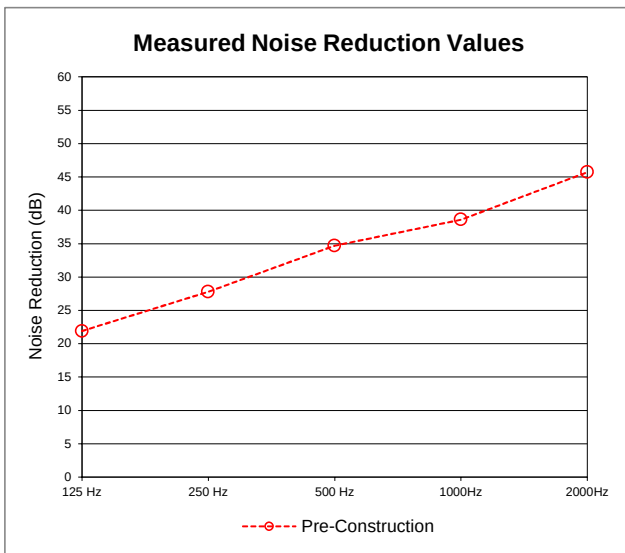



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Reeder
 Address: 925 S 206th St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.9	63.9	61.4	59.5	51.1	63.1
Exterior Measurement (flush)	90.0	88.9	90.9	87.8	86.2	93.5
Exterior Adjusted	84.0	82.9	84.9	81.8	80.2	87.5
Interior Background	42.9	37.4	26.2	20.2	16.1	32.8
Interior Measurement	62.9	56.8	52.3	44.4	35.3	53.3
Interior Adjusted	62.9	56.7	52.3	44.4	35.2	53.3
Noise Reduction	21.1	26.2	32.6	37.4	45.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.2	30.9	32.5	29.2	16.8	36.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.3 dB

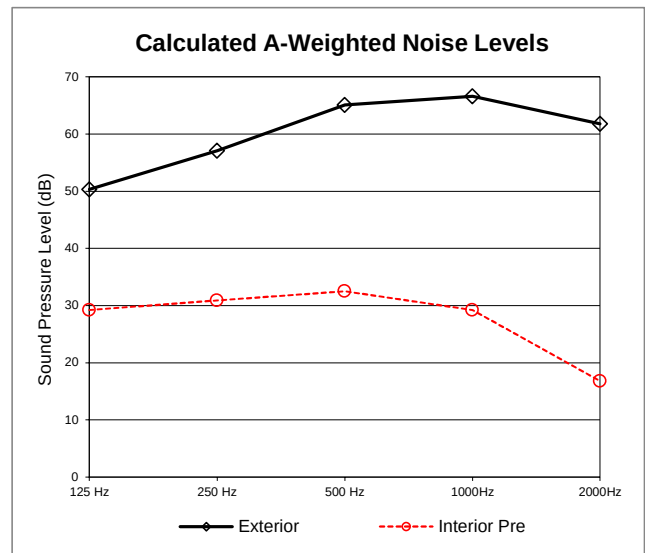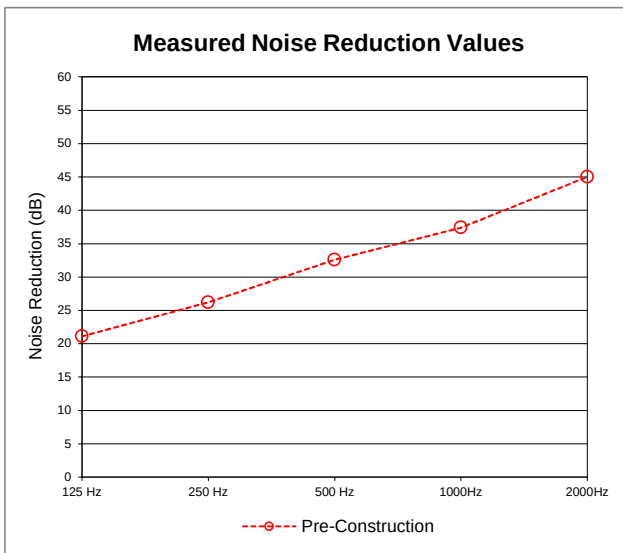



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Reeder
 Address: 925 S 206th St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.9	63.9	61.4	59.5	51.1	63.1
Exterior Measurement (flush)	92.6	91.5	92.5	89.9	85.5	95.1
Exterior Adjusted	86.6	85.5	86.5	83.9	79.5	89.1
Interior Background	49.4	38.2	30.4	26.2	20.9	37.8
Interior Measurement	69.2	63.5	59.0	52.2	42.5	60.5
Interior Adjusted	69.2	63.5	59.0	52.2	42.5	60.5
Noise Reduction	17.4	22.0	27.5	31.7	37.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.9	35.1	37.6	34.9	24.8	41.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.4 dB

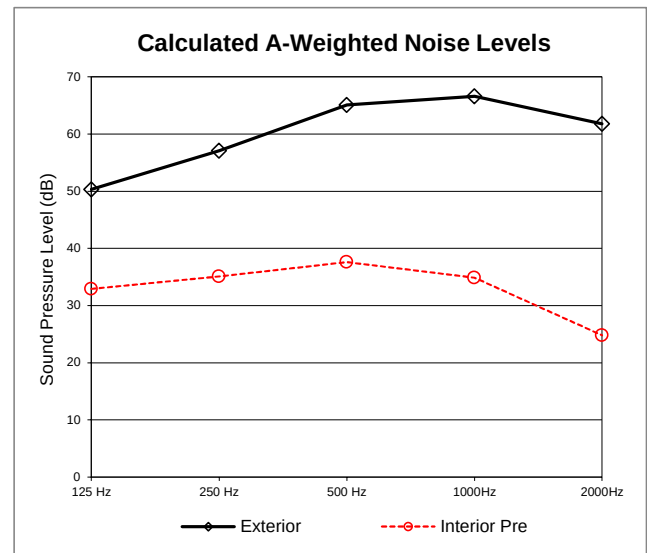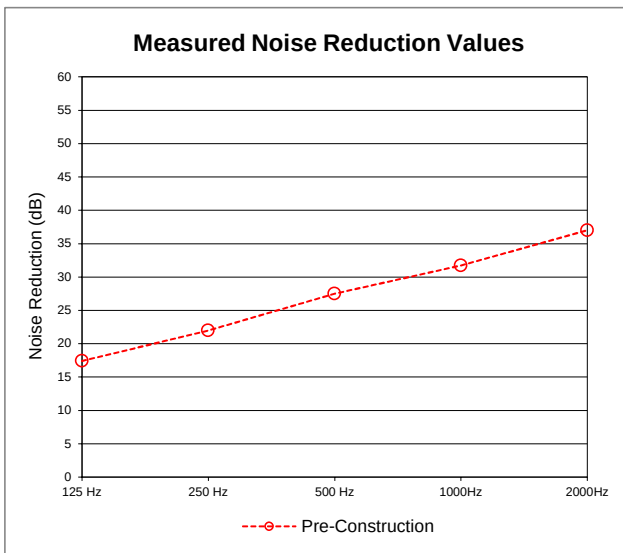



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Reeder
 Address: 925 S 206th St
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	72.3	73.5	69.0	59.7	48.7	68.9
Exterior Measurement (flush)	99.8	98.1	96.7	93.9	90.1	99.6
Exterior Adjusted	93.8	92.1	90.7	87.9	84.1	93.6
Interior Background	32.8	26.1	20.5	16.7	18.5	27.1
Interior Measurement	71.7	62.1	59.2	49.1	40.2	60.1
Interior Adjusted	71.7	62.1	59.2	49.1	40.2	60.1
Noise Reduction	22.1	30.0	31.5	38.8	43.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.2	27.1	33.6	27.8	17.9	36.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.8 dB

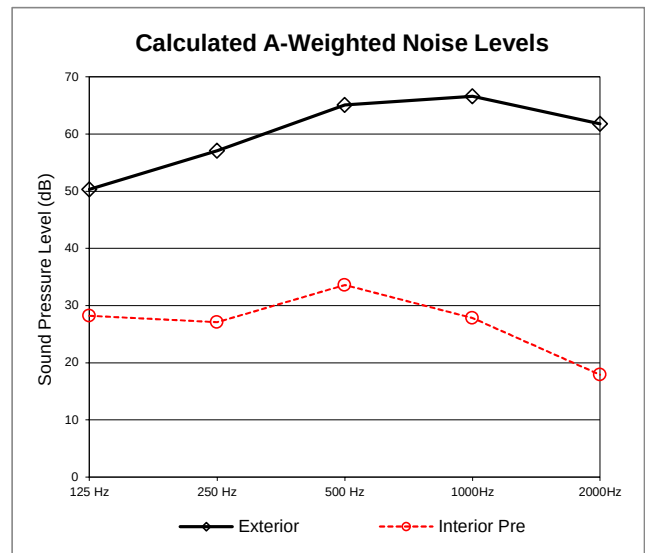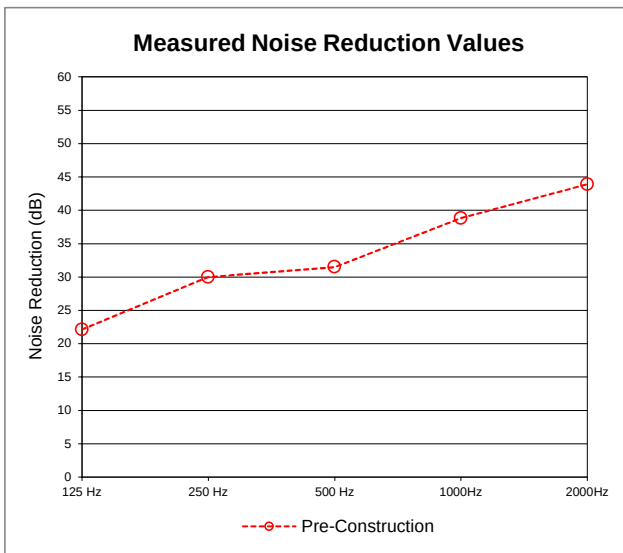



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Reeder
 Address: 925 S 206th St
 Local City: Des Moines

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.4	56.2	53.3	51.0	44.5	55.8
Exterior Measurement (flush)	111.3	110.5	108.3	102.0	101.2	111.1
Exterior Adjusted	105.3	104.5	102.3	96.0	95.2	105.1
Interior Background	28.5	22.9	12.8	8.7	9.2	20.4
Interior Measurement	72.6	69.0	64.0	54.8	42.2	64.8
Interior Adjusted	72.6	69.0	64.0	54.8	42.2	64.8
Noise Reduction	32.7	35.5	38.3	41.2	53.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	17.6	21.6	26.8	25.4	8.8	30.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						39.9 dB

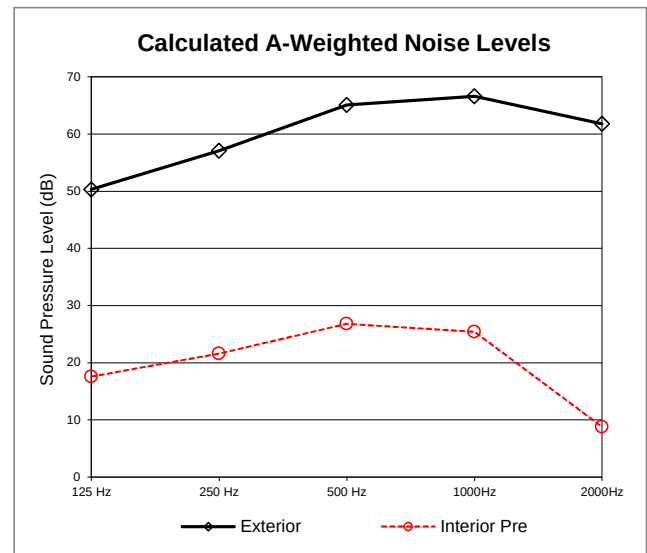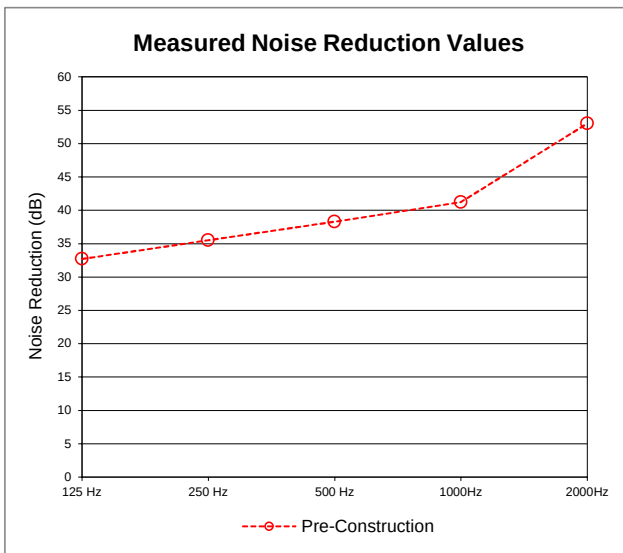



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.6	60.1	56.2	54.6	51.8	61.7
Exterior Measurement (flush)	84.1	79.9	84.5	81.0	78.4	87.2
Exterior Adjusted	77.9	73.9	78.5	75.0	72.4	81.2
Interior Background	44.0	25.2	22.1	18.6	18.3	33.7
Interior Measurement	55.7	45.6	42.8	38.8	34.4	45.6
Interior Adjusted	55.4	45.6	42.8	38.8	34.3	45.3
Noise Reduction	22.5	28.3	35.7	36.2	38.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.8	28.8	29.4	30.4	23.7	35.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.5 dB

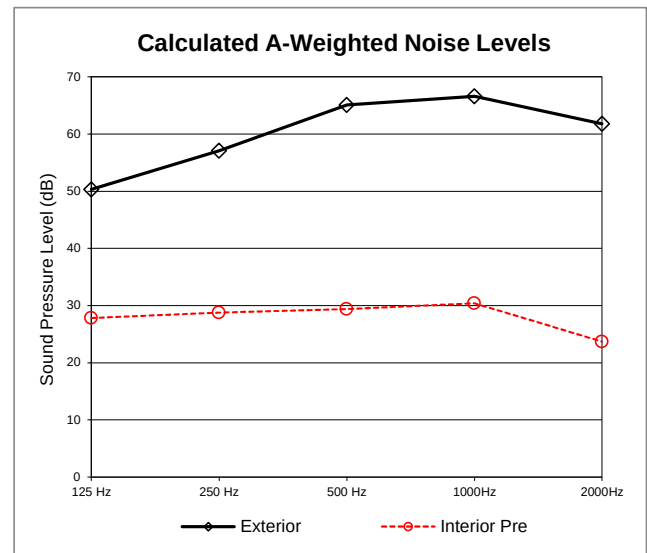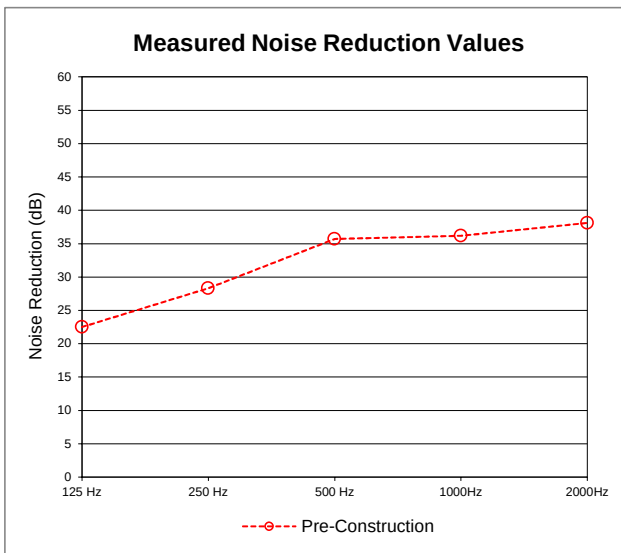

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Dining Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.1	50.7	51.3	50.5	42.3	53.8
Exterior Measurement (flush)	92.8	93.3	95.2	88.6	87.3	96.5
Exterior Adjusted	86.8	87.3	89.2	82.6	81.3	90.5
Interior Background	41.1	37.6	33.5	30.3	28.2	36.6
Interior Measurement	64.9	63.0	59.2	55.3	50.7	60.9
Interior Adjusted	64.9	63.0	59.2	55.3	50.7	60.9
Noise Reduction	21.9	24.3	30.0	27.3	30.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.4	32.8	35.1	39.3	31.2	41.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.1 dB

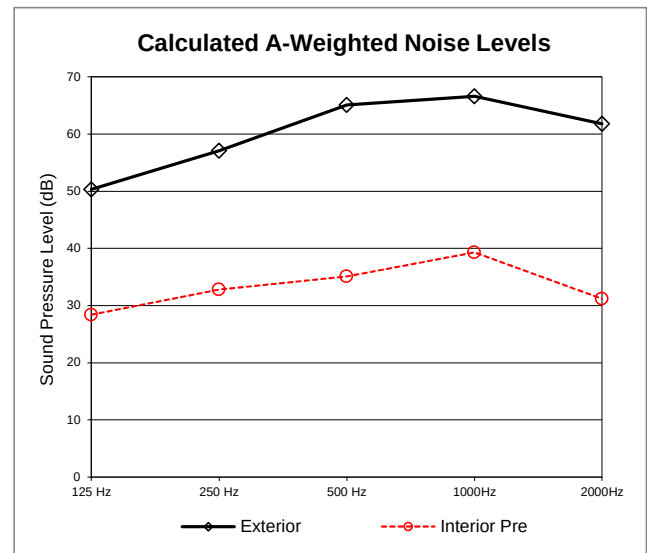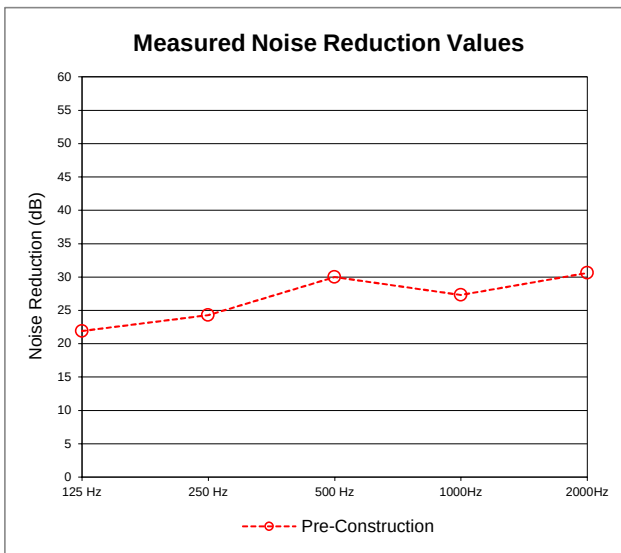



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.1	50.7	51.3	50.5	42.3	53.8
Exterior Measurement (flush)	86.5	90.6	89.6	87.9	86.1	93.9
Exterior Adjusted	80.5	84.6	83.6	81.9	80.1	87.9
Interior Background	37.6	32.0	31.2	29.7	27.7	35.3
Interior Measurement	61.5	56.2	50.4	44.2	40.9	52.8
Interior Adjusted	61.5	56.2	50.3	44.0	40.7	52.7
Noise Reduction	19.0	28.4	33.3	37.9	39.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.3	28.7	31.8	28.7	22.4	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

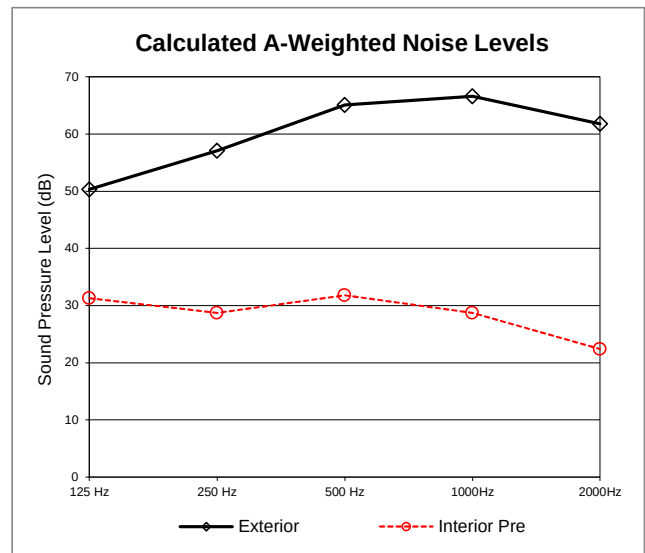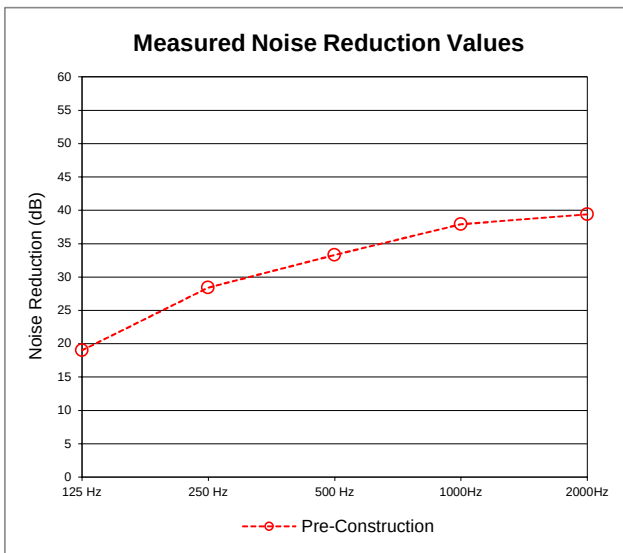



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.6	60.1	56.2	54.6	51.8	61.7
Exterior Measurement (flush)	84.5	77.1	85.0	80.5	77.7	86.5
Exterior Adjusted	78.4	71.0	79.0	74.5	71.7	80.5
Interior Background	40.8	32.4	28.0	30.0	20.4	33.5
Interior Measurement	56.5	45.6	45.1	38.9	35.3	46.5
Interior Adjusted	56.4	45.4	45.0	38.3	35.2	46.3
Noise Reduction	22.0	25.6	34.0	36.2	36.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.3	31.5	31.1	30.4	25.3	36.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.2 dB

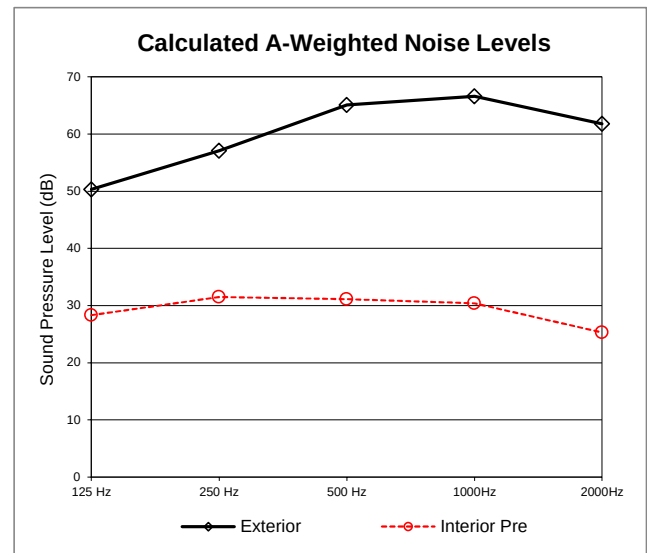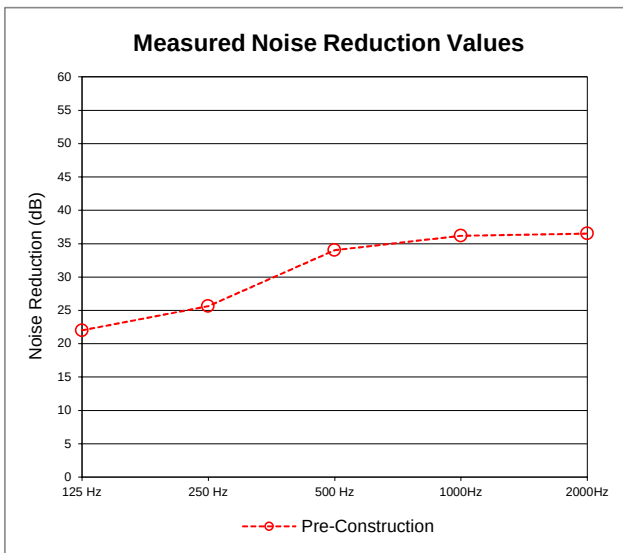



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.6	60.1	56.2	54.6	51.8	61.7
Exterior Measurement (flush)	84.4	77.5	82.5	78.8	77.6	85.2
Exterior Adjusted	78.3	71.4	76.5	72.8	71.6	79.2
Interior Background	39.3	25.8	20.1	21.5	19.1	38.8
Interior Measurement	53.4	39.6	37.3	31.6	28.7	43.3
Interior Adjusted	53.2	39.4	37.2	31.2	28.2	42.0
Noise Reduction	25.1	32.0	39.3	41.6	43.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	25.2	25.1	25.8	25.0	18.4	31.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						38.5 dB

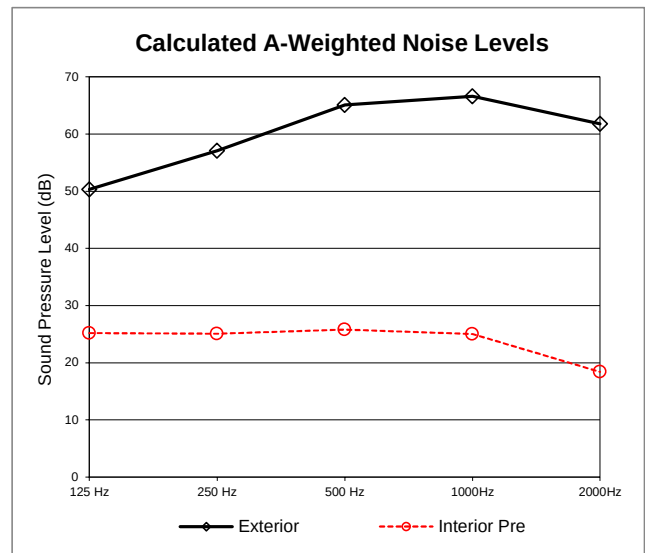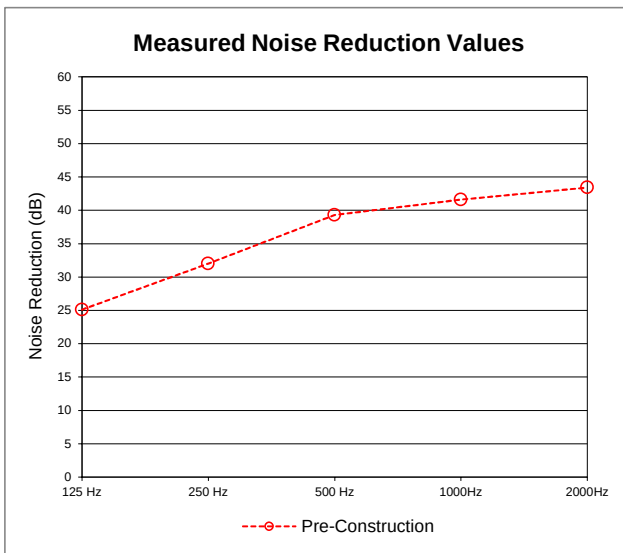



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Bedroom 3 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.6	60.1	56.2	54.6	51.8	61.7
Exterior Measurement (flush)	84.2	74.9	81.8	79.4	76.5	84.2
Exterior Adjusted	78.0	68.8	75.8	73.4	70.5	78.2
Interior Background	40.8	32.4	28.0	30.0	20.4	33.5
Interior Measurement	58.3	49.8	53.0	48.1	42.1	53.4
Interior Adjusted	58.2	49.7	53.0	48.0	42.1	53.4
Noise Reduction	19.8	19.1	22.8	25.4	28.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.5	38.0	42.3	41.2	33.4	46.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						24.0 dB

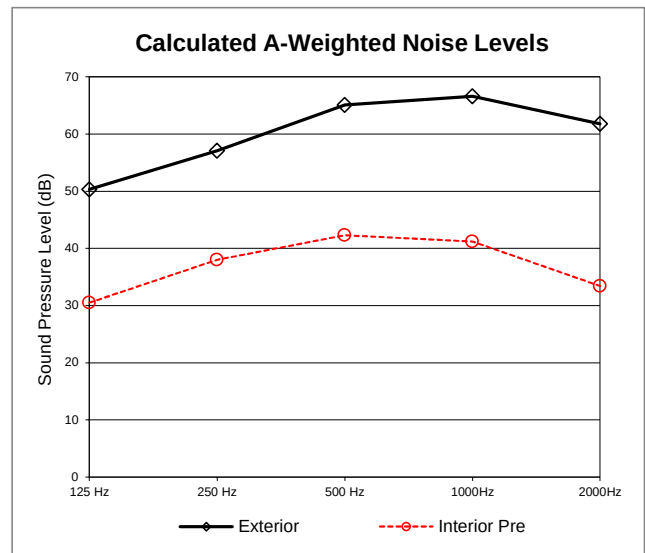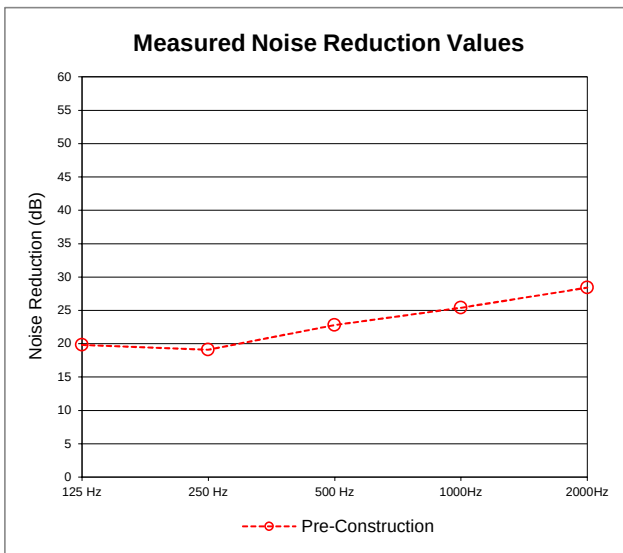

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Bedroom 3 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.6	60.1	56.2	54.6	51.8	61.7
Exterior Measurement (flush)	88.9	93.1	90.2	87.3	87.5	94.7
Exterior Adjusted	82.8	87.1	84.2	81.3	81.5	88.7
Interior Background	40.8	32.4	28.0	30.0	20.4	33.5
Interior Measurement	65.2	56.5	50.3	43.1	37.6	53.2
Interior Adjusted	65.2	56.5	50.3	42.9	37.5	53.2
Noise Reduction	17.6	30.6	33.9	38.4	44.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.7	26.5	31.2	28.2	17.8	36.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.6 dB

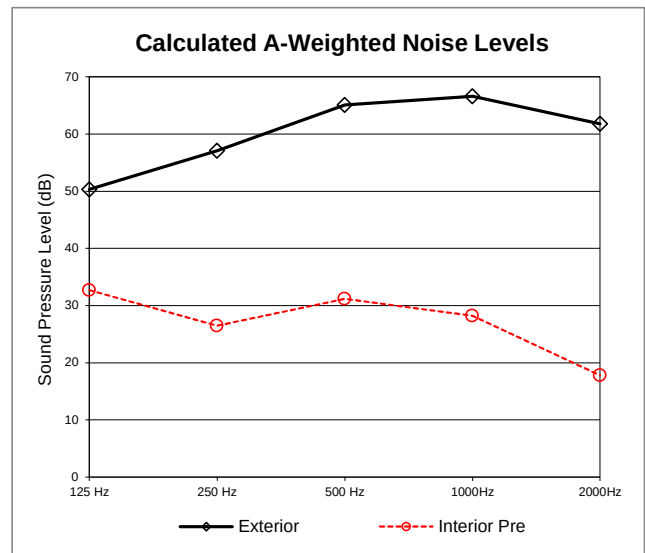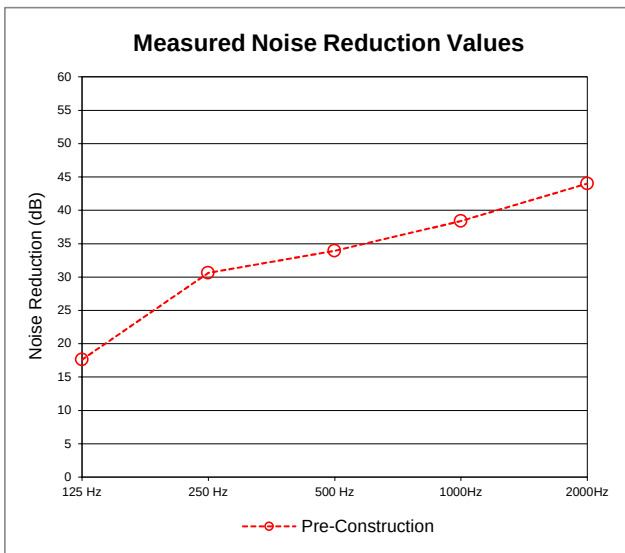



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Office Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.0	60.1	59.2	55.4	44.1	60.0
Exterior Measurement (flush)	88.2	92.6	91.2	88.0	86.5	94.9
Exterior Adjusted	82.2	86.6	85.2	82.0	80.5	88.9
Interior Background	39.9	30.7	27.5	21.9	20.7	31.7
Interior Measurement	62.6	56.4	49.2	41.6	39.9	52.6
Interior Adjusted	62.6	56.4	49.2	41.6	39.8	52.6
Noise Reduction	19.6	30.2	36.0	40.4	40.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.7	26.9	29.1	26.2	21.1	34.8
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.2 dB

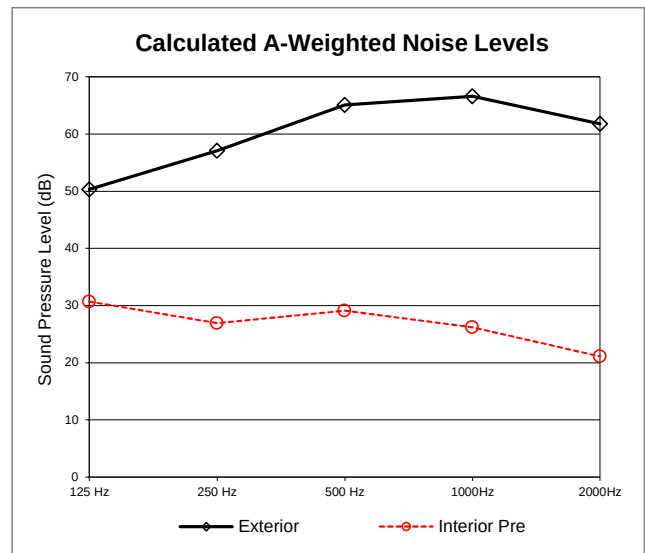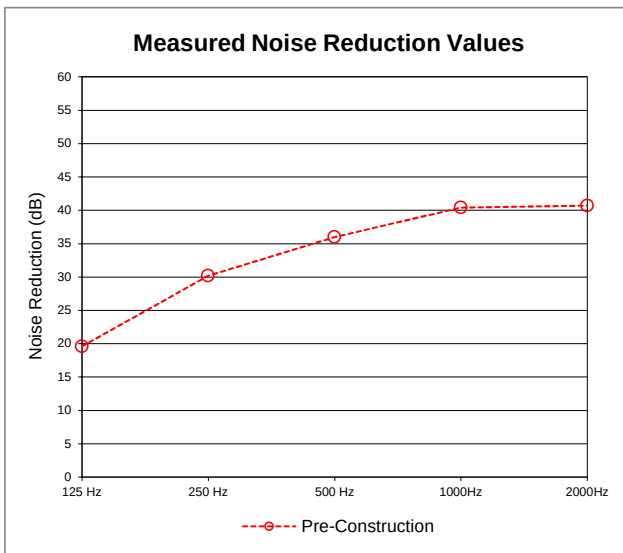



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: McCaughan
 Address: 2209 S 222nd St
 Local City: Des Moines

Tested Room: Office Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 23, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	62.0	60.1	59.2	55.4	44.1	60.0
Exterior Measurement (flush)	90.1	92.8	92.9	89.5	88.3	96.2
Exterior Adjusted	84.1	86.8	86.9	83.5	82.3	90.2
Interior Background	39.9	30.7	27.5	21.9	20.7	31.7
Interior Measurement	64.8	57.3	51.8	45.2	38.6	54.1
Interior Adjusted	64.8	57.3	51.8	45.2	38.5	54.1
Noise Reduction	19.3	29.5	35.1	38.3	43.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.0	27.6	30.0	28.3	18.0	35.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.5 dB

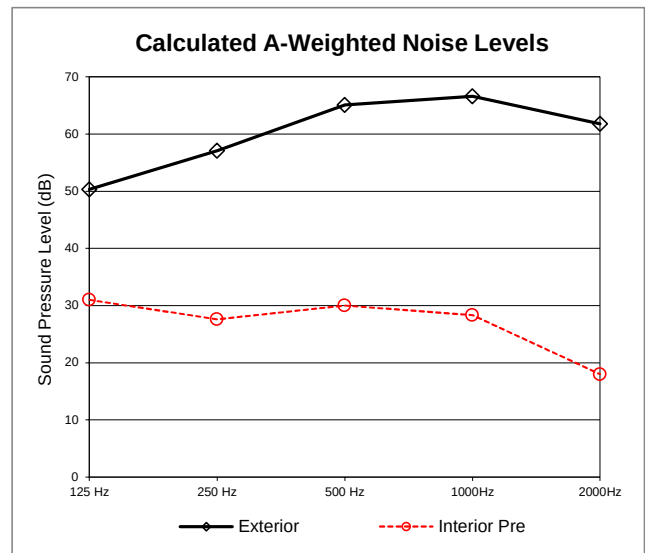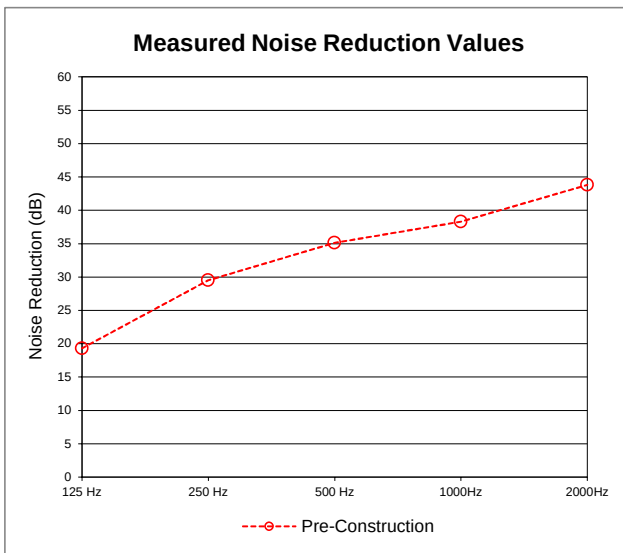



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Rivera & Boyle
 Address: 2035 S 229th St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.7	46.0	44.6	43.4	44.5	50.9
Exterior Measurement (flush)	89.5	92.1	95.0	90.9	87.5	96.5
Exterior Adjusted	83.5	86.1	89.0	84.9	81.5	90.5
Interior Background	47.0	35.8	25.5	21.9	18.0	34.0
Interior Measurement	66.2	58.2	53.9	46.3	39.5	55.5
Interior Adjusted	66.1	58.2	53.9	46.3	39.5	55.5
Noise Reduction	17.4	27.9	35.1	38.6	42.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.9	29.2	30.0	28.0	19.8	36.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.5 dB

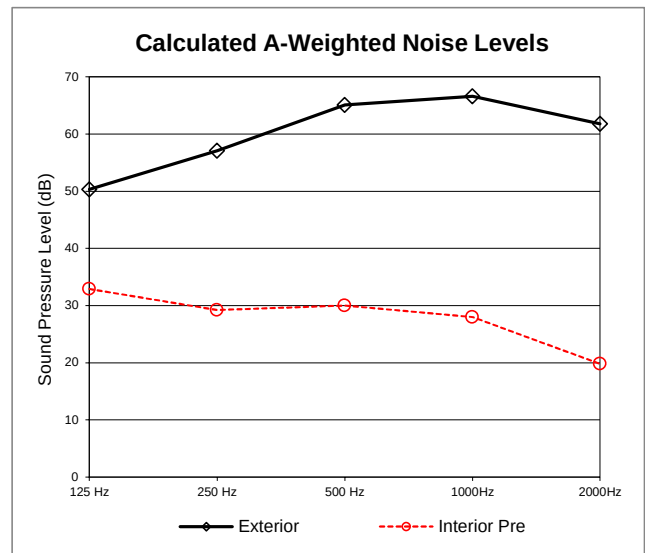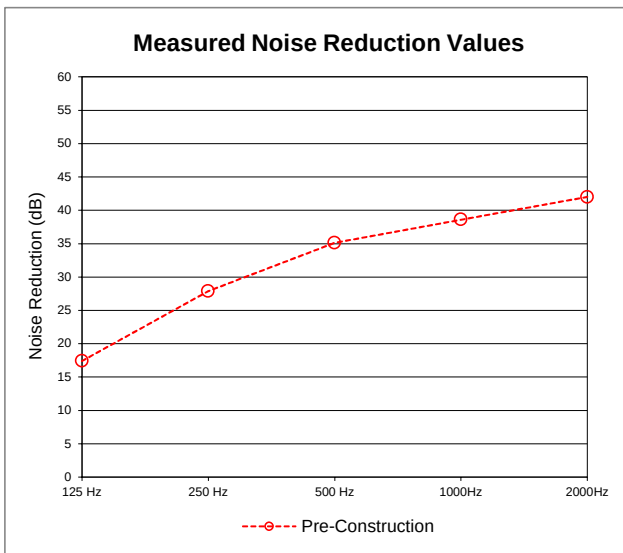



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Rivera & Boyle
 Address: 2035 S 229th St
 Local City: Des Moines

Tested Room: Sitting / Dining / Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	53.9	54.1	52.7	43.6	55.9
Exterior Measurement (flush)	87.4	84.4	89.0	84.4	81.6	90.2
Exterior Adjusted	81.4	78.4	83.0	78.4	75.6	84.2
Interior Background	40.9	36.9	29.8	27.2	21.9	33.9
Interior Measurement	63.4	53.6	49.6	44.5	42.2	52.6
Interior Adjusted	63.4	53.5	49.6	44.4	42.2	52.5
Noise Reduction	18.0	24.9	33.4	34.0	33.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.3	32.2	31.7	32.6	28.4	38.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.3 dB

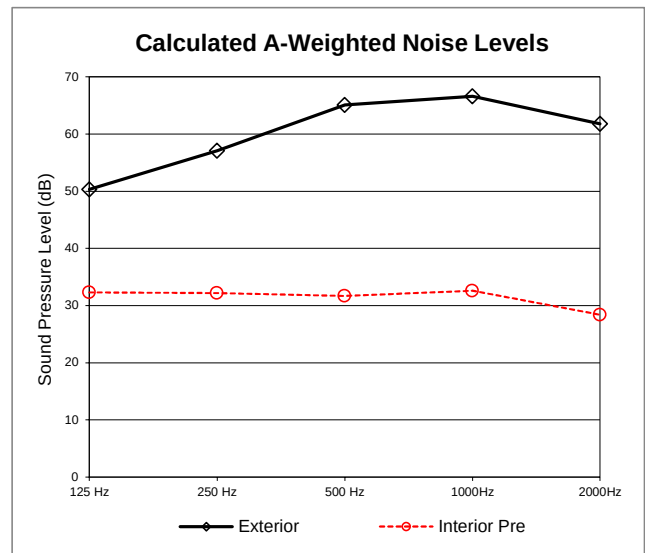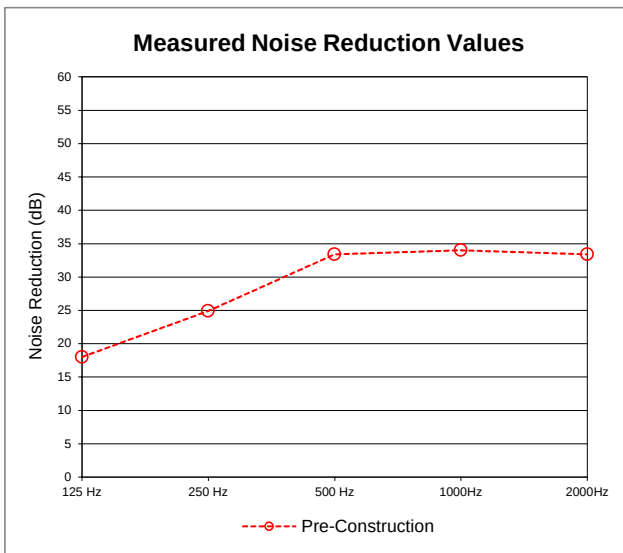



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Rivera & Boyle
 Address: 2035 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.6	53.9	54.1	52.7	43.6	55.9
Exterior Measurement (flush)	90.5	92.8	94.5	89.2	85.6	95.2
Exterior Adjusted	84.5	86.8	88.5	83.2	79.6	89.2
Interior Background	45.2	38.1	30.6	24.0	25.7	34.9
Interior Measurement	66.0	54.0	49.5	43.3	35.9	52.7
Interior Adjusted	66.0	53.9	49.4	43.2	35.5	52.6
Noise Reduction	18.5	32.9	39.1	40.0	44.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.8	24.2	26.0	26.6	17.7	34.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.7 dB

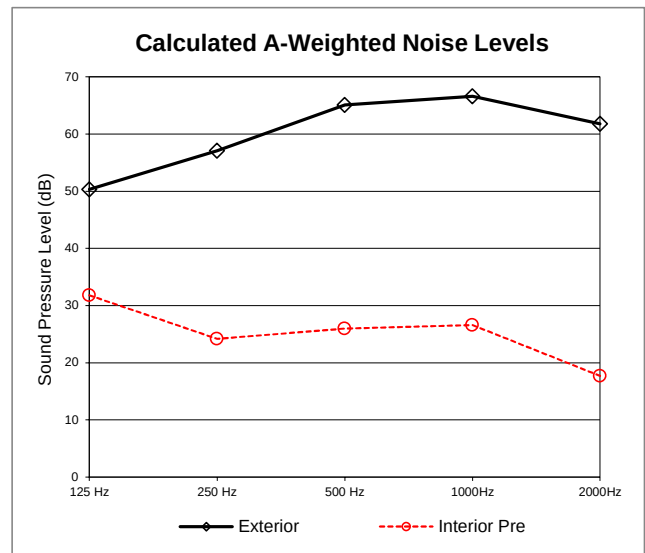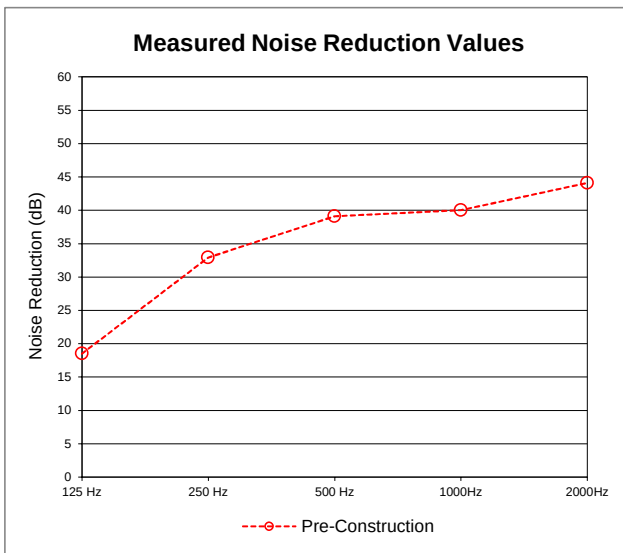



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Rivera & Boyle
 Address: 2035 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.7	46.0	44.6	43.4	44.5	50.9
Exterior Measurement (flush)	89.0	87.4	91.9	86.5	82.3	92.5
Exterior Adjusted	83.0	81.4	85.9	80.5	76.3	86.5
Interior Background	37.2	32.5	29.2	30.4	30.4	35.7
Interior Measurement	65.2	49.4	45.4	39.1	32.2	50.8
Interior Adjusted	65.2	49.3	45.3	38.5	30.9	50.7
Noise Reduction	17.8	32.1	40.6	42.0	45.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.5	25.0	24.5	24.6	16.4	34.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.7 dB

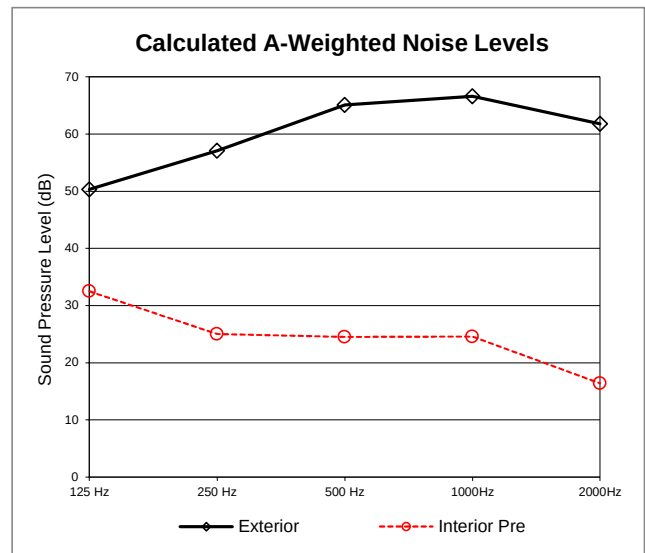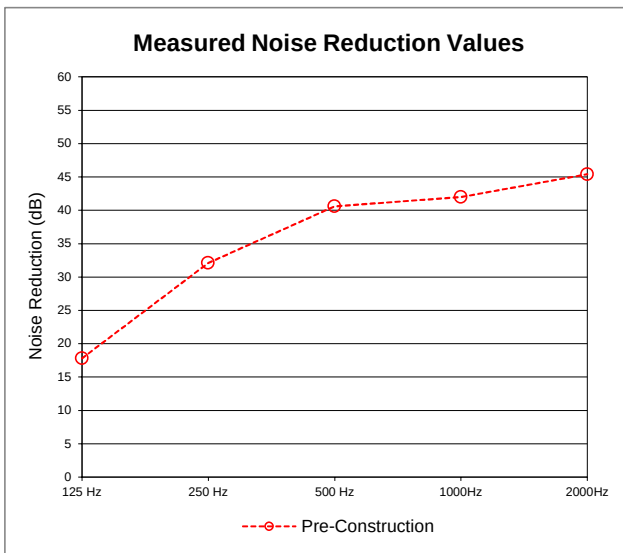

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Rivera & Boyle
 Address: 2035 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	61.7	58.9	55.5	54.6	50.1	58.8
Exterior Measurement (flush)	93.2	91.9	92.5	87.2	84.2	93.4
Exterior Adjusted	87.2	85.9	86.5	81.2	78.2	87.4
Interior Background	47.2	36.7	28.2	26.2	24.5	35.2
Interior Measurement	66.7	58.7	52.6	43.8	41.8	55.2
Interior Adjusted	66.7	58.7	52.6	43.7	41.7	55.2
Noise Reduction	20.5	27.2	33.9	37.5	36.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.8	29.9	31.2	29.1	25.3	36.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.6 dB

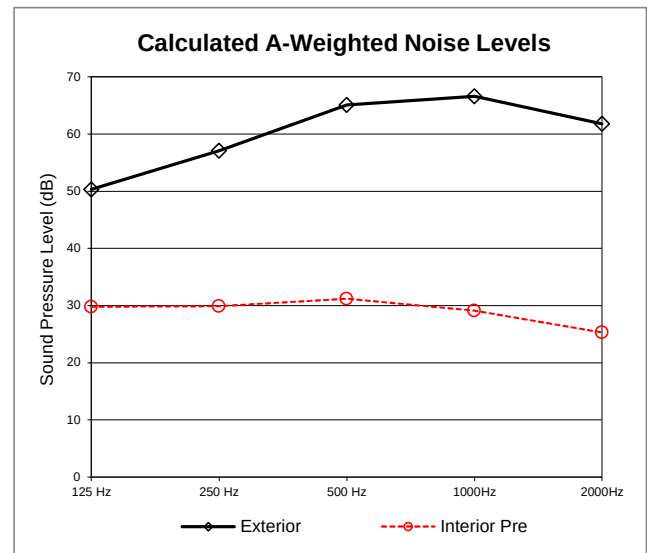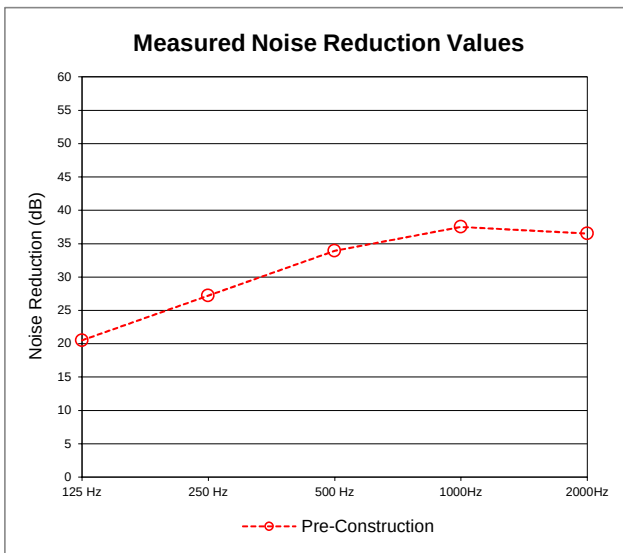



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Rivera & Boyle
 Address: 2035 S 229th St
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	54.7	46.0	44.6	43.4	44.5	50.9
Exterior Measurement (flush)	90.0	89.1	92.7	87.2	82.5	93.2
Exterior Adjusted	84.0	83.1	86.7	81.2	76.5	87.2
Interior Background	33.7	28.0	27.8	29.5	28.9	35.3
Interior Measurement	67.4	53.8	50.2	42.6	34.4	53.4
Interior Adjusted	67.4	53.8	50.2	42.4	33.1	53.3
Noise Reduction	16.6	29.3	36.5	38.8	43.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.7	27.8	28.6	27.8	18.4	36.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.6 dB

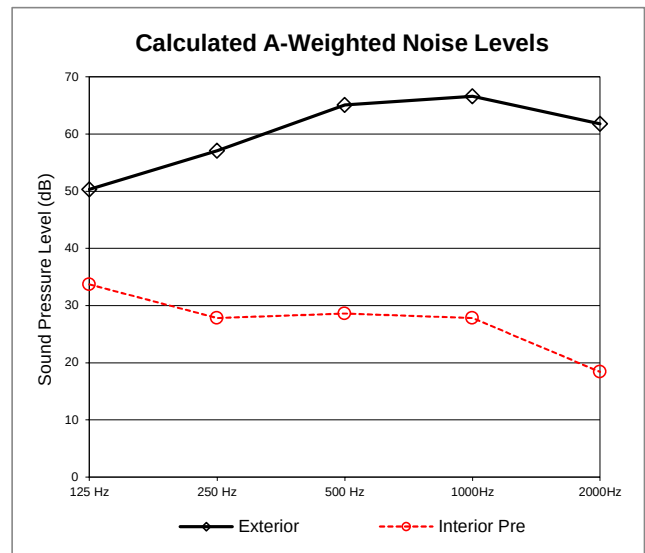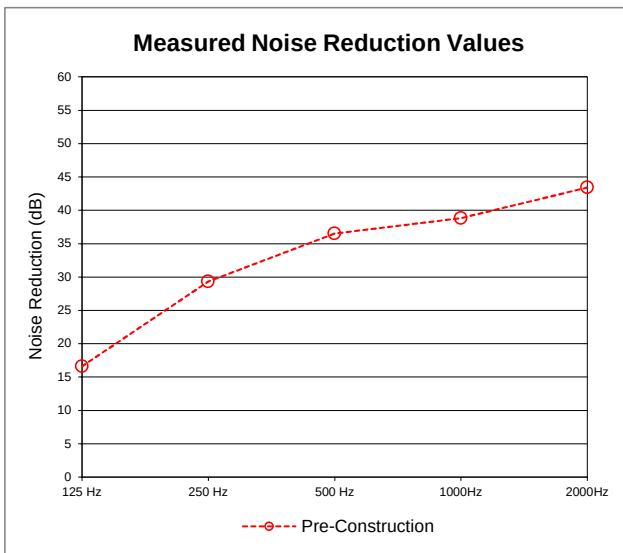

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.5	48.1	50.4	51.0	42.7	53.9
Exterior Measurement (flush)	87.7	89.4	89.1	87.5	83.6	92.9
Exterior Adjusted	81.7	83.4	83.1	81.5	77.6	86.9
Interior Background	38.3	35.4	30.5	25.5	26.0	34.3
Interior Measurement	65.6	59.6	50.9	45.6	41.9	55.1
Interior Adjusted	65.6	59.6	50.9	45.6	41.8	55.1
Noise Reduction	16.1	23.8	32.2	35.9	35.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.2	33.3	32.9	30.7	26.0	39.2
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.8 dB

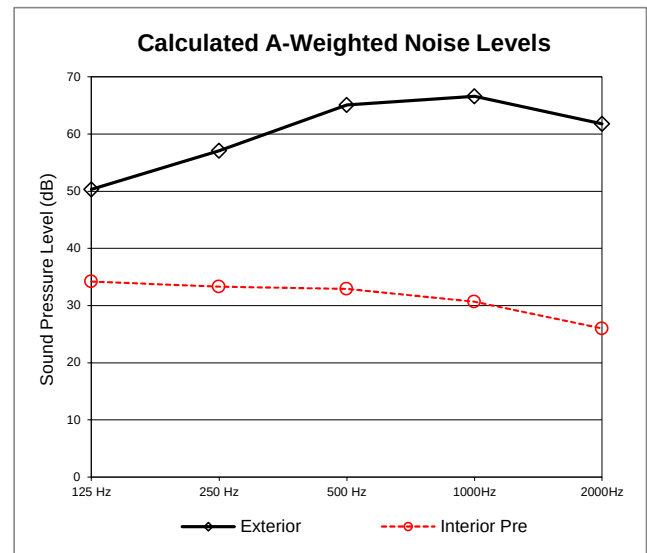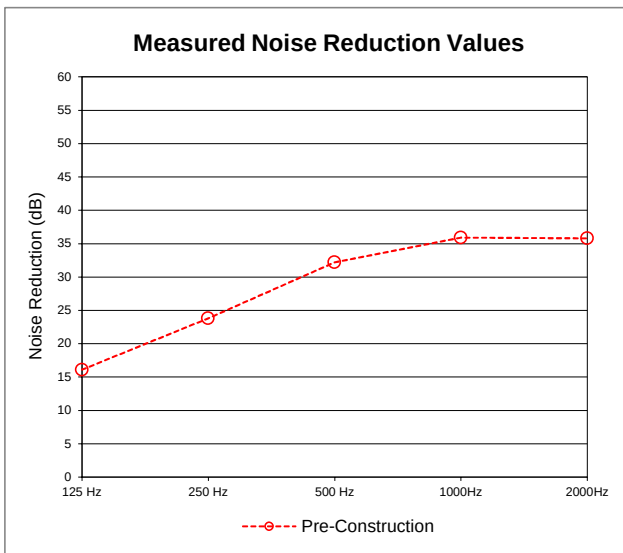

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Dining / Kitchen / Office Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	63.0	56.0	51.9	48.5	44.5	54.5
Exterior Measurement (flush)	90.2	85.1	87.9	84.6	84.2	91.3
Exterior Adjusted	84.2	79.1	81.9	78.6	78.2	85.3
Interior Background	38.1	29.2	20.3	16.2	16.0	27.5
Interior Measurement	65.4	54.4	51.9	46.8	47.3	55.2
Interior Adjusted	65.4	54.4	51.9	46.8	47.3	55.2
Noise Reduction	18.8	24.7	30.0	31.8	30.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.5	32.4	35.1	34.8	30.9	40.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.7 dB

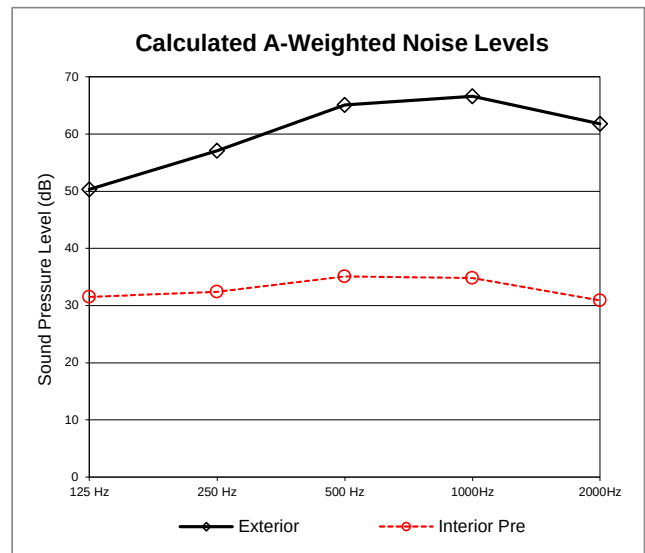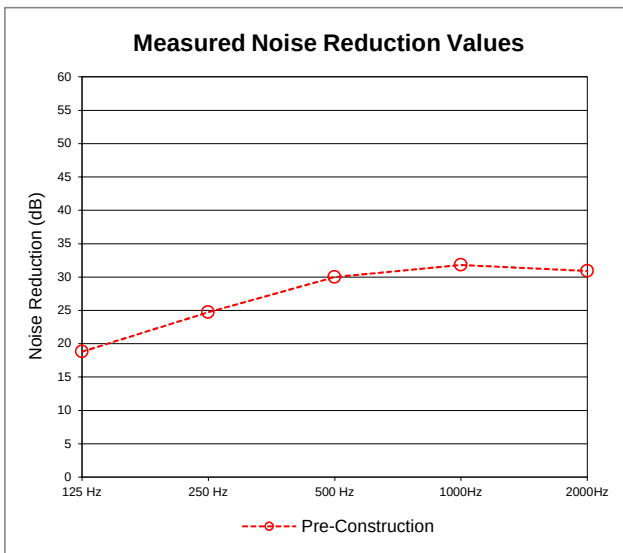

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Dining / Kitchen / Office Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.5	48.1	50.4	51.0	42.7	53.9
Exterior Measurement (flush)	89.6	92.3	91.0	88.1	86.1	95.5
Exterior Adjusted	83.6	86.3	85.0	82.1	80.1	89.5
Interior Background	38.1	29.2	20.3	16.2	16.0	27.5
Interior Measurement	64.1	57.2	50.2	42.9	40.0	53.6
Interior Adjusted	64.1	57.2	50.2	42.9	40.0	53.6
Noise Reduction	19.5	29.1	34.8	39.2	40.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	30.8	28.0	30.3	27.4	21.7	35.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.4 dB

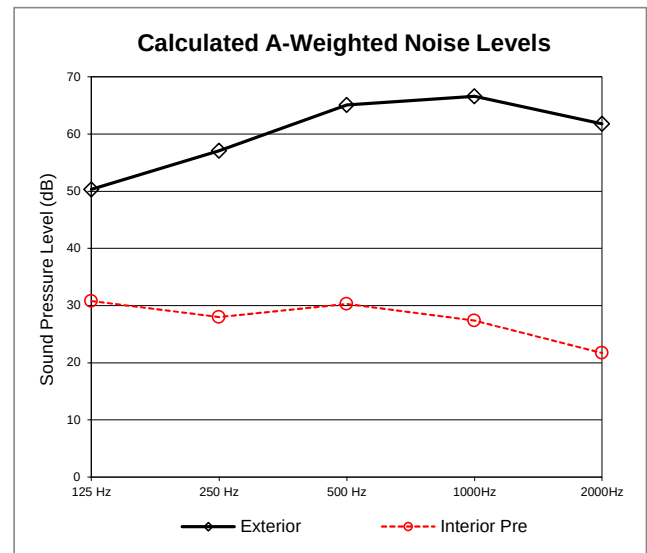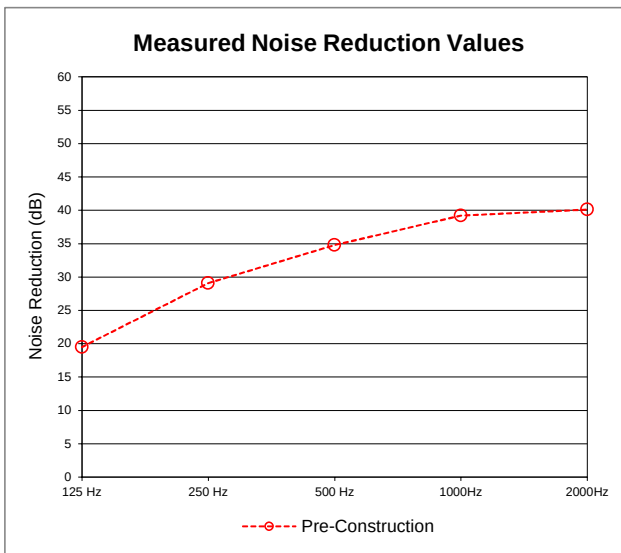

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	53.5	48.1	50.4	51.0	42.7	53.9
Exterior Measurement (flush)	96.5	91.1	91.2	89.0	85.6	95.0
Exterior Adjusted	90.5	85.1	85.2	83.0	79.6	89.0
Interior Background	33.4	26.1	19.4	15.7	17.3	26.3
Interior Measurement	66.8	55.9	50.3	42.3	40.4	53.8
Interior Adjusted	66.8	55.9	50.3	42.3	40.4	53.8
Noise Reduction	23.7	29.2	34.9	40.7	39.2	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.6	27.9	30.2	25.9	22.6	34.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.7 dB

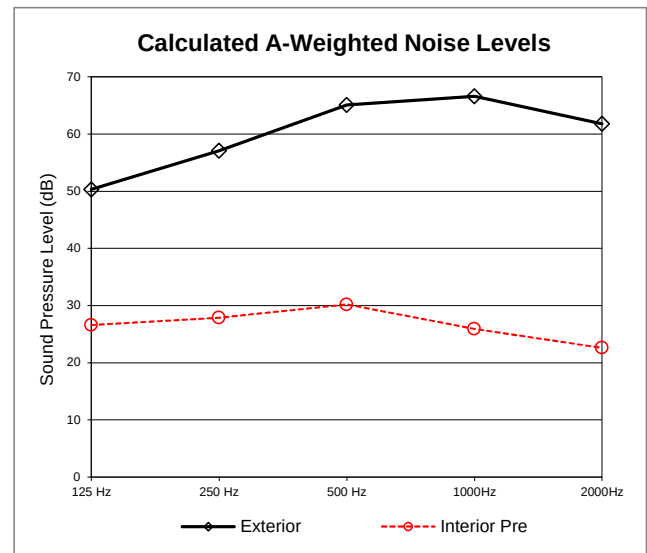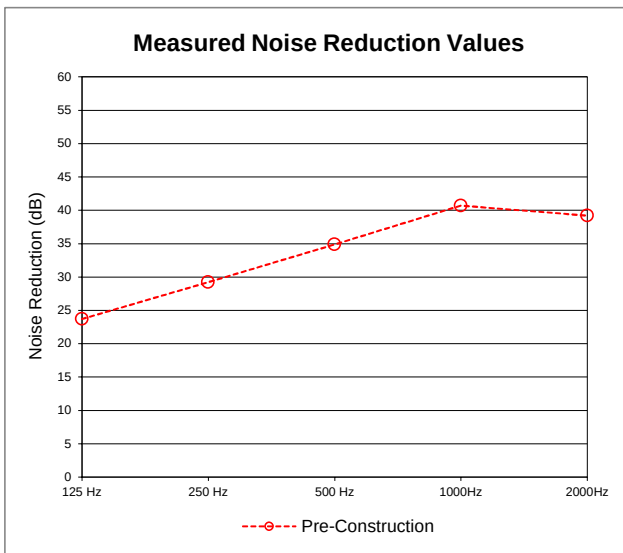



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.7	49.9	48.2	44.4	40.1	50.1
Exterior Measurement (flush)	103.1	102.1	103.1	98.6	94.0	104.9
Exterior Adjusted	97.1	96.1	97.1	92.6	88.0	98.9
Interior Background	32.7	24.5	19.9	16.2	15.8	25.1
Interior Measurement	74.0	62.4	59.2	53.7	47.2	61.6
Interior Adjusted	74.0	62.4	59.2	53.7	47.2	61.6
Noise Reduction	23.1	33.7	37.9	38.9	40.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.2	23.4	27.2	27.7	21.0	33.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						37.0 dB

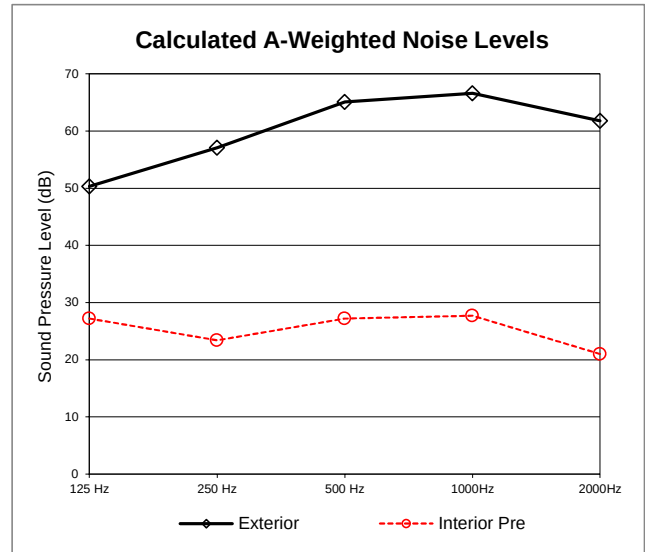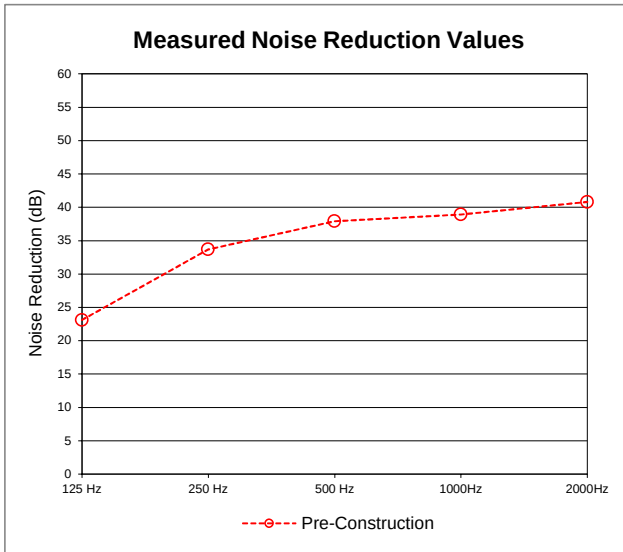



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.7	49.9	48.2	44.4	40.1	50.1
Exterior Measurement (flush)	104.1	102.8	104.2	99.5	92.6	105.0
Exterior Adjusted	98.1	96.8	98.2	93.5	86.6	99.0
Interior Background	32.7	24.5	19.9	16.2	15.8	25.1
Interior Measurement	81.3	70.2	69.0	66.3	61.5	71.8
Interior Adjusted	81.3	70.2	69.0	66.3	61.5	71.8
Noise Reduction	16.8	26.6	29.2	27.2	25.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.5	30.5	35.9	39.4	36.7	43.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						26.9 dB

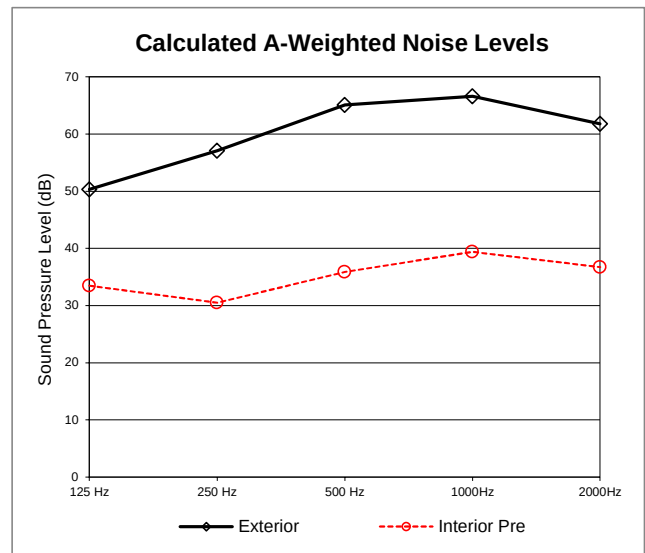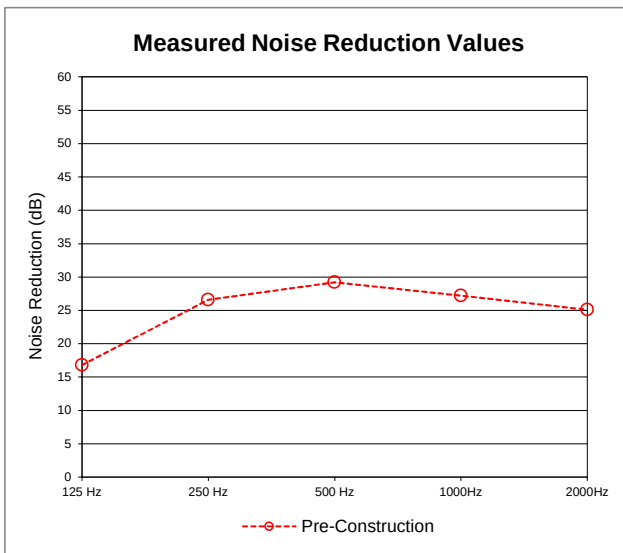



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Alfaro
 Address: 2050 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	59.5	50.1	50.1	52.6	48.0	55.6
Exterior Measurement (flush)	93.4	90.5	91.0	88.5	87.3	94.8
Exterior Adjusted	87.4	84.5	85.0	82.5	81.3	88.8
Interior Background	30.8	28.4	17.2	10.9	11.4	23.6
Interior Measurement	63.6	55.1	47.1	39.2	36.6	51.1
Interior Adjusted	63.6	55.1	47.1	39.2	36.6	51.1
Noise Reduction	23.8	29.4	37.9	43.3	44.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.5	27.7	27.2	23.3	17.1	32.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						37.4 dB

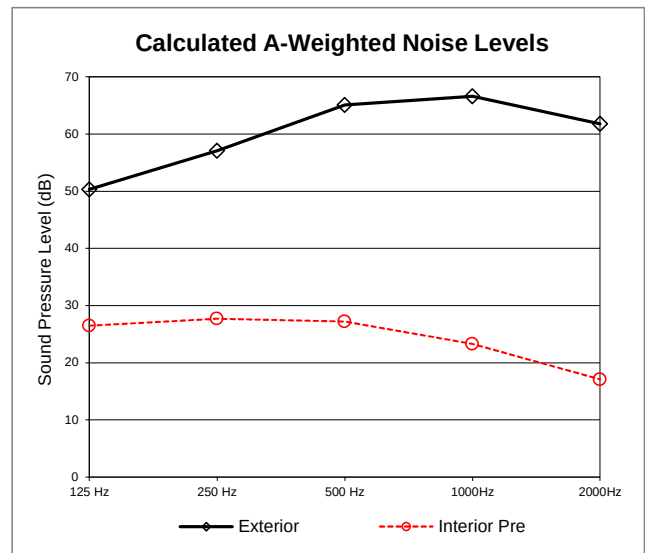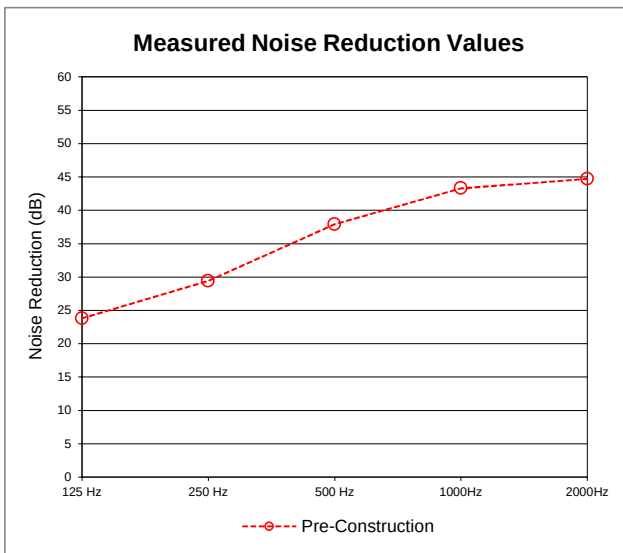

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.8	51.6	50.2	47.0	43.8	52.4
Exterior Measurement (flush)	92.8	93.6	94.1	90.0	88.3	96.5
Exterior Adjusted	86.8	87.6	88.1	84.0	82.3	90.5
Interior Background	44.0	34.9	31.0	26.1	24.0	34.5
Interior Measurement	69.9	61.0	58.5	52.6	48.6	60.2
Interior Adjusted	69.9	61.0	58.5	52.6	48.6	60.2
Noise Reduction	16.9	26.6	29.6	31.4	33.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.4	30.5	35.5	35.2	28.1	40.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.7 dB

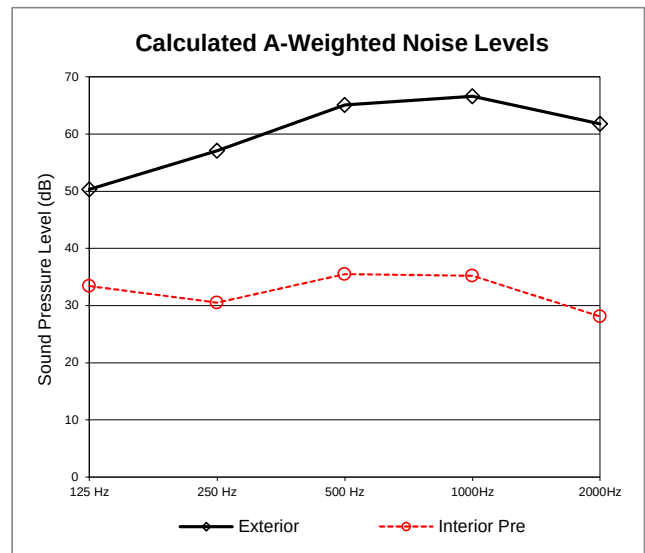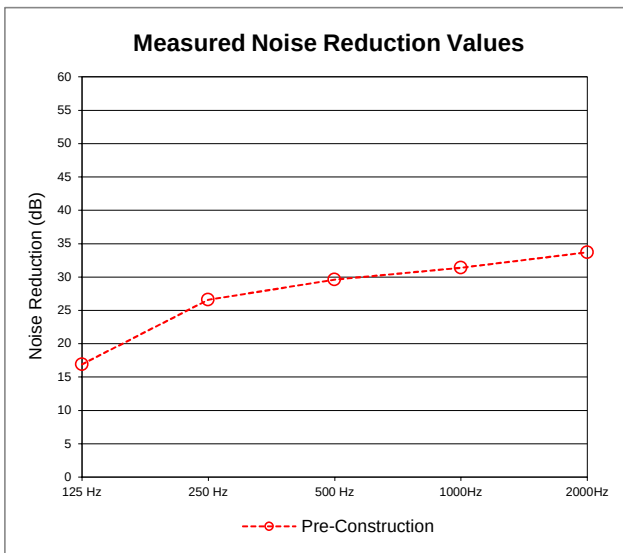

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Sitting Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)

March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	68.1	60.6	57.4	56.1	55.4	62.1
Exterior Measurement (flush)	99.5	99.4	99.9	93.9	89.8	100.9
Exterior Adjusted	93.5	93.4	93.9	87.9	83.8	94.9
Interior Background	44.9	37.5	33.5	29.3	27.5	37.0
Interior Measurement	78.8	65.6	58.5	46.1	37.5	63.9
Interior Adjusted	78.8	65.6	58.5	46.0	37.0	63.9
Noise Reduction	14.7	27.8	35.4	41.9	46.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.6	29.3	29.7	24.7	15.0	37.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.4 dB

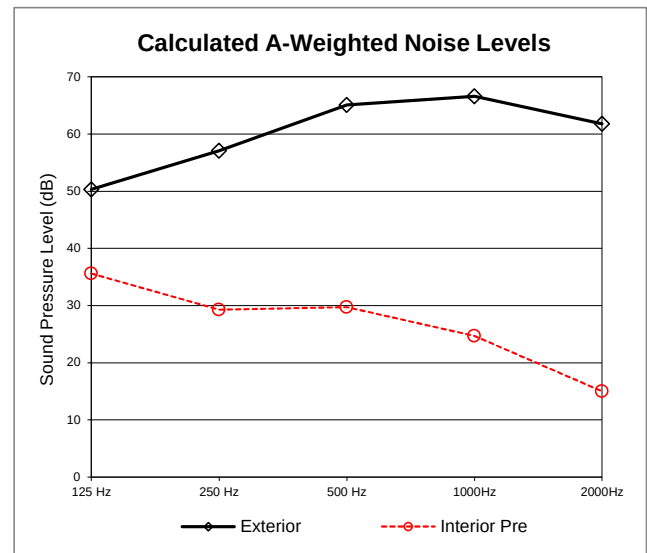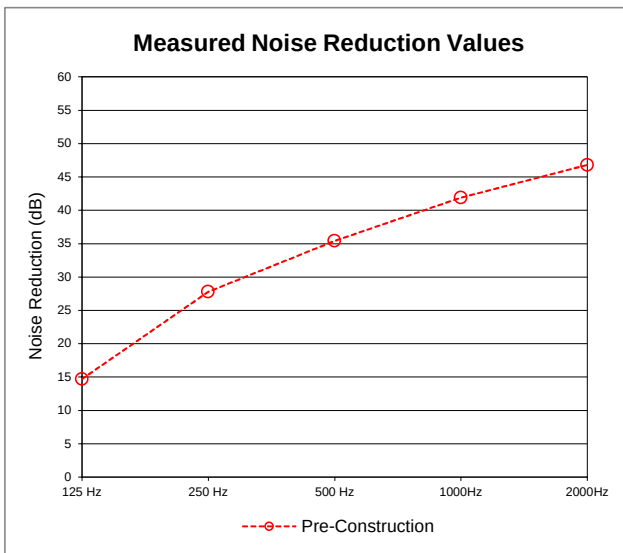



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Sitting Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	68.1	60.6	57.4	56.1	55.4	62.1
Exterior Measurement (flush)	92.3	93.5	95.8	92.0	87.5	97.1
Exterior Adjusted	86.3	87.5	89.8	86.0	81.5	91.1
Interior Background	44.9	37.5	33.5	29.3	27.5	37.0
Interior Measurement	67.0	61.4	59.1	51.7	43.8	59.6
Interior Adjusted	67.0	61.4	59.1	51.7	43.7	59.6
Noise Reduction	19.3	26.1	30.7	34.3	37.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.0	31.0	34.4	32.3	24.0	38.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.4 dB

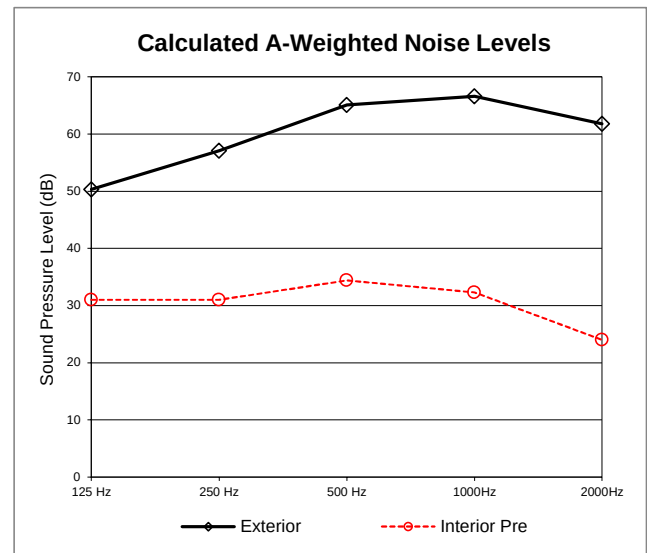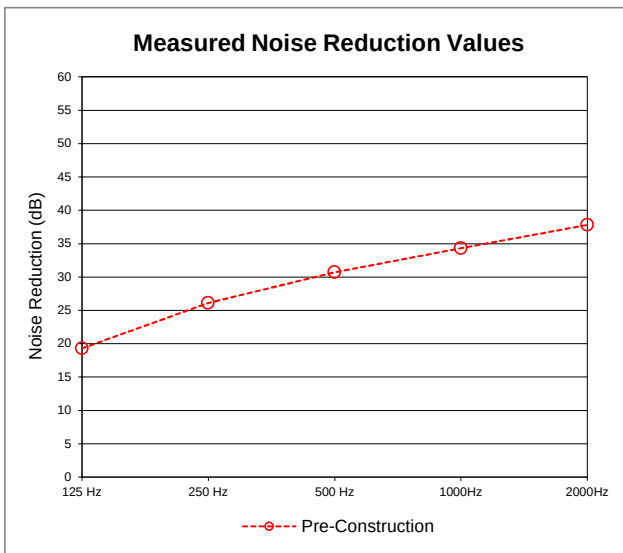



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Dining / Kitchen Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	67.3	63.8	63.8	61.4	58.2	66.4
Exterior Measurement (flush)	87.1	90.1	91.3	87.3	83.3	92.7
Exterior Adjusted	81.1	84.1	85.3	81.3	77.3	86.7
Interior Background	47.9	42.8	36.6	33.7	27.0	39.9
Interior Measurement	65.1	61.0	56.5	47.5	40.9	57.3
Interior Adjusted	65.0	60.9	56.5	47.3	40.7	57.2
Noise Reduction	16.1	23.2	28.8	34.0	36.6	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.2	33.9	36.3	32.6	25.2	40.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						29.4 dB

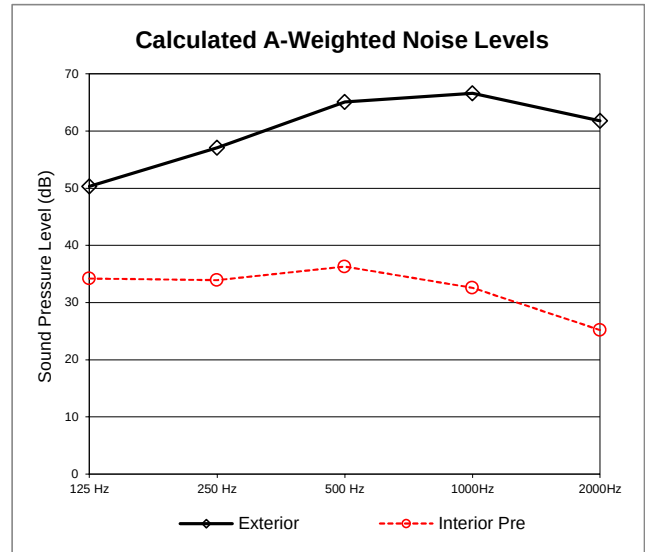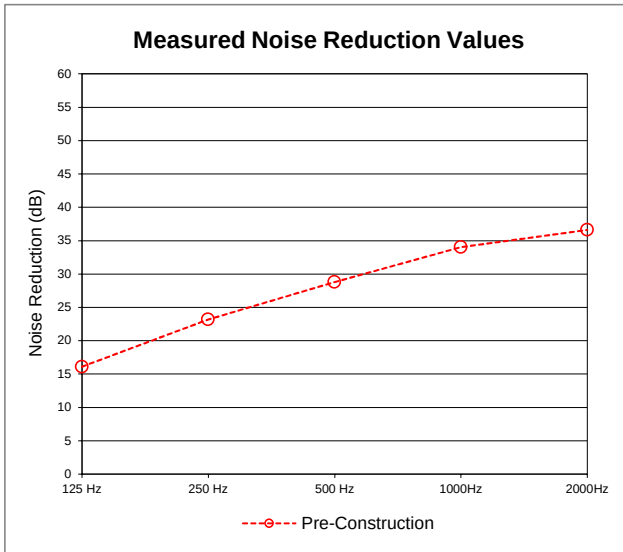



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	69.4	63.1	59.0	58.4	53.2	62.8
Exterior Measurement (flush)	94.1	92.1	93.3	89.2	87.0	95.3
Exterior Adjusted	88.1	86.1	87.3	83.2	81.0	89.3
Interior Background	46.7	37.8	31.8	30.1	26.1	36.7
Interior Measurement	66.2	58.2	52.8	41.5	33.4	54.3
Interior Adjusted	66.2	58.2	52.8	41.2	32.5	54.2
Noise Reduction	21.9	27.9	34.5	42.0	48.5	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	28.4	29.2	30.6	24.6	13.3	34.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						35.3 dB

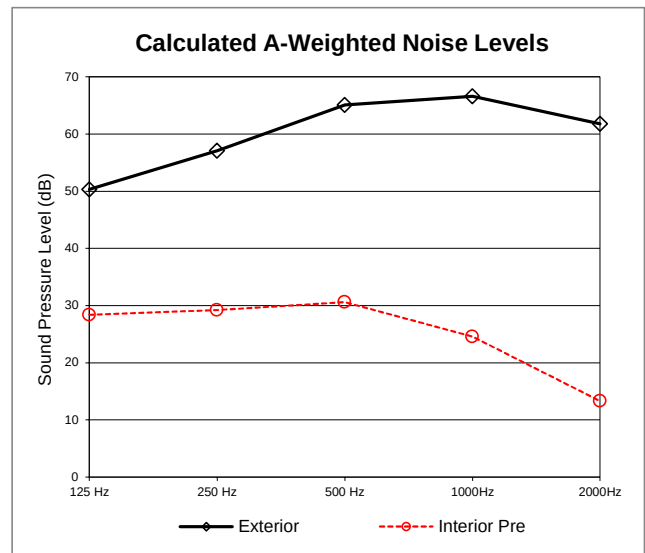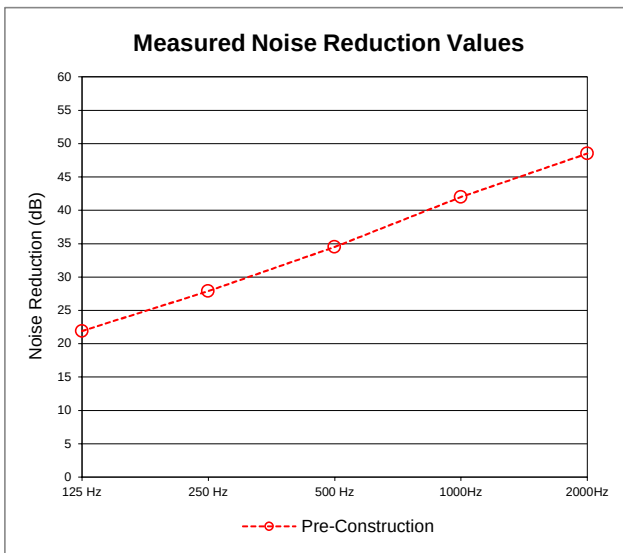



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade 1
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	57.2	59.2	58.4	54.5	62.1
Exterior Measurement (flush)	101.3	101.3	103.2	97.2	90.3	103.0
Exterior Adjusted	95.3	95.3	97.2	91.2	84.3	97.0
Interior Background	40.3	29.4	25.7	25.2	27.1	34.3
Interior Measurement	72.1	65.7	61.0	48.6	42.0	62.0
Interior Adjusted	72.1	65.7	61.0	48.6	41.9	62.0
Noise Reduction	23.2	29.6	36.2	42.6	42.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	27.1	27.5	28.9	24.0	19.4	33.4
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						36.6 dB

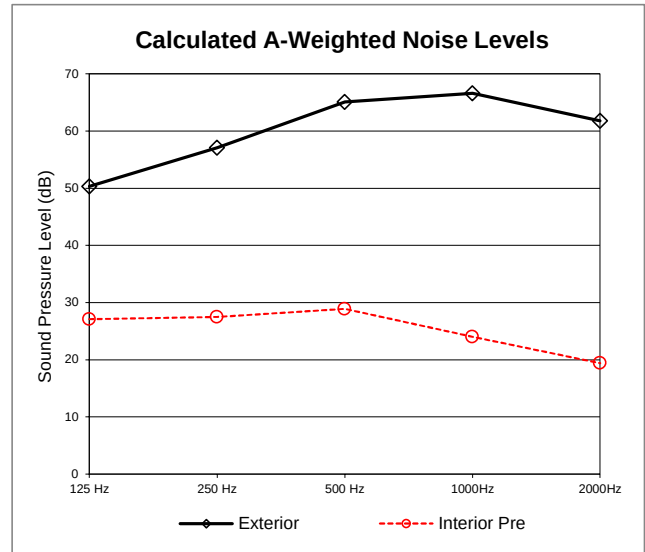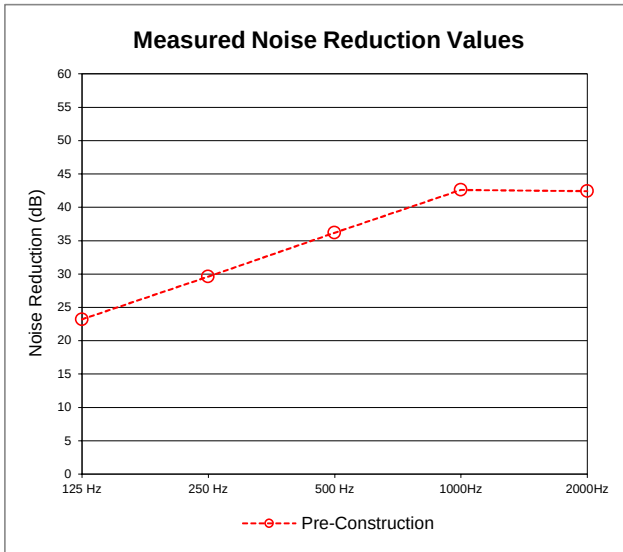



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade 2
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	60.7	57.2	59.2	58.4	54.5	62.1
Exterior Measurement (flush)	108.3	105.5	108.0	100.1	95.7	107.4
Exterior Adjusted	102.3	99.5	102.0	94.1	89.7	101.4
Interior Background	40.3	29.4	25.7	25.2	27.1	34.3
Interior Measurement	76.8	65.5	59.4	46.8	40.1	63.4
Interior Adjusted	76.8	65.5	59.4	46.8	39.9	63.4
Noise Reduction	25.5	34.0	42.6	47.3	49.8	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	24.8	23.1	22.5	19.3	12.0	28.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						41.1 dB

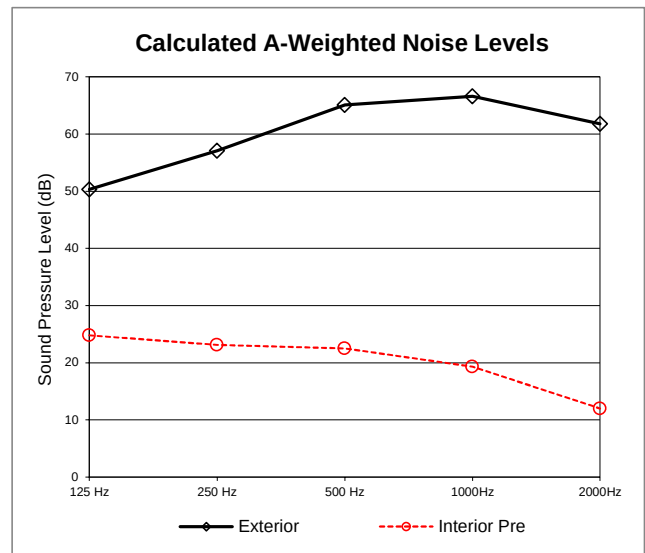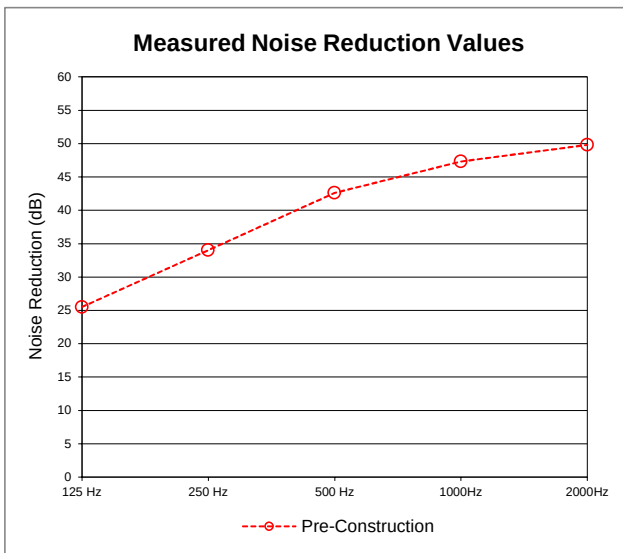



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Canas
 Address: 2106 S 229th St
 Local City: Des Moines

Tested Room: Office Façade
 Exposed Surface: Façade
 Floor / Stories: 2 of 2

Pre-Construction Sound Pressure Levels (dB)						
March 24, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	68.1	60.6	57.4	56.1	55.4	62.1
Exterior Measurement (flush)	94.1	92.1	93.3	89.2	87.0	95.3
Exterior Adjusted	88.1	86.1	87.3	83.2	81.0	89.3
Interior Background	45.8	39.6	34.3	26.7	20.8	36.1
Interior Measurement	70.3	60.2	56.7	49.5	43.3	58.4
Interior Adjusted	70.3	60.2	56.7	49.5	43.3	58.4
Noise Reduction	17.8	25.9	30.6	33.7	37.7	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.5	31.2	34.5	32.9	24.1	39.1
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.9 dB

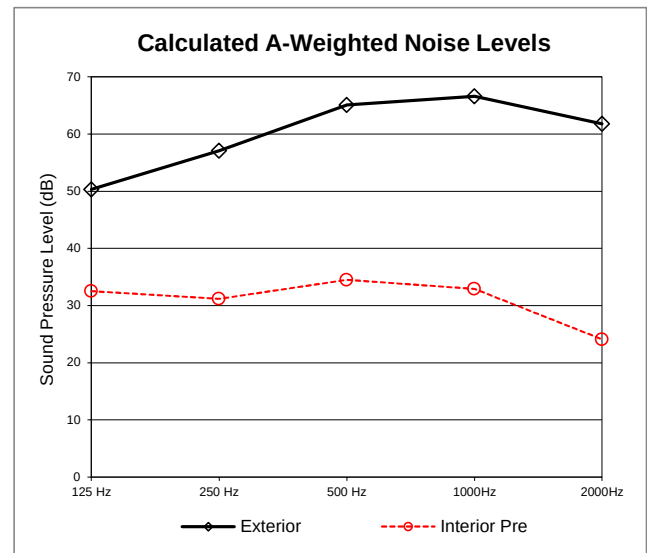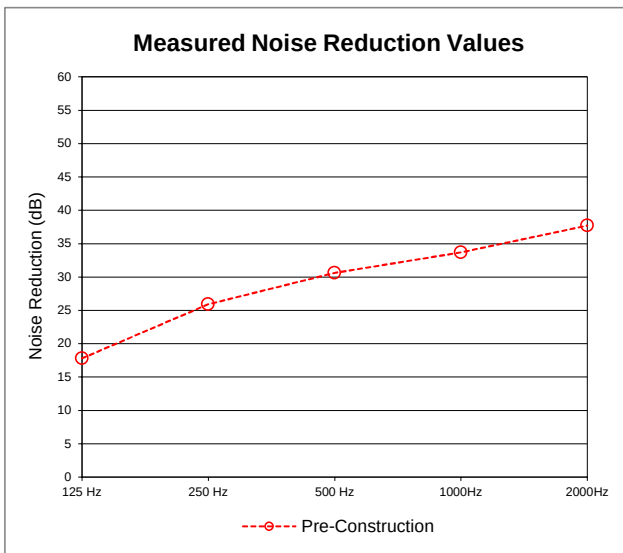

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Living Room Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.2	54.5	53.8	49.8	40.4	54.3
Exterior Measurement (flush)	81.5	85.3	84.8	83.0	82.1	89.1
Exterior Adjusted	75.5	79.3	78.8	77.0	76.1	83.1
Interior Background	41.4	34.8	30.6	26.6	24.6	33.7
Interior Measurement	60.4	52.8	46.0	39.5	42.1	50.9
Interior Adjusted	60.3	52.7	45.9	39.3	42.0	50.8
Noise Reduction	15.2	26.6	32.9	37.7	34.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	35.1	30.5	32.2	28.9	27.7	38.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						31.3 dB

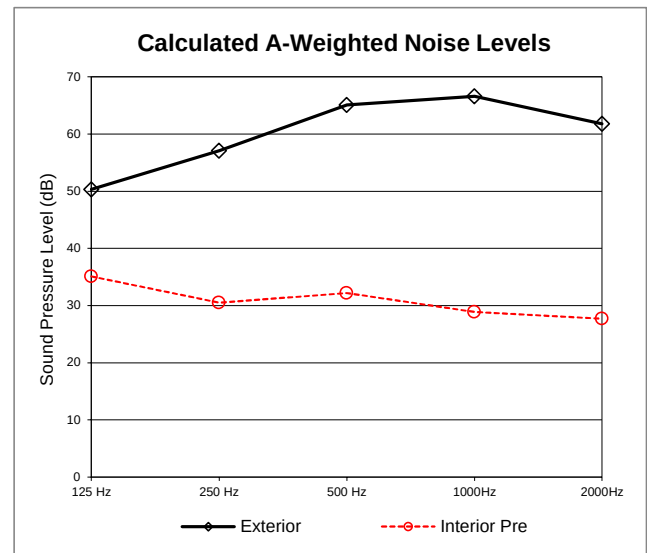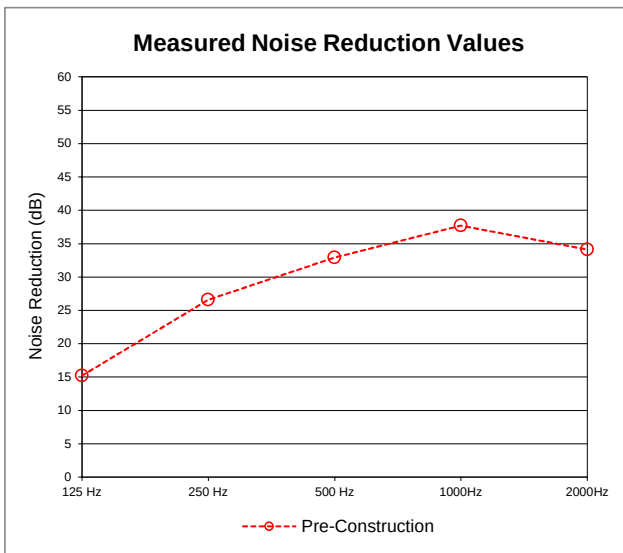

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Sitting Room Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.2	54.5	53.8	49.8	40.4	54.3
Exterior Measurement (flush)	98.1	98.5	99.3	95.5	93.1	101.9
Exterior Adjusted	92.1	92.5	93.3	89.5	87.1	95.9
Interior Background	34.7	27.9	24.2	20.4	16.1	27.5
Interior Measurement	72.8	60.0	58.9	52.8	40.1	60.5
Interior Adjusted	72.8	60.0	58.9	52.8	40.1	60.5
Noise Reduction	19.3	32.5	34.4	36.7	47.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.0	24.6	30.7	29.9	14.8	35.7
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.3 dB

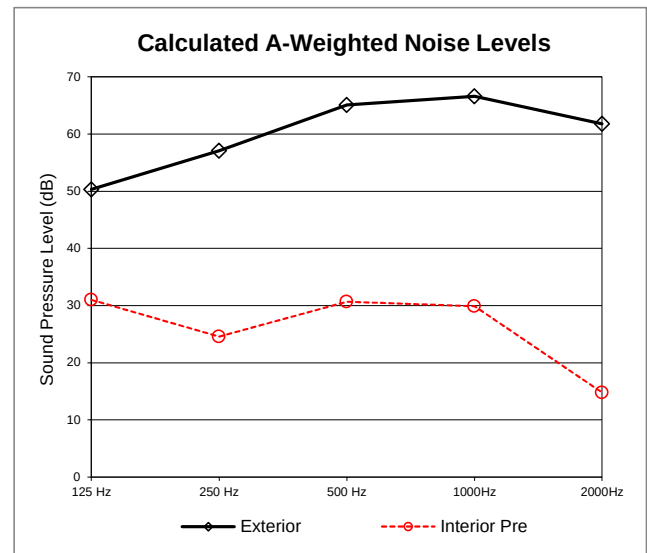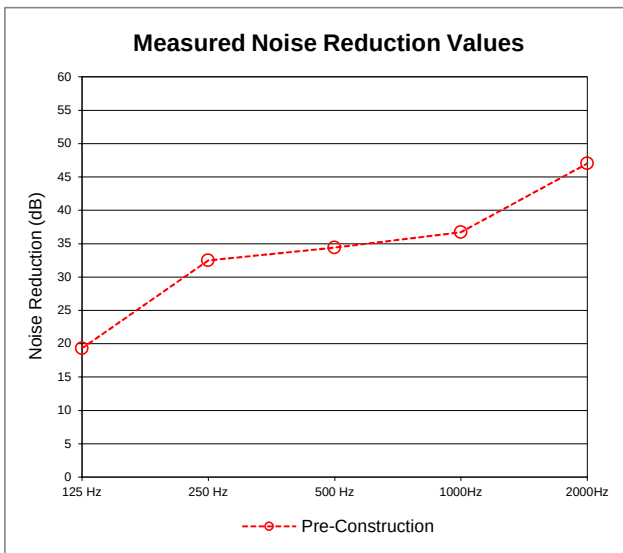



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Dining Room Façade 1
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.2	54.5	53.8	49.8	40.4	54.3
Exterior Measurement (flush)	112.4	110.6	111.9	107.1	102.8	113.0
Exterior Adjusted	106.4	104.6	105.9	101.1	96.8	107.0
Interior Background	41.2	36.3	30.8	25.4	17.8	32.7
Interior Measurement	90.1	73.9	66.2	53.7	47.7	73.8
Interior Adjusted	90.1	73.9	66.2	53.7	47.7	73.8
Noise Reduction	16.3	30.7	39.7	47.4	49.1	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	34.0	26.4	25.4	19.2	12.7	35.3
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						34.7 dB

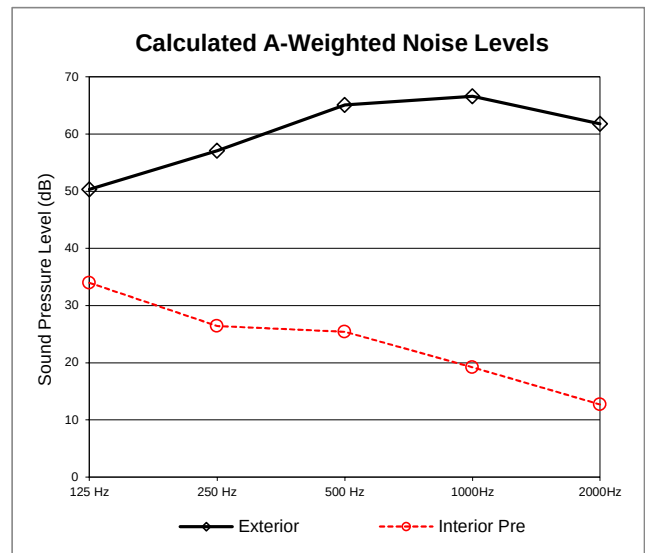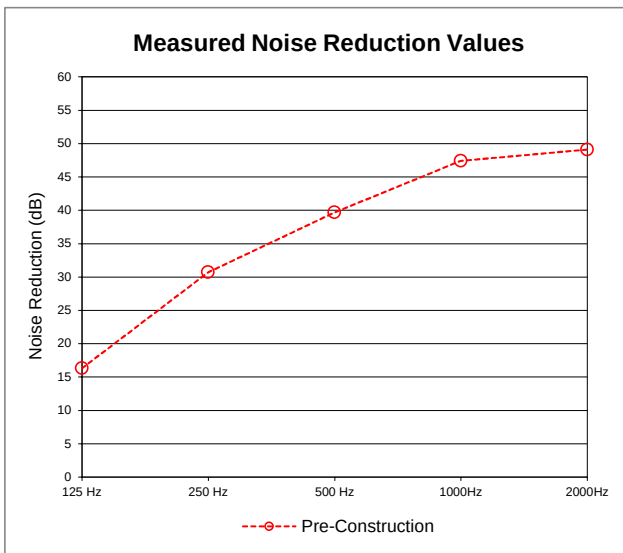

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Dining Room Façade 2
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	55.2	54.5	53.8	49.8	40.4	54.3
Exterior Measurement (flush)	96.1	95.8	97.0	93.8	91.0	100.2
Exterior Adjusted	90.1	89.8	91.0	87.8	85.0	94.2
Interior Background	41.2	36.3	30.8	25.4	17.8	32.7
Interior Measurement	72.1	72.0	66.9	61.5	60.6	69.1
Interior Adjusted	72.1	72.0	66.9	61.5	60.6	69.1
Noise Reduction	18.0	17.8	24.1	26.3	24.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	32.3	39.3	41.0	40.3	37.4	45.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						24.1 dB

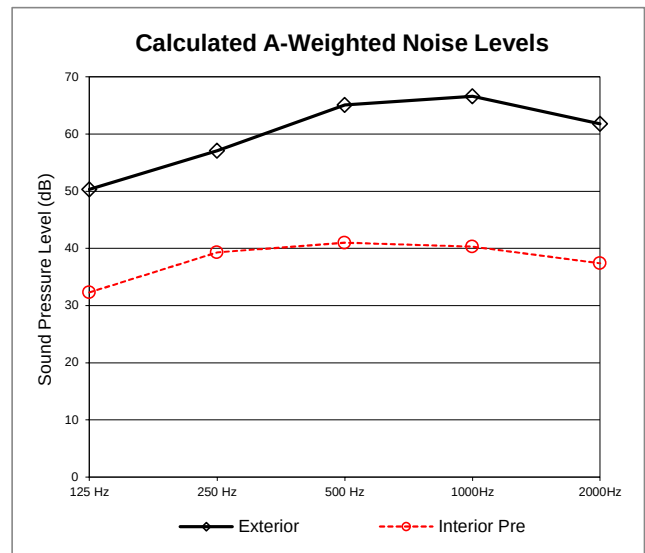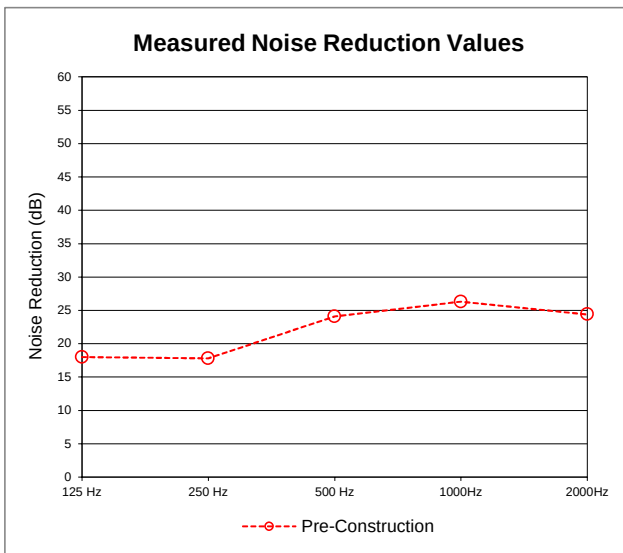



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Kitchen Façade
 Exposed Surface: Façade
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.3	54.6	53.0	50.9	41.2	54.5
Exterior Measurement (flush)	99.1	99.1	100.6	98.2	94.9	103.6
Exterior Adjusted	93.1	93.1	94.6	92.2	88.9	97.6
Interior Background	37.5	37.5	32.2	27.4	20.5	33.8
Interior Measurement	76.7	72.2	69.4	64.7	64.9	74.2
Interior Adjusted	76.7	72.2	69.4	64.7	64.9	74.2
Noise Reduction	16.4	20.9	25.2	27.5	24.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	33.9	36.2	39.9	39.1	37.8	44.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						25.1 dB

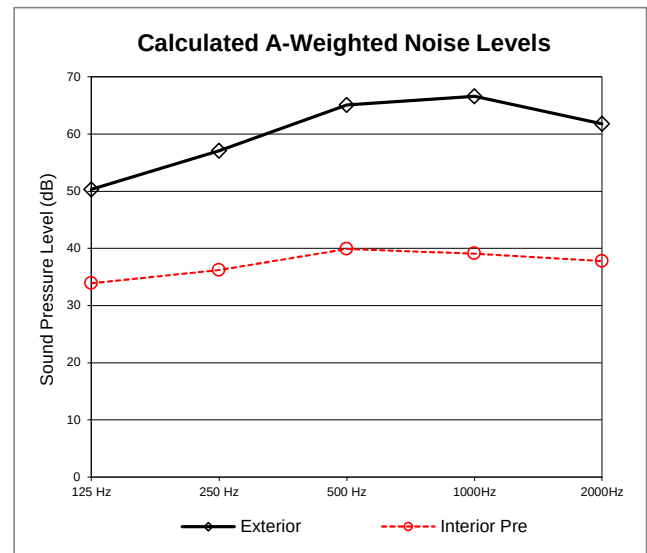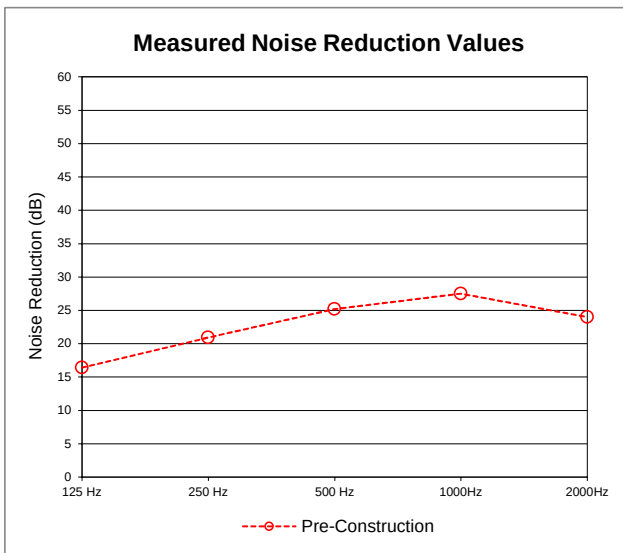



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Bedroom 1 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.3	54.6	53.0	50.9	41.2	54.5
Exterior Measurement (flush)	90.5	88.3	91.3	88.6	84.8	94.7
Exterior Adjusted	84.5	82.3	85.3	82.6	78.8	88.7
Interior Background	36.1	32.1	27.3	23.9	19.3	30.3
Interior Measurement	63.4	57.7	57.1	53.3	51.5	59.4
Interior Adjusted	63.4	57.7	57.1	53.3	51.5	59.4
Noise Reduction	21.1	24.6	28.2	29.3	27.3	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.2	32.5	36.9	37.3	34.5	42.0
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						28.0 dB

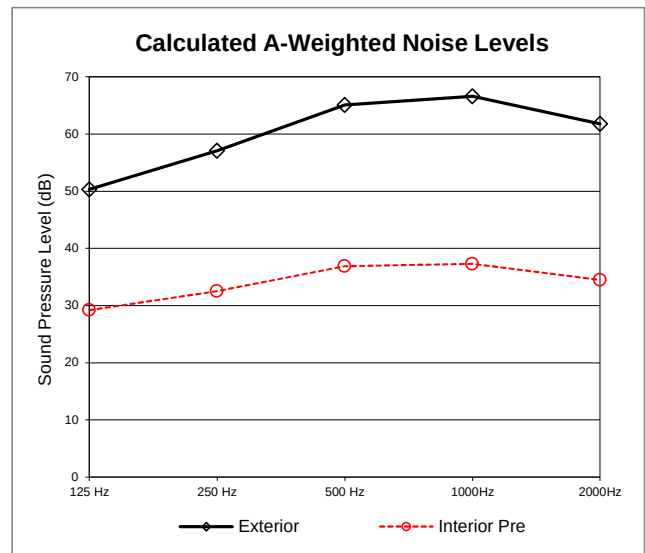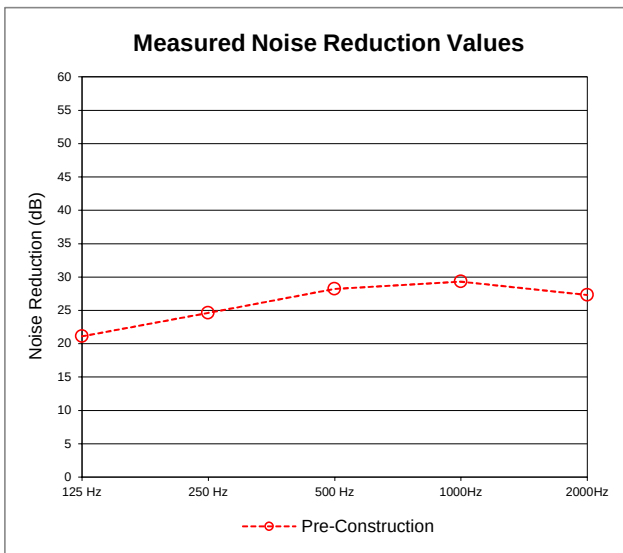

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program



Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Bedroom 2 Façade
 Exposed Surface: Façade & Roof
 Floor / Stories: 1 of 1

Pre-Construction Sound Pressure Levels (dB)

March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.3	54.6	53.0	50.9	41.2	54.5
Exterior Measurement (flush)	91.4	90.8	91.8	89.9	85.8	95.1
Exterior Adjusted	85.4	84.8	85.8	83.9	79.8	89.1
Interior Background	38.2	28.9	19.8	18.6	22.3	30.5
Interior Measurement	64.1	59.0	50.6	44.5	47.9	55.6
Interior Adjusted	64.1	59.0	50.6	44.5	47.9	55.6
Noise Reduction	21.3	25.8	35.2	39.4	31.9	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	29.0	31.3	29.9	27.2	29.9	36.6
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						33.4 dB

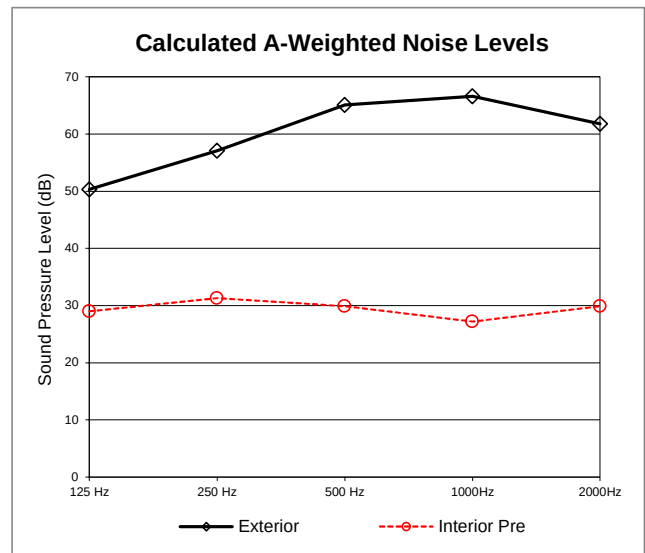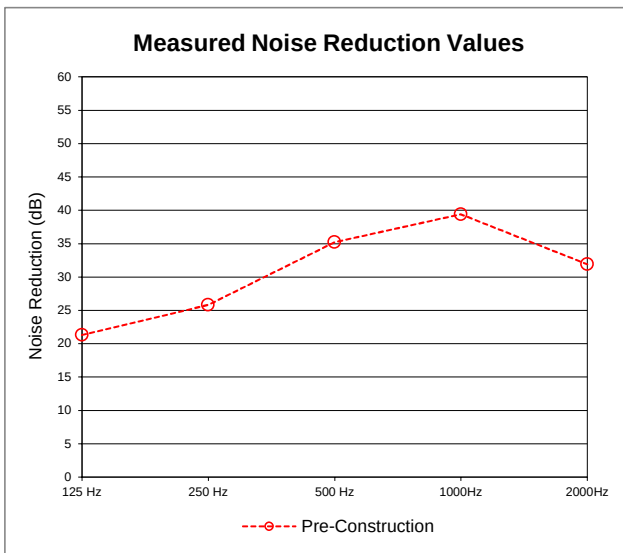



Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Bedroom 3 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.3	54.6	53.0	50.9	41.2	54.5
Exterior Measurement (flush)	90.1	88.3	88.9	88.1	86.4	94.9
Exterior Adjusted	84.1	82.3	82.9	82.1	80.4	88.9
Interior Background	33.2	25.5	17.4	13.3	12.9	24.4
Interior Measurement	59.9	58.5	54.9	46.1	39.4	55.2
Interior Adjusted	59.9	58.5	54.9	46.1	39.4	55.2
Noise Reduction	24.2	23.8	28.0	36.0	41.0	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	26.1	33.3	37.1	30.6	20.8	39.5
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						30.5 dB

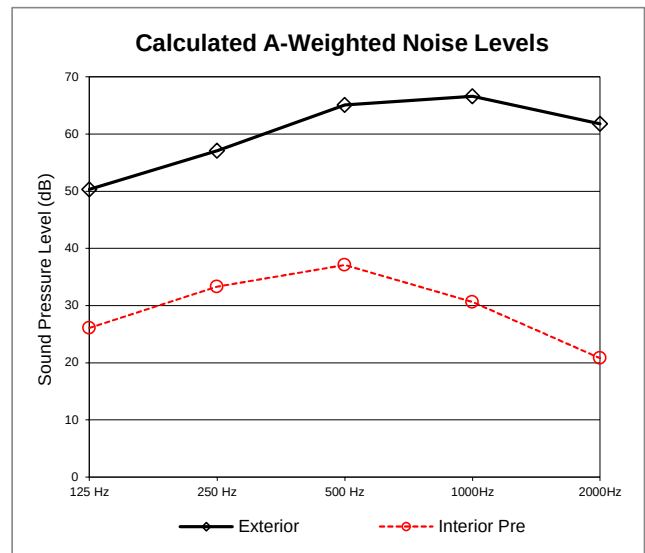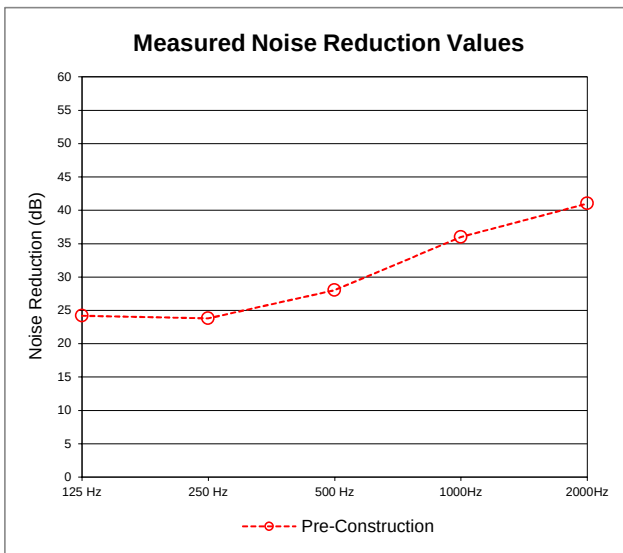

Airport: Seattle-Tacoma International Airport
 Project: Repair and Replacement Program

Job Number: 03-12150.001.004
 City and State: Seattle WA

Resident: Gavlinski
 Address: 1803 S 233rd St
 Local City: Des Moines

Tested Room: Bedroom 4 Façade
 Exposed Surface: Façade
 Floor / Stories: 0 of 1

Pre-Construction Sound Pressure Levels (dB)						
March 27, 2026	125 Hz	250 Hz	500 Hz	1000 Hz	2000 Hz	A-Weighted Overall Level
Exterior Background	56.3	54.6	53.0	50.9	41.2	54.5
Exterior Measurement (flush)	90.1	87.6	89.4	87.0	87.0	94.7
Exterior Adjusted	84.1	81.6	83.4	81.0	81.0	88.7
Interior Background	39.2	34.0	22.1	14.5	13.5	28.5
Interior Measurement	65.5	58.5	49.8	42.5	40.6	54.1
Interior Adjusted	65.5	58.5	49.8	42.5	40.6	54.1
Noise Reduction	18.6	23.1	33.6	38.5	40.4	-
Exterior Noise Level	50.3	57.1	65.1	66.6	61.8	70.0
Interior Noise Level	31.7	34.0	31.5	28.1	21.4	37.9
Noise Level Reduction (based on A-weighted Boeing 737-800 noise spectrum):						32.1 dB

